



FINANCE
Budget and Planning

Capital Planning Section
175 E 2nd, Tulsa, Oklahoma 74103-3203

To: STOC

Jake Epp
From: Capital Planning Manager

Date: April 22, 2025

Subject: April Meeting

Enclosed is the material for your April 22, 2025 meeting including the March 31, 2025 Financial Report for your review. 2016 and 2020 Sales Tax Program revenues for April 2025 and the fiscal year to date compared to 2016 and 2020 Sales Tax Program Adopted Budget Estimates are:

	Actual	Current Adopted Budget	Variance from Adopted Budget
Month of April	\$9,188,772	\$9,614,684	-4.4%
Year To Date	\$90,312,964	\$90,550,466	-0.3%

Please note the above amounts are the Sales Tax revenue only.

The 2016 and 2020 Sales Tax Programs Funds (4000 and 409), in addition to sales tax revenue, receives interest, and other revenues such as grants, transfers and miscellaneous revenues. Total revenue reported for the funds is not available until the end of the month so, the information provided below is for the most recently completed month. Total Fund 4000 and 409 revenue for the month of March was:

	Month Ending: <u>March 31, 2025</u>	Variance from <u>Adopted Budget</u>	Year Thru: <u>March 31, 2025</u>	Variance from <u>Adopted Budget</u>
Sales Tax Revenue	\$9,188,772	-4.4%	\$90,312,964	-0.3%
Interest on Investments	\$1,114,844	N/A	\$7,568,094	N/A
Other Revenue	<u>\$0</u>	N/A	<u>\$0</u>	N/A
Total Fund Revenue	\$10,303,616	-4.0%	\$97,881,058	-0.2%

04/15/2025 02:21 PM

**Office of the
City Clerk**

**SALES TAX OVERVIEW COMMITTEE
AMENDED AGENDA**

April 22, 2025, 8:00 AM

175 E 2ND ST, 3-317

The STOC will meet in person at 8:00 am on April 22, 2025.

- I. Call to Order
- II. Reading of the February Minutes
- III. Chair Report to Council
- IV. Subcommittee Reports
 - A. Vison
 - B. Public Safety
 - C. Parks
 - D. Transportation
 - E. Financial
- V. Nomination of Officers
- VI. Unfinished Business
- VII. New Business
- VIII. Adjournment

STOC

Sales Tax Overview Committee

MINUTES Sales Tax Overview Committee Meeting March 25, 8:00 a.m. 175 E 2nd St, Tulsa OK

The Sales Tax Overview Committee met for the regular monthly meeting at 8:00 a.m. on February 25, 2024.

I. Call to Order

Ashley Webb called the meeting to order at 8:01 a.m.

The following members were present:

Charles Wilkes	Linda Jenkins	Scott Asbjornson	Sylvia Powell
Brett Freisen	Tige Rodgers	Ashley Webb	Kathy Sebert
Maia Treleaven	Uriah Davis	Matt Meyer	James Deming
Deborah McKinney	Steve King	Scott Grizzle	Paul Hassink
Pamela Amburgy	Mareo Johnson	Jessica Reyes	

The following members were not present:

Jennifer White

Also present:

Nathan Pickard	Brian Whisenhunt	Andrew Witte	Mary Womble
Jake Epp	Chris Havenar	Karen Gillis	

II. Approval of Minutes

Ashley Webb made a motion to approve the February minutes. Kathy Sebert asked if small corrections like a slight misspelling needed to be corrected. Mareo Johnson made a motion to approve the minutes. Pamela Amburgy seconded, and the motion carried.

III. Chair's Report

Kathy Sebert spoke to the Council that the Zink Dam was on budget. The Turkey Mountain Urban Wilderness Trails added six additional miles of trails but that they will not be open to the public till all the planned trails are constructed. Kathy Sebert also mentioned that she spoke to the Council on the Tulsa Zoo Carnivores Exhibit and how it just kicked off. She also spoke on Fred Johnson Park and the improvements on that. The flaking on the bridge at 21st and Mingo Road that had to have the fittings re-done on

STOC

Sales Tax Overview Committee

both sides due to rusting. The Animal Services Shelter that had opening bids on February 4th. Bids for the Animal Shelter were reasonable, and results are pending.

IV. Speaker City Auditor Nathan Pickard

Nathan Pickard said that he is trying to go around to all the boards and committees and let them know that they have an elected city auditor for the last twelve years. Nathan Pickard is trying to educate the public about the role and how it can be useful for the City of Tulsa to have an independent voice evaluating things. The core commitment of the City Auditor's office is to provide accountability and community trust by listening to community residence and employees, performing audits and using consulting and reporting. The City Auditor is responsible for reporting to the Mayor and Counselors on anything they find. The Counsel can also create an ordinance or a resolution to direct the City Auditor to do things. The City Auditor has the authority to investigate the Mayor and Counselors for any ethics violation. Paul Hassink asked if the City Auditor can do fraud related investigations. Nathan Pickard replied that the City Auditor was more on the process side. The City Auditor administers the Ethics Hotline so you can do it anonymously if you witness a city employee doing something that needs to be reported. All the past audits are located on the City of Tulsa's webpage.

Maia Treleven asked how Nathan Pickard comes up with an annual audit. She wanted to know if the City Auditor was using an agile program and what credentials the auditors have. Nathan Pickard replied that the City Auditor's office follows the Institute of Internal Auditors' standards. One of the requirements of being an elected City Auditor is to be an auditor or a CPA. Maia Treleven wanted to know what the risk assessment was based on. Nathan Pickard stated that he is currently gathering risk assessment with impact. The current audit plan will be shared publicly, in past years it has not.

V. Committee Reports

A. Vision

Andrew Witte with Flintco. gave handouts of all the progress on the new Gilcrease Museum building. Flintco's team is working on a punch list of items. The spiral staircase is still waiting on the granite from Spain. The shipping should start in the next few weeks. Pamela Amburgy asked if the picture of the staircase was from the bottom up.

Ashley Webb asked if the shipment would include panels for the backside, was the paneling for the backside completed. Andrew Witte replied that the exterior of the building was completed except for the part that wraps around the skylight on the roof. Flintco has had several inspections with the City of Tulsa. Flintco is working closely with Gallagher and Associates to improve the execution and exhibit design. They are over the contract on the exhibit and the fabrication. Forecast is that onsite work will begin soon at the beginning of next year.

Linda Jenkins asked about the photo labeled the green room. She stated that the only green room that she knew of was based on a room where you wait before you go on a television show. Brian Whisenhunt, the Director of Gilcrease Museum mentioned that there was an open amphitheater on the North side of the building that the green room will be utilized for.

Linda Jenkins also asked about the parking lot that can be seen in the photographs. Andrew Witte mentioned that the parking lot closest to Stewart Park was rebuilt by the Osage Nation.

STOC

Sales Tax Overview Committee

Ashley Webb commended Andrew Witte, Mary Womble and everyone in the City who has been involved in the process. Linda Jenkins asked if STOC would get another opportunity to tour the building. Ashley Webb said that perhaps Andrew Witte needed all the building materials to finish the spiral staircase. Deborah McKinney asked if the City of Tulsa was waiting till the staircase was complete till the building was inhabitable. Andrew Witte replied that the building was habitable but once construction starts on the staircase it would not be habitable.

Brian Whisenhunt reported that Stephen Towns, a painter and quilt maker, who is based in Baltimore Maryland arrived in Tulsa last yesterday. He is Gilcrease Museum's anagogical artist in residence for our Revive Program. He is here in Tulsa for three weeks engaging with the community. Stephen Towns practice is informed by engaging with archival photos of African Americans. He is here to engage with the Eddie Fay Gates Collection, but not specifically limited to that. Stephen Towns will be back on November 5th for a lecture about his experience and the impact upon his artwork. Brian Whisenhunt is excited to have him here engaging with the Eddie Fay Gates Collection. Stephen Towns also has space at the Tulsa Artist Fellowship for the First Friday Art Crawl.

Gilcrease is also hosting Scrollathon October 6th through 10th which will bring five hundred Tulsans together with the Ladd Brothers to create a new work of art for Gilcrease Museum. The Ladd Brothers are two brothers who have a practice working in beadwork and fabric. The finished art piece will include photographs and oral histories. The community lead program Uncrease sent out a call for proposals and received almost two hundred proposals for the community performance, activities, workshops and other events in the building has been rescheduled for March through May of 2026. Pamela Amburgy asked Brian Whisenhunt if the museum was engaging with school children during the time of the museum being re-built. Brian Whisenhunt replied that the museum has been very involved in the local public schools.

B. Public Safety

Due to time constraints the report was read and accepted.

C. Parks

Due to time constraints the report was read and accepted.

D. Transportation

Due to time constraints the report was read and accepted.

E. Financial

The March collections were \$9.1M, which is about 4.4 percent below budget. Current sales tax collections are about 0.3 percent below budget for the year to date.

VI. Unfinished Business

There was no unfinished business discussed.

VIII. New Business

STOC

Sales Tax Overview Committee

There was no new business discussed.

A. Chair Presenters

Date	Presenter	Backup
May 7	Linda Jenkins	
June 4		

5/7, 6/4, 7/2, 8/6, 9/3, 10/1, 11/5, 12/3


IX. Adjournment

Motion to adjourn was made by Pamela Amburgy and seconded by Uriah Davis. Adjournment was at 9:20.

Ashley Webb, Chair



Kathy Sebert, Vice Chair



STOC

SALES TAX OVERVIEW COMMITTEE

Ashley Webb
Chair

Ashley R. Webb
Riggs, Abney, Neal, Turpen, Orbison & Lewis Inc.
Attorney At Law
Tulsa, OK 74119
(918) 699-8905

To: City Council
Date: April 2, 2025
Subject: April Report to City Council

Attached is the March 2025 Sales Tax Overview Committee (STOC) Status Report

2006 Special Extended Sales Tax

There were no expenditures in February. Encumbrances and commitments total \$702,000. Current appropriations for the 2006 Third Penny Sales Tax Extension Fund total \$273,275,000. There is a current appropriation balance of \$5,824,000.

2008 Sales Tax Special Temporary Streets

There were no expenditures in February. Encumbrances and commitments total \$38,000. Current appropriations for the 2008 Sales Tax Special Temporary Streets Fund total \$149,658,000. There is a current appropriation balance of \$4,281,000.

2014 Sales Tax

February expenditures totaled \$1,814,000, of which \$633,000 was spent on the Bridge Replacement And Rehab project. Encumbrances and commitments total \$55,098,000. Current appropriations for the 2014 Sales Tax Fund total \$580,369,000. There is a current appropriation balance of \$75,526,000.

2016 Sales Tax

February expenditures totaled \$4,839,000, of which \$4,462,000 was spent on the the Tulsa Vision Advanced Sales Tax Revenue Bonds debt service project. Encumbrances and commitments total \$5,399,000. Current appropriations for the 2016 Sales Tax Fund total \$399,172,000. There is a current appropriation balance of \$68,731,000.

2016 Revenue Bond

February expenditures totaled \$304,000, of which \$281,000 was spent on the Gilcrease Museum Expansion project. Encumbrances and commitments total \$11,546,000. Current appropriations for the 2016 Revenue Bond Fund total \$350,600,000. There is a current appropriation balance of \$6,399,000.

2020 Sales Tax

February expenditures totaled \$4,237,000, of which \$2,736,000 was spent on the Fire Apparatus and Equipment project. Encumbrances and commitments total \$9,368,000. Current appropriations for the 2020 Sales Tax Fund total \$150,506,000. There is a current appropriation balance of \$50,173,000.

2024 General Obligation Bonds

February expenditures totaled \$1,205,000, of which \$569,000 was spent on the Citywide Grant-Matching Funds for Streets project. Encumbrances and commitments total \$10,029,000. Current appropriations for the 2024 General Obligation Bonds Fund total \$156,285,000. There is a current appropriation balance of \$102,771,000.

2020 General Obligation Bonds

February expenditures totaled \$2,459,000, of which \$708,000 was spent on the Gilcrease Rd: Pine St to Admiral Blvd project. Encumbrances and commitments total \$29,749,000. Current appropriations for the 2020 General Obligation Bonds Fund total \$224,405,000. There is a current appropriation balance of \$112,067,000.

2014 General Obligation Bonds

February expenditures totaled \$2,279,000, of which \$937,000 was spent on the Maintenance Zone 3010 project. Encumbrances and commitments total \$32,443,000. Current appropriations for the 2014 General Obligation Bonds Fund total \$355,000,000. There is a current appropriation balance of \$48,470,000.

2008 General Obligation Bonds

There were no expenditures in February. Encumbrances and commitments total \$1,049,000. Current appropriations for the 2008 General Obligation Bonds Fund total \$231,104,000. There is a current appropriation balance of \$294,000.

2005 General Obligation Bonds

February expenditures totaled \$46,000, of which \$46,000 was spent on the Bridge #162: Boston Ave project. Encumbrances and commitments total \$885,000. Current appropriations for the 2005 General Obligation Bonds Fund total \$75,966,000. There is a current appropriation balance of \$13,000.

Respectfully submitted,

Ashley Webb, Chair



Attachments

cc: Christy Basgall
Jarrod Moore
Jake Epp



FINANCIAL REPORT TO CITY COUNCIL

Wednesday, April 2, 2025

I. Financial Report

Revenue: 2016 Vision 0.805 Percent and 2020 Sales Tax 0.45 Percent Sales Tax Funds

		Fiscal Year to Date
	February	Thru February
Actual	\$ 8,969,145	\$ 81,124,192
Adopted Budget - Current Year	9,189,534	80,935,782
Actual vs Budget	\$ (220,389)	\$ 188,410

Expenditures

Fund	February	Fiscal Year to Date Thru February
409 - 2020 Sales Tax	\$ 4,236,256	\$ 16,036,292
4001, 4003, 4004 - Tulsa Vision Rev Bonds	303,533	2,371,062
4000 - Tulsa Vision Sales Tax	4,838,084	38,726,186
405 - 2014 Sales Tax	1,813,835	12,175,390
404 - 2008 Streets Temporary Sales Tax	-	19,073
402 - 2006 Special Extended Sales Tax	-	539,196
TOTAL \$	11,191,708	\$ 69,867,198

II. Expenditures in Other Funds

Fund	February	Fiscal Year to Date Thru February
401 - 2001 Sales Tax	14,360	14,360
429 - 2024 GO Bond	1,204,301	37,506,112
428 - 2020 GO Bond	2,458,949	22,131,904
427 - 2014 GO Bond	2,278,948	11,713,914
426 - 2008 GO Bond	-	-
425 - 2005 GO Bond	46,000	164,450
TOTAL \$	6,002,557	\$ 71,530,739

III. Items for the City Council's Attention

- A. Monthly Financial Reports
- B. STOC Committee and Subcommittee Minutes and Reports

IV. Attachments

- A. Attendance Record for the last 12 months
- B. STOC Committee and Subcommittee Minutes and Reports

Respectfully submitted,

Ashley R. Webb, Chair

Attachments

cc: Christy Basgall
Jarrod Moore
Jake Epp

MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY

As of February 28, 2025

	CURRENT APPROPRIATIONS	EXPENDITURES		ENCUMBERED/ COMMITTED	PERCENT	BALANCE
		Current Month	Life To Date			
Fund 401 and Fund 403						
2001 Third Penny Sales Tax and 2006 Advance Funded Sales Tax	\$ 112,613,794	\$ 14,360	\$ 112,611,407	\$ -	100%	\$ 2,387
Fund 402						
2006 Third Penny Sales Tax Extension	\$ 273,274,569	\$ -	\$ 266,748,643	\$ 701,538	98%	\$ 5,824,389
Fund 404						
2008 Sales Tax Special Temporary Streets Fund	\$ 149,658,132	\$ -	\$ 145,338,831	\$ 37,841	97%	\$ 4,281,459
Fund 405						
2014 Sales Tax Fund	\$ 580,368,725	\$ 1,813,835	\$ 449,745,023	\$ 55,097,596	87%	\$ 75,526,106
Fund 406: 4000						
2016 Sales Tax Fund	\$ 399,171,895	\$ 4,838,084	\$ 325,041,751	\$ 5,399,160	83%	\$ 68,730,984
Fund 406: 4001, 4003, 4004						
2016 Revenue Bond Fund	\$ 350,600,000	\$ 303,533	\$ 332,655,540	\$ 11,545,761	98%	\$ 6,398,699
Fund 409						
2020 Sales Tax Fund	\$ 150,506,112	\$ 4,236,256	\$ 90,965,455	\$ 9,367,740	67%	\$ 50,172,917

MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY

As of February 28, 2025

	CURRENT APPROPRIATIONS	EXPENDITURES		ENCUMBERED/ COMMITTED	PERCENT	BALANCE
		Current Month	Life To Date			
Fund 429						
2024 General Obligation Bonds	\$ 156,285,000	\$ 463,191	\$ 43,484,993	\$ 10,028,609	34%	\$ 102,771,398
Fund 428						
2020 General Obligation Bonds	\$ 224,405,000	\$ 2,458,949	\$ 82,588,760	\$ 29,749,345	50%	\$ 112,066,895
Fund 427						
2014 General Obligation Bonds	\$ 355,000,000	\$ 2,278,948	\$ 274,086,950	\$ 32,443,165	86%	\$ 48,469,885
Funds 426						
2008 General Obligation Bonds	\$ 231,103,878	\$ -	\$ 229,760,841	\$ 1,048,941	100%	\$ 294,096
Funds 425						
2005 General Obligation Bonds	\$ 75,966,289	\$ 46,000	\$ 75,067,905	\$ 885,374	100%	\$ 13,009
Fund 740: 7401-7408						
TMUA--Water Capital Fund	\$ 552,745,405	\$ 1,691,497	\$ 424,276,760	\$ 63,654,834	88%	\$ 64,813,811
Funds 750: 7501-7522						
TMUA--Sanitary Sewer Capital Funds	\$ 678,887,729	\$ 3,730,840	\$ 555,311,861	\$ 67,358,801	92%	\$ 56,217,068

STOC

Sales Tax Overview Committee

MINUTES Sales Tax Overview Committee Meeting February 25, 8:00 a.m. 175 E 2nd St, Tulsa OK

The Sales Tax Overview Committee met for the regular monthly meeting at 8:00 a.m. on February 25, 2024.

I. Call to Order

Ashley Webb called the meeting to order at 8:02 a.m.

The following members were present:

Ashley Webb	Linda Jenkins	Kathy Sebert	Tige Rodgers
Steve King	Scott Grizzle	Brett Friesen	
Maia Treleaven	Matt Meyer	James Deming	
Deborah McKinney	Paul Hassink	Pamela Amburgy	

The following members were not present:

Charles Wilkes	Jennifer White	Sylvia Powell
Mareo Johnson		

Also present:

Steve Lassman	Jonah Toay	Chris Havenar	Karen Gillis
Michelle Barnett	Jake Epp		

II. Approval of Minutes

Ashley Webb made a motion to approve both December and January minutes with the exception of adding Steve King to the roster of members present. Pamela Amburgy seconded, and the motion carried.

III. Chair's Report

Ashley Webb spoke to the Council that Sales Tax Revenues were down in the month of January. He commented that there were several new faces in the Council. Kathy Sebert mentioned that Karen Gilbert was back as a Counselor again.

IV. Committee Reports

STOC

Sales Tax Overview Committee

A. Vision

Michelle Barnett and Jonah Toay from Tulsa Partner spoke to the STOC committee. Michelle Barnett is the Senior Vice President of Economic and Workforce Development for Partner Tulsa. She mentioned that there had last been a report back in the month of December, with a summary of annual work in revitalization revolving loan. Linda Jenkins asked for clarification on which project Michelle Barnett was referring to. Michelle Barnett said that she was reporting on Item Eleven Project Number 170080 and Project Two: Retail Revitalization Revolving Loan Fund, Project One: Business Resilience and Recovery Fund, and some parts of Project Four: Communications Strategy. Jonah Toay the Small Business Development Manager for Partner Tulsa, helps with small business development and retail revitalization rotating loan fund. The fund was originally used to develop businesses along the bus rapid system corridor, to help create vibrant commercial projects. City Council expanded the fund so that it also includes commercial corridors as identified by the retail market strategy that was implemented in 2018. This fund provides a zero percent interest loan for businesses to plug the gap between different sources of funding. The funds cap out at either \$200,000.00 or 20% of the funding needed. Tulsa Economic Development Corporation approves the loans, then TEDC will refer a client to Tulsa Partner to help with additional sources of funding. City Council then approves the funding once the approval process goes through Tulsa Partner. Pamela Amburgy asked Jonah Toay if the loans were operating funds for business. Jonah Toay clarified that that yes, the loans were operating funds. Pamela Amburgy commented that if the funds are revolving then how long will the funds revolve. Ashley Webb commented that in theory the funds were regenerating. Jonah Toay replied that the loans were intended to be short term loans, most of the loans he had experience with were around seventy-two months. Deborah McKinney asked if there was a certain time period that loans were opened and closed by and were loan applicants informed if they were approved or not. Michelle Barnett answered that most loan applicants come through TEDC, so Tulsa Partner worked alongside TEDC. Linda Jenkins commented that it would be nice to know what the address was of the businesses that had received the loans and when the award was actually made. Linda Jenkins remarked that Silk Salon and Tuly's Tacos were downtown, and Decopolis is at 11th and Peoria. Michelle Barnett mentioned that fifteen corridors had been identified. Linda Jenkins asked if there were any projects up at 36th Street North in her area. Michelle Barnett said that Tulsa Partner was working with Tulsa Housing Authority for over a year and a half on putting together a facade grant program for North Tulsa commercial facilities or building. Linda Jenkins asked if next time Tulsa Partner returns if the STOC could have address of business, when loans were awarded and counsel districts of the businesses. Pamela Amburgy mentioned that the hold up on Gilcrease Museum could not get a certificate of occupancy till the summer because of the marble on the steps being unfinished. Kathy Sebert mentioned that if the steps came by April, then it would be fifteen to sixteen weeks before the museum could open.

B. Public Safety

Deborah McKinney commented that she was surprised that the manufacture of the new fire engines were allowing the firemen to tell them where they want their tools placed in the engines. Kathy Sebert mentioned that the new mayoral administration had just announced the re-organization of City Design Studios and the Department of City Experiences. Paul

STOC

Sales Tax Overview Committee

Hassink commented that Ellen Ray was one of the designers that moved. She was under James Wagnor and is now under Anna America. Steve Lassman remarked that Anna America will now be over Parks, Asset Management, and the former City Design Studio. Ellen Ray will be staying under James Wagner.

A new ground-breaking for the William S. Smith African Wilds is scheduled for March 5th at the Tulsa Zoo. Pamela Amburgy mentioned that the STOC would probably need a new Zoo report soon.

C. Parks

Steve Lassman reported on the McClure Park project. ACS is currently fabricating a shade sale turf area to be delivered mid-March and to begin installing the plunge pool area. This area is intended to be a lounge area. The lounge area is to be completed by the summertime. The plunge pool had been demolished.

Ashley Webb mentioned that the Aquatics Director Nick Pond should be excited about the improvements. Steve Lassman commented that Nick Pond just turned in his resignation and is moving to the City of Norman.

Steve Lassman will have an update on Fred Johnson Park and draft plans in the next STOC report. It includes a new playground, water feature, skate feature, covered basketball court, dog park area and pickle ball courts.

D. Transportation

Ashley Webb commented that there were no public notices yet on the multi-million-dollar Gilcrease road expansion. Kathy Sebert mentioned that Doug Helt did a walk-through and a punch list.

E. Financial

The February collections were \$9.2M, which is about 2.4 percent below budget. Current sales tax collections are about 0.2 percent below budget for the year to date.

VI. Unfinished Business

There was no unfinished business.

VIII. New Business

A. Chair Presenters

Date	Presenter	Backup
Apr 2	Ashley Webb	
May 7	Linda Jenkins	

4/2, 5/7, 6/4, 7/2, 8/6, 9/3, 10/1, 11/5, 12/3

IX. Adjournment

STOC


Sales Tax Overview Committee

Motion to adjourn was made by Kathy Sebert and seconded by Maia Treleaven. Adjournment was at 9:15.

Ashley Webb, Chair

Handwritten signature of Ashley R. Webb in black ink.

Kathy Sebert, Vice Chair

Handwritten signature of Kathy Sebert in blue ink.

Sales Tax Overview Committee

STOC

SALES TAX OVERVIEW COMMITTEE

12-Month Attendance Record

Mar-25

Member	Expires	District	Jan-25	Feb-25	Mar-25	Apr-24	May-24	Jun-24	Jul-24	Aug-24	Sep-24	Oct-24	Nov-24	Dec-24	# Attended	# Possible	Comments
Wilkes, Charles	Dec-26	1	A	A	P										1 of 12		
Jenkins, Linda (Secretary)	Dec-28	1	P	P	P										3 of 12		
Asbjornson, Scott	Dec-26	2	A	P	P										2 of 12		as of Dec. 23
Powell, Sylvia	Dec-24	2	A	A	P										1 of 12		
Friesen, Brett	Dec-26	3	P	P	P										3 of 12		as of 6/24
Vacant	Dec-24	3	NM	NM	NM										0 of 9		
Rodgers, Tige	Dec-26	4	P	P	P										3 of 12		as of 12/24
Webb, Ashley (Chair)	Dec-24	4	P	P	P										3 of 12		
Sebert, Kathy (Vice-Chair)	Dec-26	5	P	P	P										3 of 12		
White, Jennifer	Dec-28	5	P	A	A										1 of 12		
Treleaven, Maia	Dec-28	6	P	P	P										3 of 12		as of Aug. 2023
Davis, Uriah	Dec-26	6	NM	NM	P										1 of 10		as of Mar 25
Meyer, Matt	Dec-26	7	P	P	P										3 of 12		
Deming, James	Dec-24	7	P	P	P										3 of 12		
McKinney, Deborah	Dec-26	8	P	P	P										3 of 12		as of Sep 23
King, Steve	Dec-28	8	P	P	P										3 of 12		
Grizzle, Scott	Dec-26	9	P	P	P										3 of 12		
Hassink, Paul	Dec-24	9	P	P	P										3 of 12		
Amburgy, Pamela	Dec-26	M	P	P	P										3 of 12		
Jessica Reyes	Dec-28	M	NM	NM	P										1 of 10		as of Jul 23
Johnson, Mareo	Dec-26	M	A	A	P										1 of 12		as of Mar 25
Members Present			14	14	19	0	0	0	0	0	0	0	0	0			

A = ABSENT

P = PRESENT

NM = NO MEMBER APPOINTED

OC = OUT OF COUNTRY

OT = OUT OF TOWN on Business

Prepared by City of Tulsa
Department of Finance
Budget & Planning Division
Capital Planning Section

(2) Tulsa Economic Development Project

Attendees:

Kathy Sebert
Pamela Amburgy
Steve King
Paul Hassink
Uriah Davis
Matt Meyer
Mareo Johnson
Linda Jenkin
Deborah McKinney



DATE:
April 15, 2025

To: STOC

From: Parks, Culture & Recreation – CABS (City Architectural Building Services)

Subject: Vision Tulsa Project Updates

– **Projects List**

1. 170000 Zink Dam
2. 147200 Williams Crossing (Arkansas River Pedestrian Bridge)
3. **170005 South Tulsa / Jenks Lake and Related Amenities**
4. 170010 Turkey Mountain Urban Wilderness
5. 170020 New Trail East Bank Cousins
6. 170025 23rd & Jackson Redevelopment
7. 170030 Gilcrease Museum
8. 170050 Tulsa Zoo Elephant Exhibit
9. 170065 South Mingo Corridor
10. 170080 Citywide: Commercial Revitalization
11. 170080 Citywide: Route 66
12. 170080 Citywide: Gateway Signage
13. 170085 Peoria-Mohawk Business Park
14. 170145 Vision Arts – Tulsa Arts Commission

– **Completed Projects**

170035	Cox Arena District	January 2019
170035	Cox Business Center Renovation	September 2023
170040	Tulsa Fairgrounds	November 2021
170045.1	Airport Infrastructure – AA Tail Slot	January 2019
170045.2	Airport Infrastructure – Navistar	December 2021
170045.2	Airport Infrastructure – Spirit	December 2024
170045.4	Airport Infrastructure – AA	July 2024
170055	Langston Healthcare	December 2024
170060	BMX National Headquarters	January 2025
170070	Public Schools Safety First	February 2025
170095	Community Health East Clinic	April 2020
170100	Air National Guard MTC	September 2024
170110	North Peoria Connection, 56 th – Mohawk	March 2020
170115	TCC Career Placement	August 2019
170125	McCullough Park	February 2023
170130	Mohawk Sports Complex	March 2022
170135	GO plan Bike Ped Master Plan	March 2022
170140	Route 66 Train Depot	October 2022

1. No. 170000

Project Name: Zink Dam
 Representative: Brooke Caviness, COT
 Total Funding: \$63,602,369.27
 Available Funding: \$63,602,369.27
 Design Firm(s): Jacobs/CH2MHill, HISINC, LLC
 Contractor: Crossland Construction Company
 Start Date: 10.18.2020
 Anticipated Completion: August 2024 (Opening held Labor Day 2024)

- Construction 105.8% billed, 95.07% time (updated for Change Order #4) as of **03.18.25**
- Dam and flume substantial completion **08.30.24**
- Punch list underway for Crossland, working to complete by **late Spring 2025**
- Items include:
 - City fiber coordination for wave park camera network quote received 01.21.25, Purchase Order in process, **ongoing**
 - Obermeyer inclinometers – fine tuning programming in process, **ongoing**
- Assembling of O&M manuals in process

2. Project No. 147200

Project Name: Williams Crossing (Arkansas River Pedestrian Bridge)
 Representative: Jeff Stava, RPA/TGP and Brooke Caviness, COT
 Total Funding: \$34,650,000.00 (\$27.4M City, \$7.25M private)
 Available Funding: \$34,650,000.00
 Design Firm(s): SBP, MVVA, GKFF, and River Parks
 Contractor: Crossland Construction Company
 Start Date: 05.14.2021
 Anticipated Completion: Fall 2024 (opening held Labor Day 2024)

- Tier III Funding - \$7.25 million in funding and donations secured
- Construction \$30,702,616.22 of \$31,769,504, or 96.6%. as of 04.15.25
- The project is substantially complete
- Added bike and pedestrian trail intersection painted markings at east and west River Parks trails with remaining contingency funds, 100% closeout billings to be submitted once painting is completed
- Trail safety work to be completed Spring / Summer 2025 with private donor money

3. No. 170005

Project Name: South Tulsa / Jenks Lake and Related Amenities
 Representative: Veronica Page and Brooke Caviness, COT
 Total Funding: \$64,214,000.00
 Available Funding: \$27,737,208.88
 Design Firm(s): Jacobs, Black & Veatch, PMg
 Contractor: TBD
 Start Date: TBD
 Anticipated Completion: TBD

- Cost estimate to be based on 10% Conceptual plans
- Agreement to PCSSC **04.16.25**
- Field explorations:
 - Survey: April 20225

- Geotech: May – June 2025
- Design effort (less than 10%): February 2026
- Cost estimate: February 2026

4. Project No. 170020

Project Name: Turkey Mountain Urban Wilderness
 Representative: Jeff Edwards, RPA (River Parks Authority)
 Total Funding: \$ 7,600,000.00
 Available Funding: \$ 7,600,000.00
 Design Firm(s): LandPlan Consultants, Inc (LPCI)
 Contractor: TBD
 Start Date: TBD

- Acquisition of property: \$5,490,928.25
- Turkey Mountain Master Plan components: \$2,109,071.75
 - Updated master site plan 10.18.23 provides overall site planning strategy for the south side of Turkey incorporating all projects: (RAISE Grant to extend west bank trails from Turkey Mtn to Jenks, REI and possible changes to 71st and Elwood intersection, parking lot expansion at Turkey, and a new voter approved IOT 2023 maintenance facility for River Parks to possibly be located at Turkey).
 - Now that master plan has been updated, final modifications to 71st Street trail improvements are moving ahead.
 - Plans being revised to align with Master Plan and feedback to be given prior to going out to bid. Plans being revised by Landplan for 71st Street connector trail project for bidding **Spring 2025, ongoing.**
- Amendment with Landplan forthcoming to design a below grade tunnel pedestrian crossing from the access road off 71st street, **ongoing.**
- RPA has received preliminary design of tunnel for the safe crossing along 71st and the rehab connector hard paved trail and is under review, **ongoing.**
- RPA has trail maintenance projects underway. New and old trail alignments to address erosion and clearing, ongoing.
- ODOT final land boundary has been defined and land acquisition price offer for portions of one of the westerly 2 Placerder properties (City owns) has been finalized at \$1,388,777.
- No impact on Mitchell Park exchange parcel.
- Funding received from ODOT from land sale will reimburse the Vision Tulsa funding for RPA.
- A subsequent amendment will be entered into with RPA to fund Turkey Mountain improvements.
- COT and RPA have entered into a MOU for City Engineering to administer the bidding of the 2 parking lot projects, bids pre-work with Tri-Star held 01.20.25.
 - Paving the existing gravel lot at Elwood and West 61st Street - Vision funding and Tulsa County ARPA funding.
 - New parking lot for trailhead on Placerder property - ARPA funds.
 - **Site clearing and grading is ongoing for the west parking lot.**
- Wallace Engineering is designing a safe road crossing from the upper parking lot to the new water tower site that will be activated with an additional 8 miles of multi-use trails in early 2025.
- Private funding will be constructing an outdoor downhill bike park in early 2025.
- Roughly 6 new miles of trails have been constructed (The Sanctuary Trails) – **Anticipated opening is slated for 06.04.25.**
- **71st Connector Trail pavement upgrade update: Due to a critical ATT fiber line in the path of the re-designed tunnel for the pedestrian and roadway separation, the project is on hold for construction until ATT determines when the communication line can be moved.**

5. Project No. 170020

Project Name: New Trail East Bank 101st to Cousins Park

Representative: Henry Som de Cerff, COT
Total Funding: \$ 4,000,000.00
Available Funding: \$ 600,000.00
Design Firm(s): LandPlan Consultants, Inc (LPCI), Garver
Contractor: TBD
Start Date: TBD

- Conceptual design completed 02.16.2018 (\$68,454.00)
- Conceptual cost estimate for trail \$10.2 million, with time value at 3% for 13 years - \$15.0 million, with land, total cost is \$26 million.
- TAP (Transportation Alternative Program) grant awarded March 2021 through INCOG to fund design (\$133,991.00 requested, \$107,193.00 awarded, COT to pay additional \$27K to fund the full design value of \$133,991) for Riverside Drive (Vensel Creek to south of Creek Turnpike)
 - Land Plan has been selected as design consultant for Vensel Creek design plans only (does not include construction funding).
 - Scoping agreement ODOT LG 2360. This area is also in the footprint of the RAISE grant, design among 2 projects to be coordinated as part of effort.
 - An NTP has been received from ODOT for the Vensel Creek portion. **Survey is ongoing.**
- TA (Transportation Alternative) grant applications: 3 additional segments to Cousin's Park have been approved., 103rd to 110th awarded \$1M federal funds
Design Agreement has been approved with Garver. **NTP from ODOT is pending.**
- Funding Agreements for 110th to 116th and 116th to 121st have been routed to ODOT for execution.
- Trail segments will be coordinated with the South Tulsa / Jenks Dam project – **ongoing**

6. Project No. 170025

Project Name: 23rd & Jackson Redevelopment Site – Relocation Study Design and Acquisition

Representative: COT
Total Funding: \$1,000,000.00
Available Funding: \$ 181,000.00 balance
Design Firm(s): Cyntergy

- Scope includes planning, design work and partial acquisition costs to relocate Public Works, update master plan site at Harvard and Mohawk, appraise and acquire operation yard location.
- Draft report submitted to Administration, February 2020
- Acquisition of 2 parcels – Tulsa County Yard on North Harvard - \$320K (Vision funding), 56th & Garnett - \$1.46 million (water enterprise funds) – closing for both 08.30.2020
- **Operations staff supporting TARE, Water and Sewer, and a non-profit group has occupied Engineering North and South Buildings.**
- **Balance of funding to be used by Water and Sewer to address parking lot once building is demolished at 2445 S. Jackson. Waiting for environmental evaluation of asbestos before building can be demolished.**

7. Project No. 170030

Project Name: Gilcrease Museum
Representative: Brian Lee Whisenhunt, Gilcrease, Mary Womble, COT
Current Budget: \$140,465,850
Total Funding: \$140,465,850 (\$91,517,113 public + \$48,948,737 private, includes \$1,250,00 from Osage Nation)
Fundraising Goal: \$ 0
Design Firm(s): Smith Group, 1 Architecture; Gallagher & Associates, Scenario
Construction Manager: Flintco, LLC
Start Date: 05.10.22
Scheduled Completion: September 2025

Anticipated Completion: September 2025 (Building only, Exhibits November 2026)

- Funding:
 - Public Funding total: Vision (\$65 M), Remaining bond funds from past Gilcrease projects (\$2.6 M), IOT 2 (\$6 M), ARPA City Funding (\$1 M), Public Utilities (\$817,113.00), Supplemental Appropriations (\$6.1M), IOT3 (\$10M) = \$91,517,113.00
 - Private Funding total (\$48,948,737)
- Building Construction **93.9% billed as of 03.31.25.**
- Delivery of remaining metal roof panels and Sky Stair metal panels from Spain have caused a delay in construction, weekly calls held to push schedule, **ongoing**
- Architectural punch walk **held 03.12.25 and 03.13.25, punch list working**
- Construction update from **03.25.25** attached at end of report.
- Exhibits fabrication – **billed 14.3%** – Scenario: \$13,232,479.00. Kickoff for exhibits held 10.02.24, weekly calls ongoing with design and construction team. Exhibits to be completed late 2026.
- Osage Nation north parking lot – **completed 03.28.25**

8. Project No. 170050

Project Name: Tulsa Zoo Elephant Exhibit
Representative: Lindsay Hutchinson, TZMI, Steve Lassman, COT
Total Funding: \$ 25,000,000.00
Available Funding: \$ 25,000,000.00 (City) + \$7.6M (TZMI) = \$32.6 M
Design Firm(s): Selser Schaefer Architects dba Narrate
Construction Manager: Nabholz Construction
Start Date: 04.04.22
Scheduled Completion: March 2025
Anticipated Completion: March 2025

- \$20M of \$25M was previously allocated for Elephants with remaining \$5M originally allocated for front entrance.
- TZMI requested remaining \$5M to go towards Elephants, TZMI has funded remaining \$7.6M for Elephants.
- Total budget for Elephants is \$32,682,000, fundraising is complete.
- TZMI amendment approved by Board the week of 06.05.23 to eliminate cap on TZMI private fundraising, City funding is capped.
- IOT (Improve our Tulsa) 2 to provide \$6M to front entrance in FY25 / FY26.
- Ribbon cutting held **04.07.25**
- **Closeouts and O&M warranties being compiled**

9. Project No. 170065

Project Name: South Mingo Corridor
Representative: Patty Parks, COT
Total Funding: \$ 15,000,000.00
Available Funding: \$ 15,000,000.00
Design Firm(s): Benham Design, LLC (170065), Garver (170065A), Poe (170065B)
Contractor: APAC Oklahoma (170065 First Phase)
Tri-Star Construction, LLC (170065A Second Phase)
Start Date: 01.27.25 (170065A Second Phase)
Scheduled Completion: TBD
Completion: TBD

- First Phase: 71st to 81st on Mingo (Project 170065) – complete as of 01.31.23
- Second Phase: 91st from Mingo to Memorial (Project 170065A)
- Garver is consultant

- 404 permit submitted to USACE on 10.11.21, will get 404 permit before project goes out to bid. Preliminary 404 mitigation cost is approximately \$1.1M
- NWP (Nationwide Permit) approved by USACE 09.12.22, valid until 03.14.26. Aquatic Resource Protection Plan required as part of USACE 404 permit. ARPP approved 10.01.24
- Honey Springs Mitigation Bank credit cost \$973,706.50, agreement signed 12.14.22
- Construction funding in Improve Our Tulsa 2 - \$10.7 million
- Right-of-way: (20 parcels identified originally) complete
- Utilities: Windstream, ONG and PSO are complete
- Contractor Tri-Star Construction LLC, \$12,800,000.00. Contract executed 10.01.24
- Construction started 01.27.25. **Site grading and temporary asphalt placement is ongoing.**
- **Third Phase: 81st to 91 on Mingo (Project 170065B)**
- Poe is consultant, Contract fulfilled at 60% plans: contract complete 09.01.2020
- Estimated construction cost is \$ 9 M, does not include ROW or utilities
- Construction funding in 2026 (earliest). Design to be completed at a later date.

10. Project No. 170080

Project Name: Citywide Commercial Revitalization
 Representative: Michelle Barnett, Partner Tulsa
 Total Funding: \$ 3,600,000.00
 Available Funding: \$ 1,454,393.39 remaining
 Design Firm(s): Place Dynamics, Inc., Medium Giant

- Retail Market Study by Place Dynamics, Inc. (\$125K) completed January 2019
 - Will inform use of Commercial Revitalization fund, as well as assist Route 66 Commission in targeting Route 66 funds
- **Project 1: Business Resilience and Recovery Fund** - \$1.1 million Total.
 - Reimbursement from CARES act dollars is expected to fully fund the Commercial Revitalization Strategy.
 - All funds disbursed (\$1.1 million)
 - City has received \$994,777.14 as of 02.10.25 in repayments
- **Project 2: Retail Revitalization Revolving Loan Fund** - \$1.5 million Total (formerly Bus Rapid Transit Revolving Loan Fund)
 - \$725,058 loaned to date, \$674,942 remaining obligated to loan
 - TAE0 awarded \$950,000 grant from THA/HUD for expansion of RRRLF in 36th Street North and North Peoria corridors leveraging \$140,000 in local match as detailed in Project 4 below.
- **Project 3: Destination Districts** - \$250K Total.
 - \$32K spent, \$218K left to spend
 - COT administering (Samantha Exance with Tulsa Planning Office): Greenwood, Route 66, Kendall Whittier, and Global District (formerly International District) (21st & Garnett area).
 - Remaining \$218K will be used to designate new destination districts. City staff working to expand program to allow for more models of participation and the majority of funds will be used for kickstarting new districts
 - **Destinations Districts Retreat held 03.25.25 – informed community members and business and property owners focused on placemaking, collaboration and upcoming projects in Tulsa’s districts.**
- **Project 4: Communications Strategy** - \$400K Total.
 - \$100K spent, \$300K encumbered
 - \$100K – Medium Giant media strategy consultant - work completed
 - TAE0 engaged national vendor, Retail Strategies, in April 2024 to actively market city sites to retail brokers using its funding.
 - Encumbered \$300,000 to support Retail Revitalization Revolving Loan Fund expansion with HUD funding in January 2025.

- Local match of \$160,000 to leverage \$1,050,000 in federal funding for RRRLF specific to the 36th Street North and North Peoria corridors – encumbered – to be implemented as contract between City and TEDC
- Façade Improvement grant – local match of \$140,000 proposed to leverage \$950,000 in Choice Neighborhoods grant – TAE0 Board approved 12.19.24.
- Contract from City to TAE0 planned for Mayor’s signing agenda week of 02.21.25.
- Final THA/HUD approval to begin Façade Grant Program expected March 2025.

11. Project No. 170080

Project Name: Route 66 Beautification & Reinvestment
 Representative: Autumn Tiller, COT
 Total Funding: \$ 3,700,000.00
 Available Funding: \$ 810,000.00 (\$265K each year through 2028)
 Design Firm(s): COT staff

- Route 66 Commission and COT staff providing oversight.
- Retail Market Study informed targeted funding uses on corridor
- Uses include marketing, wayfinding, façade grants, neon sign grants, project maintenance and Special Events grants.
- 76 neon sign grants in various stages of contracting through installation.
- Total for neon signs: **\$1,396,592.92** total costs, **\$504,106.44** total grants.
- Marketing contract with Undaunted signed 08.10.23 ended 08.31.24.
- The Commission has decided not to select any of the respondents from the marketing RFP and have chosen to use Visit Tulsa for marketing to maximize ongoing efforts for the upcoming Rt 66 centennial in 2026.
 - Visit Tulsa will perform the Commission’s typical marketing campaigns as well as work on event planning for the centennial.
 - Agreement with Visit Tulsa signed by Mayor 02.12.25 and work is underway, **\$75,000 billed to date**
- Avery Centennial Plaza: 25 of 28 bollard covers have been installed, 3 damaged bollards **to be replaced pending material availability.**
- E 11th Street Streetscape: This original Vision 2025 project included fluted pole with Route 66 Tulsa Banners in the center median between a Wayfinding sign at Mingo Road and an Interpretive Plaza south of the Mingo intersection.
 - Vision Tulsa Repair and Replace project: Replace 4 banners and 2 fluted poles. Replace bracket arms for all 9 fluted poles. Repair 2 pole footings resulting from vehicle collisions and theft.
 - Project has been awarded, materials **shipped** to site late February 2025, installation by Third Generation Electrical **date TBD.**
- Crystal City replacement plaques for (5) vandalized locations – **costs gathered 02.24.25, install date contingent on production.**
- Route 66 Rising: **painting quote received 02.25.25, sheet metal quote outstanding.**
- Cyrus Avery Pedestrian Bridge Repairs: metal mesh “Tulsa” panel replacement estimate received 02.17.25
- Meadow Gold sign repairs: **additional neon repairs completed 03.05.25**
- Rose Bowl and Meadow Gold historical markers damaged / missing; original vendor contacted for quote 04.03.25

12. Project No. 170080 / CP 23-09

Project Name: Citywide: Gateway Signage
 Representative: Elliott Stiles, COT and Daniel Jeffries, COT (TPO)
 Total Funding: \$ 3,600,000.00
 Available Funding: \$ 1,625,000.00 (\$265K each year through 2028)
 Design Firm(s): Landplan
 Start Date: 01.06.25

Scheduled Completion: TBD

- Project includes 42 signs citywide, as funding allows
- Agreement for design executed 12.09.24
- 2 Gateway Triangle signs on east and west ends of City proposed to be done by Route 66 centennial, 2026
- Surveys have started, 12.13.24, all completed as of 04.14.25
- 25% plans due mid-April 2025

13. Project No. 170085

Project Name: Peoria-Mohawk Business Park
Representative: Josh Miller, GKFF
Total Funding: \$ 10,000,000.00
Available Funding: \$ 3,860,000.00 remaining
Design Firm(s): Cedar Creek (no Vision funding) - Phase I
Route 66 Engineering - Phase II
Contractor: Crossland Heavy Phase I
Crossland - Phase II
Start Date: 01.20.25 (Bid package 4)
Scheduled Completion: TBD
Completion: TBD

- Bid package 1 – mass grading with earth change permit – completed 04.30.20
- Bid package 2 – public road and site utilities – completed 09.30.2020
- Bid package 3 – scope is water line, paving, storm and sidewalks / trail for Mohawk Blvd and the Utica cul-de-sac off 36th street North – completed 05.15.22
- 61.4% of \$10 million has been expended (\$ 3,860,000.00 remaining)
- IDP permit issued 04.30.24.
- Bid package 4 – Bids for public infrastructure opened late August 2024, uses the \$3.86M
- Scope of project includes installing an 8” water line, storm drainage to Dirty Butter Creek, widening of 36th Street North with a sidewalk, and a sidewalk extension along Mohawk.
- Initial work on widening 36th Street North and the associated storm and waterline work beneath began 01.20.25, ongoing.
- The reroute of the existing 12” waterline is complete and waiting on City testing.
- The storm water extension work is ongoing, and the new Wheeling Place has been cut in with the cul-de-sac now poured.
- The screening berm along Mohawk is planned to begin in early May 2025.
- The whole project is planned to be completed by 07.31.25.
- This investment will stimulate additional improvements by manufacturing companies looking to build new build-to-suit facilities estimated to be approximately \$40 million.

14. Project No. 170145

Project Name: Vision Arts – Tulsa Arts Commission
Representative: COT
Total Funding: \$ 2,250,000.00
Available Funding: \$ 900,000.00

- 1st round of artist grants totaling \$300K, 29 agreements signed by Mayor 09.02.2020
- 2nd round of grants totaling \$300K, 33 agreements approved by Mayor 03.03.2021.
- 3rd round of grants totaling \$150K, 12 agreements approved by Mayor 06.08.2022
- 4th round of grants totaling \$150K (Vision Arts 4) 21 agreements signed by Mayor 08.14.23.
- 5th round of grants totaling \$150K (Vision Arts 5) 21 agreements signed by Mayor as of 11.13.24. spending: 07.01.24, to 06.30.25.
- 6th round of grants totaling \$150K (Vision Arts 6)

- 44 Proposals received 12.22.24.
- Arts Commission approved grantees 03.10.25
- **Mayor approved the following 20 artist organizations on 03.26.25**

Small Organization Awards (13):

- Theatre North - \$10,000
- Tulsa Shakespeare Company - \$9,000
- Portico Dance Theatre Inc. - \$9,000
- LoLoLook - \$9,000
- Redfork Arts Foundry Tulsa - \$8,000
- Red Dirt Relief Fund - \$7,000
- World Stage Theatre Company - \$7,000
- Clark Youth Theatre - \$6,000
- Tulsa Peoples' Orchestra - \$5,000
- Goff Center for the Continuous Present - \$5,000
- Kendall Whittier Main Street - \$5,000
- Hued Songs, Inc. - \$5,000
- Trueson Daughtery - \$5,000

Large Organization Awards (7):

- Tulsa Opera, Inc. - \$15,000
 - Tulsa Historical Society - \$12,000
 - Philbrook Museum of Art - \$10,000
 - Signature Symphony at TCC - \$8,000
 - Brady Craft Inc. (DBA 108 Contemporary) - \$5,000
 - Downtown Tulsa Partnership - \$5,000
 - Tulsa Symphony Orchestra - \$5,000
- **Agreements to be processed and approved by Mayor for 07.01.25 to 06.30.26 spending cycle**



GILCREASE MUSEUM
Thomas Gilcrease Institute of American History and Art

Construction Update March 25, 2025





GILCREASE MUSEUM
Thomas Gilcrease Institute of American History and Art

Construction Update March 25, 2025



L1 Main Entry Lobby



LL2 Gallery

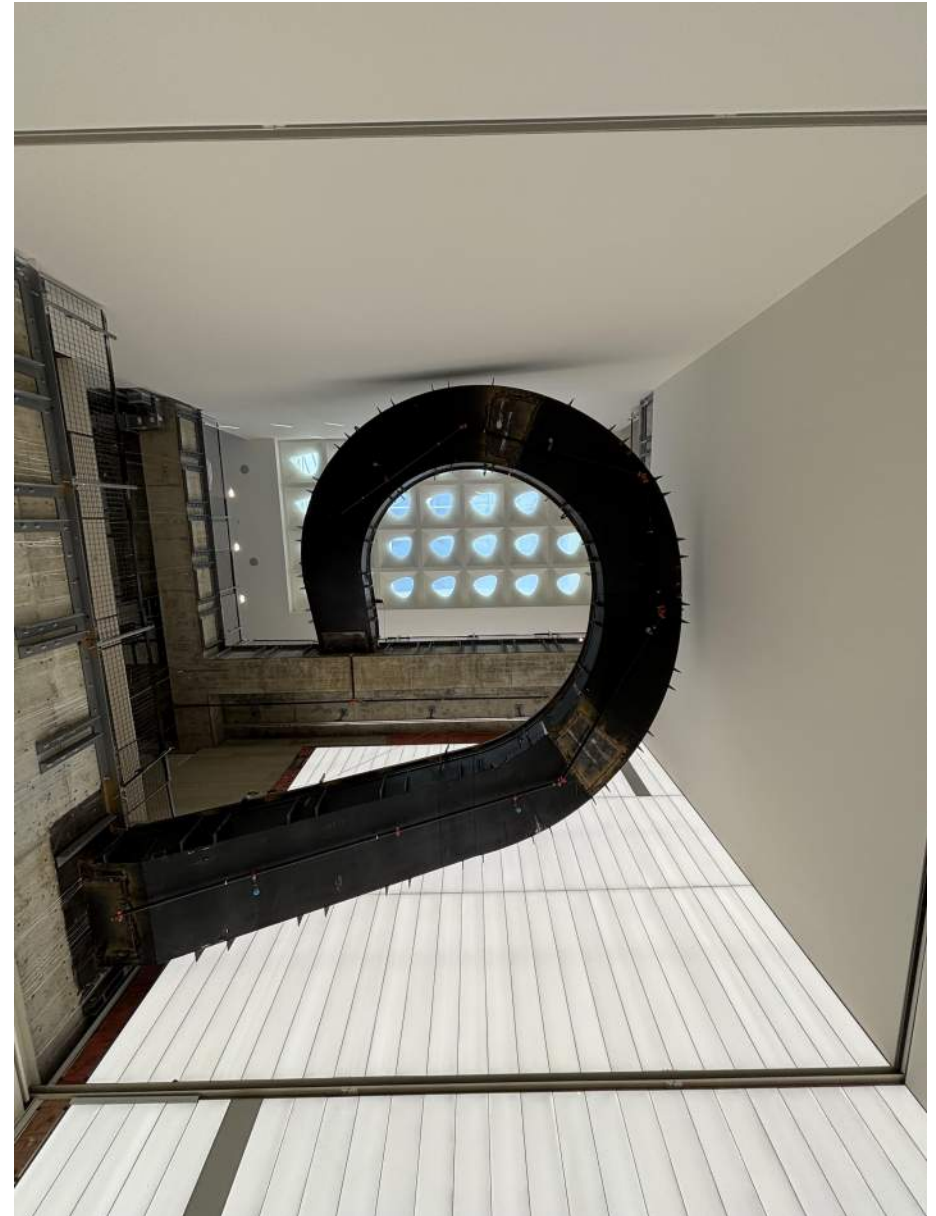


GILCREASE MUSEUM
Thomas Gilcrease Institute of American History and Art

Construction Update March 25, 2025



LL2 Community Gallery



Atrium from LL2



GILCREASE MUSEUM
Thomas Gilcrease Institute of American History and Art

Construction Update March 25, 2025



L2 Cafe



L1 Lobby



L1M Green Room



LL1 Admin



Destination Districts Update

Sam Extance, Destination Districts Manager



Destination Districts Program

To create vibrant places where people want to be.



Goals:

- Foster authentic cultural expression
- Stimulate economic development
- Develop civic pride
- Deepen the connections to places that will allow our city to retain talent and attract new residents
- Increase tourism opportunities



Destination Districts Retreat

2nd Annual Retreat – 45+ attendees

A day long event focused on placemaking, learning, and community. Covered a wide variety of topics, including:

- Building a District Tour
- The First 16 Feet
- Saavy Tulsa Program
- Public Art 101
- Launch of Design & Lease Guide Resource
- And more!



Commercial Corridor Safety Guide

Your Tool to Create Safe, Resilient Communities

This online guide provides business and property owners with helpful tips, resources, best practices, and ideas to make their business and commercial corridor safer. **Covering a wide variety of topics, including:**

- Starting a Business Watch
- Keeping Employees Safe
- Designing your Space to Prevent Crime
- Removing Graffiti
- Responding to Emergency Situations
- And so MUCH more!

Available in 100+ languages

TULSA
LEASE +
DESIGN
GUIDE



Scan & Download



[https://www.globaldistrict.org/
designleaseguide](https://www.globaldistrict.org/designleaseguide)



Questions?

Sam Extance (sjextance@cityoftulsa.org | 918-596-7651)

TulsaPlanning.org/dd

	B	C	D
1	VISION TULSA - PROJECT ACTIVITY / NEXT STEPS 03.27.25		
2	PROJECT - Economic Development	COST	COMMENTS AND NEXT STEPS
3	Arkansas River Infrastructure & Amenities (City of Tulsa Share)		
4	Zink Lake and Related Amenities		- Project coordination team: CH2 (Jacobs), GKFF, MVVA, Holly Frontier, AEP/PSO, LandPlan, INCOG, City, River Parks, Crossland, Parks and Recreation Dept, and PMG.
			- Crossland Construction Company
			- Construction is substantially complete .
			- As of 2024 \$44,823.554,34; 105.7% billed ;
			- O&M manuals being worked on by Jacobs and Obermeyer .
			- As-recorded drawings pending with project close-out .
5	Low-Water Dam with Recreational Gates & Flume	\$48,000,000	- ONGOING
6	New Pedestrian Bridge (Williams Crossing)	\$15,000,000	- Complete - All City funds expended .
7	Mitigation, Bank Stabilization & Outfall Protection for Dam		- Complete
			- Design team is Jacobs, Black & Veatch, environmental permitting consultation with PMg; City Project Manager Veronica Page; and City Project Director Brooke Caviness. Public outreach will be coordinated through DCE.
			- Cost Estimate to be based on 10% Conceptual Plans:
			> SCOPE IN FROM CONSULTANT: April 1, 2025
			> AGREEMENT EXECUTION
			Consultant: April 1, 2025
			City of Tulsa: PCSSC April 16, 2025
			Pending City Legal approval to Mayor: April 23, 2025
			> FIELD EXPLORATIONS:
			Survey: April 2025
			Geotech: May – June 2025
			> DESIGN EFFORT (less than 10%): February 2026
			> COST ESTIMATE: February 2026
8	South Tulsa/Jenks Lake and Related Amenities	\$64,214,000	- ONGOING
9	Low-Water Dam and Pedestrian Bridge		- \$8.3 million for land acquisition includes land for trail to Cousins Park. NO CHANGE
10	East Bank Park, Boat Dock, and Abutment Improvements		
11	Vensel Creek Park and Boat Dock		
	East Bank Trail Connection from Low-Water Dam to Vensel Creek		
12			
13	Mitigation, Bank Stabilization & Outfall Protection		
			- Turkey Mountain Master Plan components being constructed.
			- New parking lots for trail head on Placerder property (East Parking) and paving East Parking lot currently gravel. Project is under construction:
			> West parking lot is being cleared and graded. To be completed prior to work on East Parking lot.
			> East parking existing gravel lot at Elwood and West 61st Street is under contract for improvements.
			- 71st Street connector Trail
			> Trail to be coordinated with 71st and Elwood REI street improvements.
			> Project bidding is pending
14	Turkey Mountain Urban Wilderness	\$7,600,000	- ONGOING
			1) USACE Pre-construction Engineering and Design (PED)
			a. Cutoff Walls at superfund site, discussing alts EPA / USACE trying to break out this segment from balance of work. Call with EPA/ODEQ 02.10.25 ONGOING
			b. Anchoring structure at Charles Page Blvd.
			c. Armored overtopping area on B was 3,000 ft, now 200' - 500' per USACE.
			d. Filtered berms for A & B will not go to contracting until funding available. Filtered berms for tiebacks being evaluated. Project being evaluated for possible work segments.
			e. Levee B-Tieback to provide req'd FEMA fb (1% event is contained but does not have 4' of fb near the US412 bridge) USACE is evaluating the fill and will coordinate with FEMA.
			f. Repairs or replacement of selected culverts/penetrations/outfalls (A and B)
			g. USACE March 2023 total cost estimate \$191,057,000 compared to previous \$150,864,000. Local share \$70 million.
			h. USACE update on funding is PENDING
			2) PL 84-99 Emergency Repairs (PIR) due to May 2019 event. No local funds required.
			a. USACE repaired erosion areas and pump stations
			3) EDA Grant
			a. 100% plans approved by EDA and USACE.
			- Levee 12 Stakeholder January meeting canceled:
			- The Oklahoma State legislature approved \$50 million in funding towards the local match for Federal program. Governor Stitt signed 05.31.24.
			- Levee District invoiced City for our portion of local share for PED 11.04.24 in accordance with agreement. Payment being processed.
			- Environmental issues at Superfund site to be discussed at Friday coordination meeting at INCOG with USACE and stakeholders.
15	Levee District #12 Rehabilitation - Local Matching Funds	\$5,000,000	-- Project is being worked with USACE, EDA, and local governments. ONGOING
			- LandPlan is design consultant. Garver selected for RAISE grant with LandPlan as subcontractor.
			- Transportation Alternative grant: 103rd to 110th awarded \$1 million federal funds. Local share ranges from 20% to 30%;
			- Funding agreement with INCOG to ODOT is approved.
			- Consultant Selection 11.01.24; NTP 12.01.24; 30% Design 04.01.25; 90% field review Planned 10.01.25; ROW to be submitted in April 2025. ONGOING
16	New Trail, East Bank-101st to Cousins Park (Design and Matching Funds), AKA "River Parks Trail 101st to 121st"	\$4,000,000	
			- Project report submitted in 2020.
			- Operations staff supporting TARE, Water and Sewer, and a non-profit group has occupied Engineering North and South Buildings.
			- Balance of funding to be used by Water and Sewer to address parking lot once building is demolished at 2445 S. Jackson. Waiting for environmental evaluation of asbestos. ONGOING
17	23rd & Jackson Redevelopment Site - Relocation Study, Design & Acquisition	\$1,000,000	

	B	C	D
1	VISION TULSA - PROJECT ACTIVITY / NEXT STEPS 03.27.25		
2	PROJECT - Economic Development	COST	COMMENTS AND NEXT STEPS
			- Gallagher & Associates (G&A) - Owner's Representative (TU and City of Tulsa) - SmithGroup Architect / Flintco CM - Total cost is: \$140,465,850 . - Building to be complete September 2025 - construction 93.1% billed as of 02.28.25 . - Delivery of roof metal panels and sky stairs are being shipped from out of country. Last shipment is scheduled for 04.07.25 via air-freight (4 weeks) . - Osage Nation is finalizing the seal coat on existing parking spaces in April. The new parking lot is substantially complete . - Exhibit fabrication bid and construction administration with Scenario 02.28.25, 11.7% billed. Work to be complete November 2026 . - Preliminary schedule for exhibit construction and move of collection, Tentative complete: November 2026, Project closeout December 2026 / January 2027. - ONGOING
18	Gilcrease Museum Expansion	\$65,000,000	
19	Cox Business Center	\$54,500,000	- 100% Complete 09.27.2023
20	Arena District Master Plan	\$500,000	- 100% Complete January 2019
21	Tulsa Fairgrounds	\$30,000,000	- 100% Complete 11.09.2021
22	Airport Infrastructure		- Projects summarized below with descriptions (\$27,300,000 total)
23	American Airlines Total:	\$14,500,000	
24	AA Tail Slot	\$2,122,396	100% Complete 01.08.2019
25	Hangar 80 Re-Skin	\$1,497,344	100% Complete 01.11.2024
26	AAERO APU	\$2,005,981	100% Complete 07.10.2024
27	Master Plan	\$416,319	100% Complete 01.11.2024
28	Plating Shop Roof and Make-Up-Air Units	\$2,400,000	100% Complete 01.11.2024
29	Central Utility Plant Cooling Tower & Hangar 6 Cooling Tower	\$5,930,357	100% Complete 02.26.2024
30	Miscellaneous Expenses	\$127,604	Complete
31		\$12,250,000	
32	Airport Facilities:		
33	Air Force Plant 3 (AFP3) - Navistar	\$2,200,000	100% Complete
			- Partner Tulsa and Airport are focusing on Air Force Plant 3, Building 7 clean-up. Funds needed are \$1.3 million Vision with additional funding from DEQ and EPA funding will be used.
34	Airport (general)	\$1,674,483	- Building 7 agreement is pending for building roof.
35	City Airport Facilities - Building 6 Roof	\$925,517	- Building 6 roof replacement is COMPLETE 02.03.25
			- Spirit: \$5.0 million for various City owned facilities improvements > Paving and resurfacing COMPLETE > Fire hydrant replacements and valve repairs TMUA-W 21-08 work is COMPLETE December 2024 .
36	Spirit Leasehold Properties	\$5,000,000	
37	Grant Matching Opportunity	\$3,000,000	- To be used for future hangar grant. Local match is anticipated to be \$3.0m - NO UPDATE
38	Tulsa Zoo & Living Museum		
			- Selser Schaefer, dba Narrate is design consultant and Nabholz is CM - Grand Opening will include new barn, containment yard, and renovation of existing barn will be complete spring 2025. - Ribbon Cutting Ceremony - Mary K. and John T. Oxley Elephant Experience 04.07.25
39	Elephant Experience	\$25,000,000	
40	Langston University - Tulsa Healthcare Professions Complex Exp	\$16,250,000	- COMPLETE December 2024
41	BMX National Headquarters	\$18,600,000	- COMPLETE January 2025
42	South Mingo Corridor	\$15,000,000	
43	Mingo, 71st to 81st	\$7,489,800	
			- 2nd Phase - Engineering Consultant: Garver, 91st, Memorial to Mingo - Construction funding in Improve Our Tulsa 2 - \$10.7 million - Right-of-way Complete - Construction contract with Tri-Star: Start 01.27.25 - Utility relocations complete for ONG, PSO, and Windstream - Clearing and removal of trees on north in vicinity of 92nd EA is complete. - Temporary asphalt on south side of 91st to allow for widening of north lanes. Traffic shifted and lanes through intersections at Memorial and Mingo reduced the week of 03.24.25. - Estimated Completion December 2026.
44	91st Street, Mingo to Memorial	\$6,768,044	
45	Mingo, 81st to 91st	\$742,156	
46	Public Schools - Safety First Initiative	\$14,500,000	- COMPLETE 02.25.25
47	Capital Equipment (non-Public Safety)	\$12,000,000	- No action required
48	Citywide & Route 66 Beautification and Reinvestment		- Order of work: 1. Commercial Revitalization 2. Route 66 3. Beautification - Total of \$11,000,000 split into projects below.

	B	C	D
1	VISION TULSA - PROJECT ACTIVITY / NEXT STEPS 03.27.25		
2	PROJECT - Economic Development	COST	COMMENTS AND NEXT STEPS
			- Project 1: Business Resilience and Recovery Fund - \$1.1 million Total - Reimbursement from CARES act dollars is expected to fully fund the Commercial Revitalization Strategy - All funds disbursed (\$1.1 million) - City has received \$994,777.14 as of 02.10.25 in repayments ONGOING - Project 2: Retail Revitalization Revolving Loan Fund - \$1.5 million Total (formerly Bus Rapid Transit Revolving Loan Fund). - \$725,058 loaned to date, \$674,942 remaining obligated to loan. - Local match of \$160,000 to leverage \$1,050,000 in federal funding grants. - Local match of \$140,000 to leverage \$950,000 in Choice Neighborhoods grant for facade improvements. - Project 3: Destination Districts - \$250K Total - \$32K spent, \$218K left to spend - Destination District workshop held 03.25.25 - Developed a Commercial Corridor Safety Guide which can be accessed on-line dealing with safety tips with Police and Fire, business watch program, emergency plans, and delivery vehicle safety. - COT administering (Samantha Extance): Greenwood, Route 66, Kendall Whittier, and Global District (formerly International District) (21st & Garnett area) - Project 4: Communications Strategy - \$400K Total - \$100K spent, \$300K left to spend - \$100K – Medium Giant media strategy consultant - Launch of a \$150K - \$300K marketing campaign paused until Partner Tulsa hires a Director of Retail Recruitment – offers made, no hires yet ongoing - Once hired, this person will take a comprehensive look at commercial revitalization efforts and the use of remaining funds. NO UPDATE
49	Citywide Commercial Revitalization	\$3,600,000	
			- Route 66 Commission and Tulsa Planning staff to provide oversight - Neon sign grant program - 76 in various stages of contracting, variance / permitting and construction. \$497k in matching grants awarded to date (\$1.4 million total spent) - Legal department pursuing a trademark license agreement for commercial use of the recently awarded Patent and Trademark Office naming Tulsa as "Capital of Route 66". - Commission has approved Meadow Gold sign repairs, Cyrus Avery bridge repairs, metal mesh Tulsa replacement, Crystal City plaque vandalism repairs, etc. ONGOING
50	Route 66	\$3,700,000	
			- Gateway Beautification Signage Project CP 23-09 - 25% plans due 03.31.25 - Project scope is 42 signs citywide (or as funding allows). Survey of 36 sites complete as of 03.18.25. - Additional coordination of placement is ONGOING.
51	Citywide Beautification	\$3,700,000	
			- 100% appropriated funds are encumbered or expended with NP36 LLC - NP36 will cause to be constructed additional improvements that may include, but not be limited to manufacturing buildings, parking lots, site utilities, sidewalk on 36th St North, sidewalk extension on Mohawk Blvd, widening portion of 36th St North, stormwater drainage system to Dirty Butter Creek, etc. with footprints of building pads to support manufacturing facilities. - The private investment in these buildings and associated non-public improvements is estimated to be approximately \$40 million. - Construction started 01.20.25. Rough grading of Wheeling Street is ONGOING.
52	Peoria-Mohawk Business Park	\$10,000,000	
	Public Schools - Partnership with Union, Jenks & Tulsa Public Schools in Teacher Retention, Recruitment, and Training Efforts	\$10,000,000	- Schools share \$1.4 million per year - \$10 million appropriated to date. Balance is \$1,743,134.57 82.6% expended - ONGOING
53			
54	Community Health Connection East Clinic	\$9,975,000	- 100% Complete 04.13.20
	Air National Guard F35 (Mission Training Center) Simulator Training Center	\$9,400,000	- COMPLETED, DEDICATION HELD 09.04.24, FINAL PAYMENT PROCESSED.
55			
56	Discovery Lab - Tulsa Children's Museum Permanent Site	\$8,000,000	- COMPLETE 01.24.22.
	Peoria Connection - North Peoria Avenue, 56th St. to Mohawk Blvd.	\$7,000,000	
57			
58	Peoria BRT	\$3,700,000	- HNTB is design consultant for BRT. BRT completed 03.31.20 - BRT funding at \$4.8M. Only will use \$3.7M (additional communications work underway) Completion estimated April / May 2025. ONGOING
			- NTEDI reduced standard meetings due to completion of scoping of current projects. Standing meetings are 4th Tuesdays, 10:30 am - New traffic signals at Peoria and two connections to Mohawk – Project to advertise April 2025. - Peoria Street Rehab between 36th Street North and 56th Street North. ONGOING
59	Peoria Enhancements 56th Street North to Mohawk Blvd	\$3,300,000	
60	TCC Career Placement	\$5,320,000	COMPLETE
			- Brown Ordinance; project deleted. Money (\$3,600,000.00) reallocated to BMX, 05.08.19
61	University Center at Tulsa Authority/OSU-Tulsa		
62	McCullough Park	\$3,600,000	COMPLETE - RIBBON CUTTING 02.16.23
63	Mohawk Sports Complex	\$3,500,000	COMPLETE
	GO Plan - Priority Projects Identified in the Bicycle/Pedestrian Master Plan	\$3,125,000	COMPLETE
64			
65	Route 66 Village Train Depot	\$3,000,000	COMPLETE
			- 1st round \$300K for COVID-19 artist relief grants - 29 agreements COMPLETED - 2nd round \$300K of grants approved by Mayor 03.03.21 - 33 agreements COMPLETED - 3rd round \$150K of grants approved by Mayor 06.08.22 - 12 agreements COMPLETED - 4th round (FY24) \$150K of grants approved by Mayor 03.22.23. 21 of 21 agreements signed by Mayor as of 08.14.23. - 5th round (FY25) \$150k of grants approved by Mayor 05.01.24; 21 agreements executed and are in various phases of invoicing to be completed by 06.30.25. - 6th round (FY26) \$150k of grants - workshops held in October and next one is in November. 44 proposals received 12.22.24. - Arts Commission approved grantees 03.10.25. Should be approved by Mayor in April 2025. ONGOING
66	Tulsa Arts Commission	\$2,250,000	
67	Tulsa Performing Arts Center Trust	\$1,000,000	COMPLETE
68	TOTAL	\$510,634,000	

(3) Public Safety and Economic Development

Attendees:

Kathy Sebert
Matt Meyer
Linda Jenkins
Mareo Johnson
Scott Asbjornson
Maia Treleaven
Scott Grizzle
Deborah McKinney
Ashley Webb
Steve King



INTEROFFICE CORRESPONDENCE

TO: Sales Tax Oversight Committee (STOC)
FROM: Major Jillian Phippen, PAS
DATE: April 1, 2025
SUBJECT: Tulsa Police Fleet Activity

Fiscal Year 2024-Fleet Vehicles

Fifty-eight (58) new Ford Police Interceptor Utilities were ordered and all fifty-eight (58) have been received and fifty-seven (57) have been outfitted and are in service. One (1) is being upfitted.

Fiscal Year 2024/25-Fleet Vehicles

Fifty-nine (59) new Ford Police Interceptor Utilities have been ordered, thirty (30) have been received. Sixteen (16) have been placed into service and fourteen (14) are being outfitted.

Fourteen (14) undercover Ford F150s have been ordered and eight (8) have been received and placed in service.

Air Support Helicopters

Both Police 1 and 2 are fully operational.

- Police 1-Tail number N901TP, 2023 Airbus H125
- Police 2-Tail number N302TP, 2023 Airbus AS350B3

JP:jp

**Tulsa Fire Department
Sales Tax/Bond Projects Report
2/5/2025**

Josh Lamb
Chief of Physical Resources
Office (918) 596-1230
Mobile (918) 527-0262
joshlamb@cityoftulsa.org

Technical Heavy Rescue

P.O. 232194

Estimate \$2,006,959.45 Funded by SAFER savings

Preconstruction meetings will be held May 4-7.

Delivery is expected in February of 2026.

Extended Cab Air Trucks

P.O. 232195

Estimated total \$689,858.66 Funded by SAFER savings

Two F-550 extended cab 4x4 mini-rescue body Air Trucks.

Delivery is expected in December 2025. No new activity.

HazMat Air Truck (Small)

P.O. 240318

Estimate \$367,274.41 Funded by IOT-2

One F-550 crew cab 4x4 mini-rescue body HazMat Air Truck

Delivery is expected in June of 2026. No new activity.

Four Stock Engines

Requisition 20241097

P.O. 241130

Combined Estimate \$3,646,003.04

Funded by IOT-2 plus \$910,174.56 from SAFER savings

Pierce Enforcer Cab Pumpers without equipment

One is expected to go in service next week. The other 3 are anticipated by the end of the month.





DATE:

April 8, 2025

To: STOC

From: CABS (City Architectural Building Services), Mary Womble, AIA

Subject: CABS Project Updates

Active Projects List:

- | | | |
|-----|-------------------------------|--|
| 1. | 67520, 040430-7, and CP 23-13 | 815 S Riverside Drive |
| | a. RFP 24-327 | Roadside Attraction |
| | b. RFP 25-900 | Interactive Technology |
| | c. RFP 24-925 | Commercial Development |
| 2. | CP 24-24 | CCP Elevator Modernization |
| 3. | SP 22-12A | Municipal Courts Building ADA |
| | SP 22-12B | OTC ADA |
| 4. | 16-1-1453XX | TPAC Renovations |
| 5. | CP 24-37 | TPAC (Tulsa Performing Arts Center) IOT3 Renovations |
| 6. | SP 23-2 | TPAC – ARPA Projects |
| 7. | 146120 | TPD Uniform Renov. – Gilcrease & Riverside |
| 8. | 145500 | Animal Shelter Expansion, Phase 1 & 2 |
| 9. | SP 21-5, 2234B00006 | Citywide Public Facilities – Roofs |
| | a. SP 23-6 | Reed Park Roof Replacement |
| | b. SP 22-14 | East Yard Water Distribution Satellite Office Roof |
| | c. SP 21-7 | AB Jewell Maintenance Roof Replacement |
| 10. | 2234B00024 | Citywide Public Facilities Rehab / Repair |
| 11. | SP 20-6 | Greenwood Cultural Center Facility Rehabilitations |
| 12. | CP 23-10 | Public Safety Center |
| 13. | 147150 | Tulsa Zoo Carnivores and African Wilds |
| 14. | CP 24-20 | Tulsa Zoo Rainforest HVAC and Electrical Upgrades |
| 15. | CP -xx | Tulsa Zoo Entrance and Parking Improvements |
| 16. | SP 22-7 | Tulsa Police Department – Heliport |
| 17. | CP 24-19 | BOK Center & Arvest Convention Center – IOT3 |
| 18. | CP 24-27 | AFP3 Building 7 Roof Replacement |
| 19. | OSU LRFP | OSU VA Parking Garage |
| 20. | 2159FR0299 | TIA Airport ATCT and TRACON – ARPA |
| 21. | CP 24-32 | Bells Station – Route 66 Village Improvements |
| 22. | 2159FR0297 | Family Safety Center Campus – ARPA |
| 23. | TMUA-ES 2025-03 | Long Range Facility Plan for NSWWTP |
| 24. | SP 25-38 | Bazaar Grocery Store – Tulsa Metropolitan Ministries |

1836 x 1898

TUL x USA



1. Project No. 067520, 040430-7, and CP 23-13

Project Name: 815 S. Riverside Drive
Location: 815 S. Riverside Drive
Council District: 4
Representative: Mary Womble, COT
Total Funding: \$6,500,000 original funding (\$5M Vision 2025, \$1.5M Sales Tax) Available
Funding: \$4,903,968.71 (sales tax)
Design Firm(s): TBD
Contractor: TBD
Start Date: TBD
Anticipated Completion: Varies by project - TBD

- New efforts to develop site began fall 2023 via stakeholder engagement.
- Roadside Attraction RFP 24-327 (public art) - \$250,000 budget
 - Mayor signed on selected artist (Ken Kelleher); award made on 08.22.24
 - Neighborhood event held with Riverview to discuss process on 09.10.24 and landed on a final concept with Cry Baby Hill organizers with additional local iconography.
 - Final design released 11.04.24 with aligned statement from Tulsa Tough; contract executed 11.13.24.
 - Installation schedule contingent on development plans; art to be maintained by development team.
 - **Awaiting receipt of OK licensed structural engineering plans for final review (04.10.25)**
- Interactive Technology RFP 25-900 - up to \$300,000 budget
 - Up to 20 site-specific digital installations to be installed along Route 66 corridor
 - Technology consulting team to consist of product development and curatorial content/research expertise
 - Met with Visit Tulsa 10.01.24 to discuss long-term marketing & operational plan.
 - 3 proposals shortlisted; selection anticipated January 2025 following interviews
 - Devising scope of sites based on available budget for physical structures (i.e. obelisk with QR scan card) and how to market this resource appropriately.
PROJECT ON HOLD (02.25.25)
- Commercial Development RFP 24-925 - up to \$4.5 available in incentives
 - RFP issued 04.29.24, 4 responses received following 07.24.24 due date.
 - Sharp Development selected for Palmera vision - boutique recreation of vintage auto court motels. Project kickoff held 10.14.2024.
 - Sharp proposal only requested \$2.5M of incentive funding, leaving more dollars available for site improvements.
 - Met with Lt. Governor on 12.07.24. to discuss state-level incentives
 - Draft internal contract completed 12.21.24.
 - Final City incentive contingent on securing additional state-level grants; maximum remains \$4.5M. Submitting applications for TSET and Route 66 Revitalization grants in February. **PROJECT ON HOLD (02.25.25)**

2. Project No. CP 24-24

Project Name: CCP (Civic Center Parkade) Elevator Modernization
Council District: 4
Representative: Max Wells, COT
Total Funding: \$ 1,350,000



Design Firm(s): Cyntergy (by on-call selection)
Contractor: Legend Lifts (\$1,088,000)
Start Date: 03.05.25

- Modernization of CCP elevators by Cyntergy and Lerch Bates, elevator consultant
- Contract between Legend Lifts and TAE0 executed 02.13.25
- Kickoff call held 03.05.05
- **Ongoing bi-monthly meetings started 03.26.25, overall schedule requested from Legend Lifts. Submittals ongoing**

3. Project No. SP 22-12A: Municipal Courts Building ADA and SP 22-12B: OTC ADA

Project Name: ADA Transition Plan – Buildings
Council District: 1 & 4
Representative: Max Wells, COT
Total Funding: \$ 1,275,000
Design Firm(s): GH2
Contractor: Magnum Construction (\$734,856.00)
Start Date: 09.09.24

- Scope includes 90% exterior ADA work at Courts, and 2 OTC packages
- **OTC:**
 - 10th floor fabric wall panels waiting on fabric samples before panel fabrication.
 - Clerk's office millwork counter complete 03.10.25. Glazing replaced 04.08.25.
- **Police Courts:**
 - All work at Police Courts complete, 04.07.25

4. Project No. 16-1-1453XX

Project Name: TPAC Renovations
Location: TPAC, 110 S 3rd Street
Council District: 1
Representative: Mary Womble, COT
Available Funding: \$ 155,000 (balance of CEI Contract)
Design Firm(s): Matrix (closed business late 2022)
Contractor: CEI, new contractor to be selected
Start Date: TBD
Scheduled Completion: TBD

- City filed suit in June 2022 – Case No. CJ-2020-2561
- City refiled suit against CEI in August 2023 – Case No. CJ-2023-2334
- Full inspection of most items (211+ items) with cost estimate report prepared by third-party architect and was received 07.12.24.
- **Met with City legal 02.20.25 to discuss settlement costs. Once settlement is paid, will discuss gathering bids / quote to finish remaining work.**

5. Project No. CP 24-37

Project Name: TPAC (Tulsa Performing Arts Center) IOT3 Renovations
Location: TPAC, 110 S 3rd Street
Council District: 1
Representative: Mary Womble, COT



Total Funding: \$ 79.7M
Available Funding: \$ 5 M
Design Firm(s): Beck Design
Contractor: TBD
Start Date: TBD
Anticipated Completion: TBD

- Initial funding of \$5M allocated November 2024
- Design Agreement with Beck Design ongoing as of 04.10.25
- Selection for CMAR (Construction Manager at Risk) to be sent out tentatively **May** 2025 following Mayoral and Council approval of privately funded portions (in addition to public funding)

6. Project No. SP 23-2

Project Name: TPAC – ARPA Projects
Location: TPAC, 110 S 3rd Street
Council District: 1
Representative: Max Wells, COT
Total Funding: \$5,500,000
Available Funding: \$5,500,000
Design Firm(s): Beck Design
Contractor: Lowry Construction (CMAR)
Start Date: 03.28.23
Anticipated Completion: 06.30.26

- \$3,166,032.92 reimbursed as of 04.08.25
- 3rd Street entrance scheduled for June 2025 – July 2025 construction
- Lighting portion of work to start June 2025

7. Project No. 146120

Project Name: Tulsa Police Department, Uniform Divisions Renovations – Gilcrease and Riverside Divisions
Council District(s): 1 & 2
Representative: Max Wells, COT
Total Funding: \$3,000,000 plus \$300,000 ADA funding
Available Funding: \$2,609,000 plus \$300,000 ADA funding
Design Firm(s): BKL
Contractor: Magnum Construction (\$2,233,072.00)
Start Date: 11.18.24
Scheduled Completion: 11.25.25

- **GID:**
 - Framing drywall, ceiling grid and tile complete
 - HVAC & Lighting complete
 - Asphalt patching complete
 - Painting continues
 - Waiting on new doors
 - Floor & Wall tile to begin soon
 - Parking lot fog seal continues
 - Ballistic glazing on order
- **RID:**
 - Framing and drywall @ 95%
 - Ceiling grid & tile @ 100%, painting @ 10%.
 - EFIS complete on east side of building



- HVAC and Lighting complete
- Fence & Gate installed.
- Asphalt crack & fog seal complete.
- Upcoming: Locker room tile, continue painting

8. Project No. 145500

Project Name: Animal Shelter Expansion, Phase 1 & 2
Location: **5995 E. 36th Street North**
Council District: **3**
Representative: Max Wells, COT
Total Funding: \$ 13,884,552.29 (\$2,750,000 - IOT1; \$2,080,000 - IOT2; \$500,000 - ARPA County; \$2,500,000 - ARPA City; Supplemental Appropriation Budget Amendment - \$6,100,000; \$44,532.29 Transfer from Ventilation project; Crematorium - \$89,980)
Available Funding: \$ 13,884,552.29
Design Firm(s): GH2
Construction Manager: Timberlake Construction Start
Date: TBD
Scheduled Completion: TBD

- **Authorization for Awards of Contracts for Base Bid signed 04.04.25.**
- **Allowance Authorization for Add-Alternate #1 working.**

9. Project No. SP 21-5, 2234B00006

Project Name: Citywide Public Facilities – Roofs
Council District(s): **Varies**
Representative: Max Wells, COT
Total Funding: \$ 2,400,000 Available
Funding: \$ 400,000
Design Firm(s): GH2, BKL, JCJ
Contractor: Lowry

- **Reed Park Roof Replacement (SP 23-6)**
 - 95% Design review meeting held 08.08.24
 - Final document review held 03.07.25, consultant correcting design issues.
 - **Final documents due 04.22.25.**
- **East Yard Water Distribution Satellite Office Roof (SP 22-14)**
 - Project Substantially Complete 11.08.24.
 - Project complete. Final payment to contractor signed by Public Works 02.14.25 and is routing for Mayor's signature.
- **AB Jewell Maintenance Roof Replacement (SP 21-7)**
 - **Final pay routing for TMUA and Mayoral signatures 04.04.25**

10. Project No. 2234B00024

Project Name: Citywide Public Facilities Rehab / Repair



Council District(s): **Varies**
Representative: Thomas Chandler, COT
Total Funding: \$ 7,000,000
Available Funding: \$ 2,610,000

- Work for various projects as maintenance needs arise
- Fire station 32 – ATS microprocessor being purchased
- Fire Station 14 – work on generator March 2025
- Fire Station 12 – updated interior finishes completed for workout room

11. Project No. SP 20-6, 147150

Project Name: Greenwood Cultural Center Facility Rehabilitations
Location: **322 North Greenwood Ave.**
Council District: **1**
Representative: Bhree Barrett, COT
Total Funding: \$ 5,340,000 - IOT2
Consultant(s): JCJ / Moody Nolan Architects
Design Fees: \$128,459.76 (Master Plan) + \$565,076.80 (Design) = \$693,536.56

- Master Plan phase report submitted 10.18.23, budget approximately \$2M+ over.
- Fundraising ideas were contemplated between October 2023 and October 2024.
- GCC Board held meeting 10.16.24 and voted to move forward with City-only funds with no additional fundraising for this phase of the project.
- Project re-kicked off / re-started 10.29.24.
- Design meetings ongoing bi-weekly.
- **50% Design Development set issued 03.28.25.**
- **Site visit to review proposed finishes on 04.01.25.**
- **75% CDs expected mid-May.**

12. Project No. CP 23-10

Project Name: Public Safety Center
Location: **12222 E State Farm Blvd South**
Council District: **7**
Representative: Mary Womble, COT
Total Funding: \$63,500,000 (\$45M PSC, \$16M Maintenance Facility)
Available Funding: \$ 45,000,000 (Allocated November 4, 2024)
Design Firm(s): Narrate and DLR Group
CMAR: Flintco
Start Date: December 2024
Scheduled Completion: TBD

- Building purchased, closed 11.05.24
- Consultant interviews with TPD, TFD, City Medical, TAEMA and Asset Management held late January / early February 2025. **Second round of interviews held first 2 weeks of April 2025**
- Initial programming **validation summary received 03.27.25 and is under review**
- Conceptual design to start **after second round of interviews, 04.14.25, 12-week duration (July 2025)**



13. Project No. 147150

Project Name: Tulsa Zoo Carnivores and African Wilds
Location: **6421 E 36th Street North**
Council District: **1**
Representative: Bhree Barrett, COT
Total Available Funding: \$ 8,000,000 (2014 Sales Tax) + \$20,920,000 (Private funding) =
\$ 28,920,000
Design Firm(s): WDM (contracted with TZMI)
CMAR: Nabholz
Start Date: 03.06.25
Scheduled Completion: TBD

- 81% of funds have been raised by TZMI.
- Reimbursement CPA (Capital Projects Agreement) between TZMI and COT
- Bids opened 11.21.24 for City funds (\$8M) and private funds (\$34M)
- Bids were roughly \$6M high, TZMI Board voted to proceed with re-bidding the project at Board meeting 01.16.25.
- Re-bids opened 02.25.25 and were found to be acceptable.
- **OAC (Owner Architect Contractor) meetings held bi-monthly, started 03.06.25.**

14. Project No. CP 24-20

Project Name: Tulsa Zoo Rainforest HVAC and Electrical Upgrades
Location: **6421 E 36th Street North**
Council District: **1**
Representative: Bhree Barrett, COT
Total Funding: \$ 8,550,000
Available Funding: \$ 8,000,000 (+ \$550,000 future funding, IOT3)
Design Firm(s): EDA-FKI Engineers (contracted with TZMI)
Contractor: TBD
Start Date: TBD
Scheduled Completion: TBD

- AAON is donating HVAC units
- **Received corrections from consultant on 04.04.25 for final review prior to bidding project**

15. Project No. CP-xx

Project Name: Tulsa Zoo Entrance and Parking Improvements
Location: **6421 E 36th Street North**
Council District: **1**
Representative: Mary Womble, COT
Total Funding: \$ 6,000,000
Available Funding: \$ 600,000 (\$600,000 FY25 + \$5,400,000 FY26, IOT2)
Design Firm(s): TBD
Contractor: TBD
Start Date: TBD



Scheduled Completion: TBD

- Fundraising by TZMI in progress, this project will start after Carnivores & African Wilds project is further along and balance of City funding is received in July 2026. (04.08.25).

16. Project No. SP 22-7

Project Name: Tulsa Police Department - Heliport
Location: 6066 East 66th Street North
Council District: N/A
Representative: Max Wells, COT
Total Funding: \$3.5M + \$1M Hardesty Grant + \$250K Chapman grant = \$870 BA
Available Funding: \$4,704,174.51
Design Firm(s): BKL, Inc.
Contractor: Stava (Lyle)
Start Date: 12.05.23
Anticipated Completion: 05.23.25 (early completion expected)

- Project Under Construction – **99% complete, punch list in progress**
- **Ribbon cutting held 04.08.25**

17. Project No. CP 24-19

Project Name: BOK Center & Arvest Convention Center – IOT3
Location: BOK Center & Arvest Convention Center
Council District: 1 & 4
Representative: Mary Womble, COT
Total Funding: \$40,000,000
Available Funding: \$ 8,000,000
Design Firm(s): GH2
Contractor: TVB (Tulsa Vision Builders)
Start Date: 09.17.24
Anticipated Completion: TBD

- Design ongoing
- **Meeting scheduled for 04.14.25 to review costs for BOK and Arvest CC**

18. Project No. CP 24-27

Project Name: AFP3 Building 7 Roof Replacement
Location: Airport
Council District: 3
Representative: Max Wells, COT
Total Funding: \$1,300,000
Available Funding: \$1,300,000
Design Firm(s): JCJ
Contractor: TBD
Start Date: TBD
Anticipated Completion: TBD

- Design Agreement – **routing for Mayoral approval**



19. Project No. 2159FR0285

Project Name: OSU VA Parking Garage
Location: 3rd & Houston
Council District: 4
Representative: Bhree Barrett, COT
Total Funding: \$ 8M sales tax + \$ 4M ARPA = \$ 12M total
Available Funding: \$ 12,000,000
Design Firm(s): GH2
Contractor: Crossland
Start Date: November 2024
Anticipated Completion: November 2025

- Project Under Construction
- First pay application for reimbursement expected **late** April 2025

20. Project No. 2159FR0299

Project Name: TIA Airport ATCT and TRACON - ARPA
Location: Tulsa airport
Council District: 3
Representative: Bhree Barrett, COT
Total Funding: \$7,000,000
Available Funding: \$7,000,000
Design Firm(s): Leo A Daly
Contractor: Flintco (CMAR)
Start Date: October 2024
Anticipated Completion: 06.30.26 (ARPA billings to be complete)

- \$2,628,233.53 reimbursed as of **04.08.25**
- Periodic site visits to review work during construction held on 01.16.25, 03.06.25, ongoing.

21. Project No. CP 24-32

Project Name: Bells Station – Route 66 Village Improvements – IOT2 CD2
Location: 3770 Southwest Blvd
Council District: 2
Representative: Bhree Barrett, COT
Total Funding: \$ 500,000
Available Funding: \$ 500,000
Design Firm(s): BKL, Inc.
Contractor: TBD
Start Date: TBD
Anticipated Completion: TBD

- Design meetings started February 2025.
- Scoping design Agreement with consultant 03.26.25, PCSSC **04.16.25**

22. Project No. 2159FR0297

Project Name: Family Safety Center Campus - ARPA
Location: 2829 South Sheridan Road



Council District: 5
Representative: Bhree Barrett, COT
Total Funding: \$ 1,000,000
Available Funding: \$ 1,000,000
Design Firm(s): KKT Architects
Contractor: Crossland
Start Date: 10.30.24
Anticipated Completion: TBD

- Project Under Construction
- City ARPA money to be used for construction.
- \$1M in ARPA funds has been billed as of 02.28.25
- Periodic site visits with CABS and ARPA every 6 weeks or so – 01.13.25, 03.26.25, ongoing.

23. Project No. TMUA-ES 2025-03

Project Name: Long Range Facility Plan for NSWWTP
Location: NSWWTP (Northside Wastewater Treatment Plant)
5628 N 105th E Ave
Council District: N/A
Representative: Bhree Barrett, COT
Total Funding: \$238,000
Available Funding: \$238,000
Design Firm(s): BKL, Inc.
Contractor: N/A
Start Date: TBD
Anticipated Completion: TBD

- Masterplan for NSWWTP.
- **Kickoff scoping meeting with consultant on 04.04.25.**
- **Awaiting scope and fees from BKL for Agreement preparation**
- **Agreement will include additional funding for 2 buildings**
- **Project kickoff scheduled for 08.08.25.**

24. Project No. SP 25-38

Project Name: Bazaar Grocery Store – Tulsa Metropolitan Ministries, CD3
Location: NE corner of Pine & Yale
Council District: 3
Representative: Mary Womble, COT
Total Funding: \$500,000
Available Funding: \$500,000
Design Firm(s): TBD
Contractor: TMM
Start Date: 01.13.25
Anticipated Completion: TBD

- Project Under Construction. Slab poured 03.17.25
- First reimbursement invoices expected to start April 2025

(4) Parks

Attendees:

Kathy Sebert
Matt Meyer
Linda Jenkins
Scott Asbjornson
Maia Treleaven
Mareo Johnson
Scott Grizzle
Deborah McKinney
Ashley Webb
Steve King

STOC Report

04/10/25

Submitted To: Sales Tax Overview Committee

Submitted By: Steve Lassman

1. McCLURE PARK SLIDE / PLUNGE POOL (147500-1R)

- 7440 E. 7th Street – District 3
- 2014 Sales Tax – part of McClure Pool Reconstruction Project
- **Budget: \$39,647.21**
- Old slide tower removed starting April 26, 2023.
- Project provides shade shelter with tables and benches that can be used for the pool patrons.
- Due to high costs and lack of bidders for slide, we will be demoing plunge pool.
- Met with Ark Wrecking and ACS playgrounds on site 11.19.24. Ark wrecking completed demo to plunge pool on 12.11.24 at a cost of \$26,100.00.
- **Artificial turf surfacing and shade structure ordered from ACS, currently being fabricated. These features will be installed in place of the previous plunge pool site. Equipment delivered on site 04.04.25, contractors to begin work week of 04.07.25 with installation to be complete by early May.**

2. SAVAGE PARK IMPROVEMENTS (147230)

- 17800 E. 21st Street – District 6
- 2014 Sales Tax
- Budget: \$120,000 (\$15,000 in FY2019 and \$105,000 in FY2020)
- Consultant: Method Architecture
- Design Fees: \$22,173.63
- Scope of work: HVAC improvements, flooring, painting, and roofing at Savage Park Concession, Restrooms.
- **Work to be completed by Purchase Orders through City annual contractors in coordination with Little League user group.**

3. WOODWARD PARK IMPROVEMENTS (147250)

- 2324 S. Rockford Ave. – District 4
- 2014 Sales Tax (147250.ArchEngr.)
- Budget: \$4,850,000 (\$870k in FY20 and \$3,980k in FY21)
- Consultant: LandPlan Consultants, Inc.
- Kick-off meeting was held June 10, 2020.
- 100% design was submitted on April 21, 2023. Staff have reviewed documents in preparation for advertising for bids. Review comments have been submitted to the Consultant.
- Tree damage from the June 2023 storm has been coordinated with the Consultant.
- Final review with consultant was held December 14, 2023. Changes to the irrigation system and civil work are to be made to protect the root zones of existing trees.
- Revised 100% Documents received April 18, 2024. Staff is preparing documents to advertise for bids.
- Pre-Bid meeting July 16th 2024 and bids open August, 16th 2024.
- Notice to Proceed sent. Conformed drawings received. Construction contract signed by Mayor. Pre-Work Meeting held 12.16.2024.
- **Groundbreaking was expected 01.21.25 and has been delayed while contractors source a 90" RCP pipe. Meet with Landplan and Jonesplan 03.14.25 to discuss RCP revisions and confirm changes.**
- **Expected groundbreaking and construction to start Late April, 2025**

4. CHAMBERLAIN PARK POOL RECONSTRUCTION (147300)

- 4940 North Frankfort Ave. – District 1
- 2014 Sales Tax (147300.ArchEngr.)
- Budget: \$2,424,185 IOT2 + **\$1,000,000 IOT3 + \$192,793.07 McClure Funding Transfer + \$103,902.07 Whiteside Plumbing Transfer + \$8,919.22 Playground Equipment Transfer + \$325.81 Whiteside Pool Transfer + \$5,201.03 Playground Surfacing for an updated budget of \$3,735,327.77**

Consultant: Alaback Design Associates

- Design Fees: \$266,583.77

STOC Report

04/10/25

- Community Outreach approved Pool moving to Chamberlain Park – Brown Ordinance processed.
- Contract was approved March 9, 2022. Design Kick-off meeting was held March 17th.
- 100% Documents were submitted on January 17, 2023.
- Final drawings were submitted on August 31, 2023.
- Submittal to State Health Department occurred on September 6, 2023.
- Health Department approval was received January 9, 2024.
- Advertising for bids began January 19, 2024, with bids opening February 16, 2024
- Bid has been awarded to Magnum Construction at a cost of \$3,437,544 for the base bid.
- **Pool Excavation and construction of pool house ongoing. Ongoing coordination of pool house security system and sewer line for new planned rec center.**
- **Construction, demo, and site work began May 16, 2024. Expected project completion in early June 2025.**

5. TULSA ZOO CARNIVORES (147150)

- 5701 East 36th Street North. – District 1
- 2014 Sales Tax and Private Funding
- Budget: \$8,000,000 (2014) + \$20,920,000 (Private) = \$28,920,000 funding secured to date
- Current Cost Estimate = \$37,000,000
- Consultant: WDM (contract is with TZMI)
- **Cost control activities continue to reduce overall costs of the project – reduced length and width of Boardwalk; removal of train depot complex; changed viewing building from round to square.**
- **TZMI is raising the final \$4.8 million required to totally fund this project.**
- **100% Plans received from WDM on 09.03.24. City Design Studio comments returned.**
- **Prebid Walkthroughs held 10.30.24 & 10.31.24.**
- **Bid Package #1 to include demo, tile and flooring, building specialties, roller patio shades, and earthwork and site utilities. Package 1 advertised 11.21.24.**
- **Prebid Meeting was held 02.07.25, bids reopened 02.25.25, Nabholz selected as Construction Manager at Risk.**

6. TZMI ZOO AND LIVING MUSUEM ELEPHANT ENCOUTNER

- 6421 E 36th St N – District 1
- Bid Package 1, Earthwork, PKG 2 and PKG 3 have been awarded
- Construction ongoing
- City appropriation increased to full Vision provided \$25,000,000.00 per TZMI request.
- TZMI providing balance through their fundraising
- Amendment No. 2 approved by mayor on 01.04.2023 to increase IMGP to \$31,033.91 for Nabholz Construction
- Amendment No. 3 with Nabholz executed 01.24.24
- 404 Permit (approval for use of fill material in flood plain) issued 09.10.24
- **Project completion expected March 2025 due to cage work and artificial rock vendor delays.**
- **Ribbon Cutting held 04.07.25**
- **Awaiting As-Built drawings to begin final pay application and project close out.**

7. FRED JOHNSON PARK IMPROVEMENTS (SP21-6)

- 6002 South Riverside Drive – District 7
- IOT2 Sales Tax (2244P00012) + IOT3
- Total Budget: \$3,125,000 (IOT2) + \$5,000,000 (IOT3) = \$8,125,000
- Master Plan Fees: \$39,950
- Master Plan Consultant: Greenplay / Berry Dunn Consultants
- Design Consultant: Landplan Consultants
- Design Fee: \$800,207.23
- A Design Contract was approved by PCSSC on December 12, 2023, and approved on the Mayor's signing Agenda.

STOC Report

04/10/25

- Design kick-off meeting was held March 5, 2024. Design meetings to be held every 2 weeks through the preliminary design phase.
- 25% Plans returned to city August 2024, comments returned to Landplan October 2024.
- **65% Plans received 12.09.24, city comments returned 02.04.25.**
- **Landplan proceeding with design. 95% drawings for city review are expected early May.**
- **Advertising for bids is expected summer 2025 with construction beginning in January 2026 and being completed in Fall 2026.**

8. SWAN LAKE FOUNTAIN REHABILITATION (2242P00030)

- 1573 Swan Drive – District 4
- IOT2 Sales Tax (2244P00030)
- Total Budget: \$1,700,000 (IOT2) + \$500,000 (IOT3) = \$2,200,000
- Scope: Rehabilitation of the historic Swan Lake Fountain and improvements to the water quality of the lake.
- Consultant: Alaback Design Associates, Inc.
- Design Fees: \$203,825.55
- Design agreement has been approved – the Design Kick-off meeting was held May 12, 2022.
- A Neighborhood Meeting was held September 20, 2022.
- Final mylar drawings were submitted on October 6, 2023.
- Advertising for bids began November 3, 2023, with bids opening December 8, 2023.
- The bid was awarded to Daris Construction with a cost of \$1,871,542.350 for the Base Bid and Alternate #1 (aeration system).
- Pre-Construction Conference was held February 6, 2024.
- A Public Neighborhood Meeting was held February 20, 2024.
- Construction began March 25, 2024.
- Cofferdams are installed. The draining of the construction site completed.
- Fountain demolished end of May 2024.
- Fountain stone selected 05.14.24
- Foundation work underway July 1st, 2024.
- Concrete Plinth and “Donut” poured, currently installing plumbing work.
- Architectural stone being placed on foundation. GPSI on site for fountain plumbing work.
- PSO on site for power connection.
- Ribbon cutting with Mayor held 11.20.24
- Cofferdam removed; electrical work completed. Fountain maintenance training session held 01.08.25
- **Final Walk held 01.30.25, Daris has completed punch list items. Awaiting final close out documents.**
- **Parks working with Aaron fence to use remaining funds to replace chain link fencing with faux wrought iron fence. Fence delivery expected Mid-April with installation complete by late May.**

9. ZINK PARK EROSION AND SITE REPAIRS

- 3216 S Trenton Ave.- District 4
- IOT2 Sales Tax (2244B00009)
- Total Budget: \$151,800
- Consultant: Wallace Engineering
- Design Fees: \$10,500.00
- Scope: repair damaged stone stairs at NE corner of tennis courts and remediate ground water in lower park.
- Final Design drawings received October 27, 2023
- **Earthsmart Construction (contract through Stormwater) is providing all improvements on this project at a cost of \$118,000.**
- **60% plans for lower park expected July 2024, stormwater overseeing design.**
- **Upper elevation erosion was started by April 1, 2024, and was completed October 1, 2024. Tennis courts reopened.**

10. TENNIS COURT REHABILITATION

- Parks System Wide – All Districts

STOC Report

04/10/25

- IOT2 Sales Tax (2244P00011)
 - Budget: \$1,200,000
 - Project is to repair and resurface tennis and sports courts, provide new nets, screens, fencing, and new sports striping.
 - Specifications have been prepared and submitted to Purchasing for Bidding.
 - Purchasing Bid opened April 13, 2023. 4 bids were submitted.
 - Staff has selected 2 contractors who submitted the lowest responsible bids.
 - Total Estimated Improvement Costs: \$1,110,483.00 / Construction cost: \$945,774.00
 - Purchase Orders have been approved and contracts have been finalized.
 - A pre-construction meeting was held with John Henzel to discuss and schedule work on the first 5 courts (Skelly Park, Rose Dew Park, Starks Park, Terwilliger Park, and Challenger 7 Park)
 - 2nd pre-construction meeting was held with CBE Construction for 14 courts (Cowan, Carbondale, Norberg, Hicks, Explorer, McClure, Ute, Langenheim, Lacy, Manion, Whiteside, Heller, Tracy, West Highlands, and Lakeview Parks).
 - Construction on the first 5 courts with Henzel began April 2, 2024.
 - Construction on the CBE courts began June 1, 2024.
 - Completed Courts: Terwilliger, Rose Dew, Starks-Cheyenne, Manion, Heller, Tracy, McClure, Carbondale, Norberg, Hicks, Whiteside, Skelly, Explorer, Langenheim, Skelly
 - **Courts to resume construction April 2025: Ute, Cowan, Lacy, West Highland, and Lakeview.**
 - **2025 court RFP sent out 04.09.25, Awaiting bids, work expected to start Late May. List of 2025 courts to be refinished is included below.**
 - **2026 court plans are draft plans and may be subject to change.**
11. REED PARK CENTER ROOF REPLACEMENT (SP23-6)
- 4333 S. Yukon Ave. – District 2
 - IOT2 – Parks Facilities (2242B00009) for Design Fees
 - IOT3 – Parks Roofing Improvements for Construction
 - Consultant: GH2 Architects
 - Fees: \$41,439.68
 - Consultant submitted 25% review drawings on January 30, 2024.
 - 95% drawings were submitted on April 5, 2024
 - **100% plans received from GH2 11.04.24, city returned corrections 12.16.24.**
 - **Corrections from GH2 returned 01.06.25, reviewed with GH2 03.07.25. GH2 making additional updates.**
12. CARL SMITH PARK SEWER LAGOON EXPANSION AND REPAIR (SP23-4)
- 17120 E. 21st Street – District 6
 - IOT2 Sales Tax – Park Facilities
 - Budget: \$650,000
 - Consultant: E&E Engineering & Associates, LLC
 - Expansion of the existing sanitary sewer lagoon system to meet current needs and codes.
 - Consultant has submitted the draft report which has been reviewed by City staff.
 - **Water and Sewer Department has taken over the management of this project due to their expertise.**
13. REED PARK REC. CENTER IMPROVEMENTS (2244B00009)
- 4333 S. Yukon Ave. – District 2
 - IOT2 – Parks Facilities (2242B00009)
 - Scope: Paint exterior walls of Center
 - Contractor: Bacco Construction (Purchase Order)
 - Budget: \$81,696 – proposal is being prepared by contractor.
 - **Interior painting completed September 30th, 2024**
 - **Exterior painting started 01.30.25.**
14. PARKS HVAC REPLACEMENT @ GARDEN CENTER (CP 24-15)

STOC Report

04/10/25

- 2324 S. Rockford Ave. – District 4
 - IOT2 Parks Facility – 2244B00009
 - Budget: \$475,893.00 (IOT2 facilities)
 - Design: N/A
 - Purchase Order with Logic Heat & Air is processing.
 - Purchase Order cost = \$174,180.
 - **Work with Logic was completed 09.15.24, awaiting final close out.**
15. PARKS HVAC REPLACEMENT MULTIPLE SITES (CP 24-16)
- IOT2 Parks Facility – 2244B00009
 - Budget: \$1,702,843.00 (IOT2 facilities)
 - Design: N/A
 - Purchase Order is being processed for HVAC equipment to be provided for Woodward Gift Shop, 1710 Charles Page (upstairs), Garnett Station, Woodward Linneaus.
 - Purchase Order cost = \$19,065.29
 - **Completed: Woodward Gift Shop, Woodward Barn, Garnett Station, Oxley Nature Center, Mohawk Station, 1712 Charles Page, Reed, 1710 Charles Page (Waterworks), Dawson, Mohawk Golf (First Tee), Lacy, Centennial Center**
 - **In Progress: Reed, in coordination with Roof Replacement (See Item 11)**
 - **Chamberlain not started, to be completed with larger rec center work (See Item 29)**
16. HILL PARK IMPROVEMENTS (CP-9)
- 210 E. Latimer Pl. – District 1
 - IOT2 Project Funding: \$2,750,000 (\$500K FY25 + \$2.250K FY26) IOT2
 - Design: Consultant Selection after scope of work is identified through Neighborhood Meetings.
 - Design Fees: TBD
 - **Public meeting held October 14th at Ben Hill Community Center. Additional community input session held at Rudisill Library 02.03.25.**
 - **Design RFP approved by PCSSC and sent to consultants 02.21.25, proposals to be returned 04.18.25.**
17. MOHAWK PARK REHAB AND RENOVATION (CP-10)
- 5701 E 36th Street North – District 1
 - IOT2 Project funding: \$1,000,000 (\$100K FY25 + \$900K FY26)
 - Parks staff is having meetings w staff and user groups to determine scope of project.
 - Design: Consultant Selection pending
 - Design Fees: TBD
18. CW – PARK SYSTEM PARKING REHAB (CP-11)
- IOT2 Project Funding: \$1,000,000 (\$525K FY25 + \$475K FY26)
 - Design: TBD
 - Parks staff prioritizing parking lots that need repairs.
 - **Parking funding allocated to Dream Keepers grant match. See Item 31.**
19. HUNTER RENOVATION & EXPAND (147170 – CP24-17)
- 5804 E. 91st - District 9
 - IOT Project Budget: \$400,000
 - Design – N/A
 - **Scope: Interior improvements made in coordination with ADA Hunter improvements.**
 - **Anticipate improvements to be made through Purchase Orders.**
 - **Plans in review by Parks staff, compiled comments returned to McIntosh 02.20.25.**
 - **Awaiting trail design updates from McIntosh.**
 - **Restroom modifications underway under existing BEN construction contract.**
20. PARKS ADA IMPROVEMENTS @ HUNTER PARK (145200)

STOC Report

04/10/25

- 5804 E. 91st – District 9
- IOT funding: \$163,702.76 (balance) + \$1,000,000 FY25 + \$1,000,000 FY26
- Design: McIntosh Group, LLC
- Design Fees: \$43,660.00
- Construction Estimate: \$511,980.00 (05.28.2023)
- 65% Drawings submitted and reviewed by staff. Staff reviewing southern trail for interference with existing trees' critical root zones. Reviewing with Geoff Braga and engineering staff for tree issues before proceeding with construction.
- Plans in review by Parks staff, will return to McIntosh following Accessibility Advisory Committee Meeting held 02.14.25.
- **Compiled comments returned to McIntosh 02.20.25.**
- **Awaiting trail design updates from McIntosh.**

21. CW – OUTDOOR PARK PLAY AMENITIES(CP-24-18)

- Parks System Wide – All Districts
- IOT2 Total Budget: \$5,500,000
- Appropriated: \$500K + \$1,200K = \$1,700,000 available
- Additional Funding: \$1,900K FY25 + \$1,900K FY26
- Breakdown of projects reviewed and approved by City Council.
- **Public press release July 1, 2024.**
- **Survey signs placed Sept 9th – Oct 15th to collect survey responses to inform playground designs and equipment.**
- **Gametime providing designs for Newblock, Rose Dew, Lakeview and Zeigler Parks. Newblock and Lakeview completed, Rose Dew underway as of 3.24.25**
- **Crouch Rec. providing designs for Shannon II, Riggs, Highland Parks (10.29.24)**
- **See attached sheet for full list of playgrounds to be improved.**

22. TZMI ENTRANCE AND PARKING IMPROVEMENTS

- 5701 East 36th Street North. – District 1
- IOT2 Funding: \$6,000,000 (\$600,000 FY25 + \$5,400,000 FY26)
- Design: TBD
- Design Fees: TBD

23. TZMI RAINFOREST HVAC REHABILITATION (2444B0010z)

- 5701 East 36th Street North. – District 1
- IOT3 Funding: - \$8,550,000 (\$8,000,000 available + \$550,000 in future)
- Design: EDA – FKI Engineers (Cy Nowkhah)
- Design Fees: private (TZMI)
- Design is 35% complete.
- Aeon is donating HVAC units
- Received the bid proposal, plans and specifications from Cy 10.15.24.
- City comments returned to Cy 10.31.24
- **Cy returned plans and specifications 12.13.24 for city review. City returned mark ups 01.03.25.**
- **City reviews sent back for corrections 03.31.25, Received consultant's updates 04.04.25.**
- **Bidding expected Late-April.**

24. TZMI ROOFING REPLACEMENT (2444B0009z)

- 5701 East 36th Street North. – District 1
- IOT3 Funding: \$1,800,000 (April 2024) + \$3,600,000 (future funding)
- Design: TBD
- Design Fees: TBD

STOC Report

04/10/25

- 3 roofs of the existing NALM (North American Living Museum) buildings are to be replaced. City staff have inspected the roofs and are preparing for selection of design consultant to provide design documents.
- **GH2 Fee proposal received 10.30.24, over budget.**
- **Revised fee proposal received 12.09.24, in review by city staff.**

25. CW – PARKING LOT REHABILITATION – HICKS PARK

- 3443 S. Mingo Rd. – District 5
- IOT3 Funding: \$800,000 (April 2024)
- **Design: GH2 Architects**
- **Fee proposal received 11.08.24, scope of services needs to be reduced.**
- **GH2 provided updated cost proposal 12.19.24.**
- **GH2 to move forward with design of parking lot at a cost of \$40,600**
- **Design Fees: \$40,600**
- **GH2 currently in design of parking lot, survey completed, designs to be returned week of 04.14.25.**

26. CW – ROOFING REPAIRS

- IOT3 Funding: \$1,625,000 (future bond sales)
- Design: TBD
- Design Fees: TBD
- Priorities are being identified.

27. CW – MECHANICAL EQUIPMENT

- IOT3 Funding: \$300,000 (future bond sales)
- Design: TBD
- Design Fees: TBD
- Priorities are being identified.

28. MOHAWK GOLF RENOVATIONS

- 5228 E. 41ST Street North – District 1
- IOT3 Funding; \$4,000,000 (April 2024)
- Design; TBD
- Design Fees: TBD

29. CHAMBERLAIN PARK IMPROVEMENTS

- 4940 North Frankfort Ave. – District 1
- IOT3 Funding; \$5,000,000 (April 2024) + **GKFF Contribution approx. \$22M (Final Total GKFF contribution to be determined following construction cost estimates from consultants)**
- Design by Studio Zewde Architects; privately funded through GKFF
- Construction funding to supplement privately funded project currently under design.
- Park Design to include a new building for the JAMC rec center with a new parking lot, new covered basketball court, new playground, new garden area, picnic shelters, walking trails, lighting and landscaping added throughout the park.
- **75% Plans received August 9, 2024, Parks has reviewed and returned comments as of 11.08.24, design ongoing to address parks comments.**

30. BERRY PARK IMPROVEMENTS

- 5002 N Wheeling Ave. – District 1
- **Budget; TBD (Total GKFF contribution to be determined following construction cost estimates from consultants)**
- Design by Studio Zewde Architects; privately funded through GKFF

STOC Report










04/10/25

- Construction funding to supplement privately funded project currently under design.
- Park design to include a new covered basketball court, playground, splash pad, picnic shelters, expanded parking lot, and a new walking loop, lighting and landscaping throughout the park.
- **75% Plans received August 9, 2024, Parks has reviewed and returned comments as of 10.31.24, design ongoing to address parks comments.**










31. DREAM KEEPERS PARK IMPROVEMENTS


















- 1875 S Boulder Park Dr. – District 4
- Combination of IOT2 Funding, District 4 Improvement Funds, Private contributions, and Outdoor Recreation Legacy Partnership Grant match for a total of \$7,224,000.00.
- Design: TBD
- Design Funds: TBD
- Project to begin construction January 2026, with completion required by December 2027.
- **Design RFP sent out 01.21.25, Proposals Returned 03.13.25, City reviewing scores for second round of firm interviews, to be scheduled week of 05.05.25.**
- **State and National Parks Service conducting State Historic Preservation Office review of the site.**

FY 2024

Park	Address	Court	Action	Current Configuration	Proposed Configuration
Cowan	10901 E. 19th St.	Tennis Court	Refinish		Configuration Unchanged
		Tennis Court	Refinish		
Lacy	2134 N. Madison Pl.	Tennis Court	Refinish		Configuration Unchanged
		Tennis Court	Refinish		
		Tennis Court	Refinish		
		Tennis Court	Refinish		
Lakeview	3829 N. Columbia Ave.				Configuration Unchanged
Ute	1900 N. Pittsburg Ave.	Basketball Court	Maintain		
		Bball Half Court	Convert to single full court		
		Bball Half Court	Convert to single full court		
West Highland	2626 W. 61st St.	Bball Half Court	Chinlone Court https://sportsmatik.com/sports/sepak-takraw/about	 	  (Enlarged Chinlone detail in link)
		Tennis Court	Maintain, add pickleball overlay		
		Tennis Court	Convert to Full Basketball		

FY 2025

Park	Address	Court	Action	Current Configuration	Proposed Configuration
Aaronson	4807 S. 87th E. Ave.	Tennis Court	Refinish, Repair Fence		
		Tennis Court	Refinish, Repair Fence		
		Bball Half Court	Convert to Single Full Court		
		Bball Half Court			
Admiral	29 N. Victor Ave.	Bball Half Court	Refinish		Configuration Unchanged
		Bball Half Court	Refinish		
		Basketball Court	Refinish		
Braden	5036 E. 7th St.	Tennis Court	Refinish		
		Tennis Court	Convert to 2 Pickleball		
Chittom Clinton	3121 E. Queen Pl.	Basketball Court	Maintain		Configuration Unchanged
		Tennis Court	Maintain		
Clark	11440 E. Admiral Pl.	Basketball Court	Refinish		Configuration Unchanged
Clark	11440 E. Admiral Pl.	Basketball Court	Refinish		Configuration Unchanged
Crutchfield	1345 E. Independence				Configuration Unchanged
		Bball Half Court	Maintain		

Darlington	5179 E. 29th St.	Bball Half Court	New Full Bball		Configuration Unchanged
		Tennis Court	Maintain		
		Tennis Court	Maintain		
Graham	6410 S. Yorktown Ave.	Tennis Court	Maintain		TBD
		Tennis Court	Maintain		
		Tennis Court	Maintain		
		Tennis Court	Maintain		
		Tennis Court	Maintain		
HB Johnson	1714 S. 123rd E. Ave.	Tennis Court	Refinish		
		Tennis Court	Refinish		
Henthorne	4825 S. Quaker Ave.	Basketball Court	Refinish		Configuration Unchanged, Repour Required
		Tennis Court	Refinish		
		Tennis Court	Refinish		
		Tennis Court	Refinish		
Highland	4909 E. 36th St.	Tennis Court	Refinish		TBD
		Tennis Court	Convert to Bike Traffic Garden		
Holiday Hills	4111 E. 54th St.	Pickleball	Maintain		Configuration Unchanged
		Pickleball	Maintain		
		Pickleball	Maintain		
		Pickleball	Maintain		
		Tennis Court	Maintain		
Kendall-Whittier	2645 E. 5th St.	Basketball Court	Maintain		Configuration Unchanged
		Basketball Court	Maintain		
		Soccer Court (Overlay)	Maintain		
Lloyd	2121 E. 29th St. North	Tennis Court	Refinish		
		Bball Half Court			
		Bball Half Court	Convert to single full court		
Loving	9162 E. Latimer St.	Basketball Court	Refinish		Configuration Unchanged
		Tennis Court	Refinish		
Maxwell	5251 E. Newton St.	Basketball Court	Maintain		Configuration Unchanged
		Basketball Court	Maintain		
		Basketball Court	Maintain		
Norvell	722 N. 77th E. Ave.	Tennis Court	Refinish		
		Bball Half Court			
		Bball Half Court	Convert to single full court		
Penney	531 S. 49th W. Ave.				Configuration Unchanged
		Bball Half Court	New Full Bball		
Reed	4233 S. Yukon Ave.	Tennis Court	Maintain		Configuration Unchanged
		Basketball Court	Maintain		
Schlegel	3825 W. 53rd Pl.				Configuration Unchanged
		Basketball Court	Maintain		
Zink	3216 S. Trenton	Tennis Court	Refinish		Configuration Unchanged
		Tennis Court	Refinish		
		Tennis Court	Refinish		
		Tennis Court	Refinish		

Playground Improvement Schedule

Playgrounds

Park Location	Condition	Fun	Parts	Observations	Action	Budget	Additional Notes	
Terrace	2	2	N	Lights	Full Replacement	200,000	Funded w IOT1	
Shannon I & II	1	2	N	Fence needed	Full Replacement	150,000	Funded w IOT1	
Aaronson	2	3	N		Full Replacement	150,000	Funded w IOT1	
Boots Adams	3	3	N		Full Replacement	150,000	Funded w IOT1	
Graham	2	3	N		Full Replacement	150,000	Funded w IOT1	
Henthorne	3	2	N		Full Replacement	150,000	Funded w IOT1	
Skelly	2	3	N		Full Replacement	150,000	Funded w IOT1	
Tracy	1	3	N		Full Replacement	150,000	Funded w IOT1	
Summerglen	2	3	N		Full Replacement	150,000	Funded w IOT1, Coordinate w Union schools	
Loving	2	3	N		Full Replacement	150,000		
Newblock	2	1	N		Full Replacement	150,000		
Hicks	2	3	N		Full Replacement	250,000		
Hill	2	3	N		Full Replacement	200,000	Part of planned park rennovation, IOT2	
Riggs	1	3	N		Full Replacement	150,000		
Dawson*	1	2	N	Playground Fence needed	Full Replacement	150,000		
Turner	2	2	N		Full Replacement	150,000		
Lantz	2	1	N		Full Replacement	150,000		
Norberg	2	1	N		Full Replacement	150,000		
Terwilliger	2	3	N		Full Replacement	150,000		
Benton	1	1	N		Full Replacement	150,000		
Boeing	3	3	N		Full Replacement	150,000		
Challenger 7	1	3	N		Full Replacement	150,000		
Manion	2	2	N		Full Replacement	150,000		
Rose Dew	1	3	N		Full Replacement	150,000		
Fred Johnson	1	3	N		Full Replacement	150,000	Funded w larger park renovation	
Zeigler				Destroyed in fire	Full Replacement	300,000	Funded w CDBG Grant	
Berry	2	1	N		Full Replacement	250,000	Part of larger park rehab, Partnered w GKFF	
Dream Keepers	3	2	N		Full Replacement	250,000	Coordinate w Indian Affairs Comm.	
Chamberlain	2	3	N		Full Replacement	242,000	Ascension Grant, Partner w GKFF	
Bales				No Existing Playground	New Playground	250,000	Coordinate w Bike Club	
Lakeview				No Existing Playground	New Playground	150,000		
Admiral	4	3	Y		Partial Enhancement	60,000		
Braden 5-12	4	2	Y		Partial Enhancement	60,000		
Clark	4	2	Y		Partial Enhancement	60,000		
Cowan	3	3	N		Partial Enhancement	60,000		
Crutchfield	3	2	Y		Partial Enhancement	60,000		
East Park Tract	4	2	Y	Needs safety fence	Partial Enhancement	60,000		
HB Johnson	1		N	Swings Only	Partial Enhancement	60,000		
Heller	4	2	N		Partial Enhancement	60,000		
Helmerich				Removed, Fire	Partial Enhancement	80,000		
Highland	4	3	Y		Partial Enhancement	60,000		
Howard	4	2	Y		Partial Enhancement	60,000	Potential Route 66 grant	
Kendall Whittier 2-5	4	3	Y		Partial Enhancement	60,000		
Kendall Whittier 5-12	4	2	Y		Partial Enhancement	60,000		
Kendall Whittier Natural	4	2	Y		Partial Enhancement	60,000		
Leake	4	2	Y		Partial Enhancement	60,000		
Lloyd	3	2	Y		Partial Enhancement	60,000		
Norvell	3	1	Y		Partial Enhancement	60,000		
Pielsticker 2-5	3	3	Y		Partial Enhancement	85,000		
Pratt	2	1	Y	Swings Only	Partial Enhancement	60,000		
Starks-Cheyenne 5-12	4	2	Y		Partial Enhancement	60,000		
Swan Lake	4	1	Y	Swings Only	Partial Enhancement	60,000		
Williams	4	2	Y		Partial Enhancement	60,000		
Woodward	3	1	Y	Swings Only	Partial Enhancement	60,000		
Admiral 5-12	2	2	N		Good Condition		If there is a need, future repairs and improvements may be made to these "Good Condition" playgrounds using the Equipment Repair & Enhancement line item below.	
Archer	3	5	Y		Good Condition			
BC Franklin	4	2	Y		Good Condition			
BC Franklin 5-12	4	5	Y		Good Condition			
Benedict				Hilcrest	Good Condition			
Braden	4	3	Y		Good Condition			
Bullette	2	3	N		Good Condition			
Carbondale	5	5	Y		Good Condition			
Carl Smith	3	2	N		Good Condition			
Celebration (West Tulsa)	5	5	Y		Good Condition			
Crawford	5	4	Y		Good Condition			
Crawford 5-12	5	4	Y		Good Condition			
Crawford 5-12b	5	2	Y		Good Condition			
Darlington 5-12	4	3	Y		Good Condition			
Florence	4	4	Y		Good Condition			
Forest Orchard	5	2	Y		Good Condition			
Gary	1	2	N		Good Condition			
Helmerich 5-12	5	5			Good Condition			
Hunter	3	3	Y		Good Condition			
Lacy	5	4	Y		Good Condition			
Langenheim 5-12	5	4	Y		Good Condition			
Langenheim 2-5	5	3	Y		Good Condition			
Maple	3	3	N		Good Condition			
Maxwell	3	3	Y		Good Condition			
Maxwell 5-12	3	3	Y		Good Condition			
McClure	5	4	Y		Good Condition			
McClure	5	4	Y		Good Condition			
McCullough	5	5	Y		Good Condition			
Minshall	3	3	N		Good Condition			
Mohawk	3	1	Y	Climbing Rock, Swings	Good Condition			
Mohawk Soccer 1	4	2	Y		Good Condition			
Mohawk Soccer 2	3	1	Y		Good Condition			
Mohawk Soccer 3	4	2	Y		Good Condition			
Owen	4	3	Y		Good Condition			
Patrick	5	3	Y		Good Condition			
Patrick 5-12	5	3	Y		Good Condition			
Penney 2-5	5	4	Y		Good Condition			
Penney 5-12	5	4	Y		Good Condition			

Philpott	4	2	Y		Good Condition		
Pielsticker 5-12	3	4	Y		Good Condition		
Plaza 2-5	5	3	Y		Good Condition		
Plaza 5-12	5	4	Y		Good Condition		
Reed	4	4	Y		Good Condition		
Savage	3	2	N		Good Condition		
Schlegel	5	5	Y		Good Condition		
Sequoyah	2	3	N		Good Condition		
Springdale	4	3	Y		Good Condition		
Springdale 5-12	4	4	Y		Good Condition		
Starks-Cheyenne 2-5	4	2	Y		Good Condition		
Vining	3	3	Y		Good Condition		
West Highland	5	5	Y		Good Condition		
Wheeling	1	2	N		Good Condition		
Whiteside Hope	5	5	Y	Accessible Playground	Good Condition		
Whiteside 5-12	4	2	Y		Good Condition		
Zink	4	3	N		Good Condition		

Yellow indicates alternate funding source (Not IOT funds)

Adult Exercise

Various Locations, TBD				Neighborhood Assessments needed to determine where improved adult exercise is needed		750,000	
Boots Adams							
Riggs							
Helmrich							
Manion							
Hunter							
BC Franklin							
Whiteside							

Water Play to Repair/Replace

Pielsticker (Mohawk)						250,000	Needs Sanitary Sewer Line
Hunter						250,000	Needs Sanitary Sewer Line
Helmrich						150,000	
Dawson						150,000	
Berry							Part of larger park rehab, partner w GKFF

Accessibility enhancements

				Ramps, Paths, Gradework, Accessible Play Features. Any additional remaining funds may also be added to this pool.			
Multiple Locations						\$ 500,000	

Equipment Repair & Enhancement

				Future replacement parts and repair costs, as they become needed, as well as future modifications including painting, new play features, interperative signage or art, and other minor improvements to keep playgrounds safe, fun, and interesting. Any additional remaining funds may also be added to this pool.			
Multiple Locations						\$ 750,000	

Total Improvement Costs	\$ 9,617,000	Incl. Zeigler, Chamberlain, Fred Johnson
Alternative Funding Sources	<u>\$ 692,000</u> -	
Remaining Cost	\$ 8,925,000	
10% Contengency	<u>\$ 892,500</u> +	
Total Remaining Costs	\$ 9,817,500	
IOT1 Total amount	\$ 4,319,795	
IOT2 Total amount	<u>\$ 5,500,000</u> +	
Total Available Funds	\$ 9,819,795	

FRED JOHNSON PARK 65%



(5)Sewer, Stormwater, and Transportation

Attendees:

Kathy Sebert
Scott Grizzle
Linda Jenkins
Steve King
Deborah McKinney
Maia Treleaven
Ashely Webb

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
FUND 405 - SALES TAX FUND (2014)											
144017	Arterial Street Rehab										
a	Charles Page Blvd. - 33rd W. Ave. to 25th W. Ave.	Jun-15	Sep-17	Garver	\$206	90%	Apr-24	Sep-24	Tri-Star	\$1,747	99%
b	49th W. Ave. - Edison St. to Charles Page Blvd.	May-18	Apr-19	CEC	\$165	85%	TBD		Tri-Star	\$776	
c	Utica Ave. - Pine St. to Admiral Blvd.	Nov-15	Apr-16	CEC	\$528	85%	TBD		Becco	\$3,400	
d	Lewis Ave. - 36th St. N. to Apache St.	Jun-18	Dec-18	Cyntergy	\$118	95%	Sep-24	Mar-25	Tri-Star	\$1,411	49%
g	Union Ave. - Southwest Blvd. to W. 41st St.	May-15	Sep-17	COT	\$158	90%					
j	Pine St. - Harvard Ave. to Yale Ave.	May-18	Apr-19	Benham	\$289	94%	TBD		Tri-Star	\$1,922	
k	Admiral Pl. - Lewis Ave. to Harvard Ave.	Jan-18	Aug-18	BKL	\$253	95%	TBD		Becco-Se AW		
l	Admiral Pl. - Harvard Ave. to Yale Ave.	Nov-16	Jul-17	Poe	\$325	95%	Feb-21	May-22	Ellsworth	\$4,177	100%
m	Sheridan Rd. - Apache St. to Pine St.	Nov-15	Sep-17	Garver	\$156	90%					
s	15th St. - Lewis Ave. to Harvard Ave.	Jan-17	Oct-17	Garver	\$302	90%	TBD		Becco	\$3,420	
t	Peoria Ave. - Admiral Blvd. to 11th St.	May-18	Feb-19	MARQUARDT	\$214	90%					
u	Peoria Ave. - 11th St. to 21st St.	Feb-16	Nov-16	MARQUARDT	\$252	85%					
v	Utica Ave. - Admiral Blvd. to 11th St.	Nov-19	Aug-20	C&K	\$317	96%					
w	Utica Ave. - 11th St. to 15th St.	Dec-16	Jul-17	BKL	\$224	90%					
x	Harvard Ave. - 15th St. to 21st St.	Sep-19	Jul-20	Garver	\$245	90%					
y	Harvard Ave. - 21st St. to 31st St.	Apr-18	Apr-19	Poe	\$469	98%	Apr-25				
z	21st St. - Yale Ave. to Sheridan Rd.	May-18	Mar-19	CEC	\$259	98%	Jan-25	Nov-25	Becco	\$2,437	13%
aa	31st St. - Yale Ave. to Sheridan Rd.	Aug-19	May-20	Garver	\$237	80%					
ac	41st St. - Sheridan Rd. to Memorial Dr.	Apr-18	Jan-19	CGA	\$262	90%					
ae	51st St. - Mingo Rd. to Garnett Rd.	Apr-18	Jun-19	Garver	\$234	90%	Feb-25	Dec-25	Becco	\$3,257	19%
aj	Sheridan Rd. - 91st St. to 101st St.	Apr-18	Jun-19	HUB	\$84	95%	Oct-24	Jul-25	Tr-Star	\$1,200	93%
al	Harvard Ave. - 41st St. to 51st St.	Apr-18	Dec-18	PEC	\$236	90%	Nov-24	Sep-25	Gradeline	\$1,600	41%
ao	Downtown Arterial Streets	May-15	Aug-15	Poe	\$923	70%					
	Phase 1 - 1st Street		Apr-16	Poe		95%	Aug-17	Jan-18	Crossland	\$1,493	100%
	Phase 2 - 5th Street		Aug-16	Poe		95%	Nov-17	Jul-18	Tri-Star	\$1,735	100%
	Phase 4 - Boulder/1ST to 10th		May-17	Poe		95%	Jan-19	Apr-20	Becco	\$4,415	100%
ao	Phase 6A - Detroit / 8th Street		Aug-17	Poe		95%	Oct-22	Aug-23	Crossland Heavy	\$4,146	100%
ao	Phase 6B - 7th Street			Poe		95%	Jun-25				
ao	Phase 7 - Cheyenne		Jan-18	Poe		95%					
ap	Pine St. & MLK Jr. Blvd Intersection	May-08	Feb-19	CP&Y	\$117	98%					
aq	Pine St. & Peoria Ave. Intersection	Jun-17	Jun-18	Schemmer	\$135	80%					
as	41st St. & Union Ave. Intersection	May-15	Sep-19	COT	\$158	99%					
aw	Admiral Blvd. & Lewis Ave. Intersection	Dec-17	Aug-18	BKL	\$250	95%	TBD		Becco	\$2,147	

CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
ax	11th St. & Utica Ave. Intersection	Dec-16	Jul-17	BKL	\$224	90%					
ay	21st St. & Peoria Ave. Intersection			MARQUARDT		85%					
ba	51st St. & Mingo Rd. Intersection	Apr-18	Mar-19	Garver	\$234	95%	Feb-25	Dec-25	Becco--See AE		19%
bb	71st St. & Sheridan Rd. Intersection	Mar-17	Nov-17	Cytergy	\$99	95%			ODOT-STP		
144020	Citywide Non-Arterial Routine and Preventive Maintenance			C&K		100%			Crossland		
144105	Widen 25th W. Ave., Edison to Apache (design)	Apr-21		Poe		95%	Jun-25				
144108	Widen Pine Street, Mingo to U.S. 169 (design)	Jun-23	Apr-24	Garver	\$439	80%					
144120	Gilcrease Expressway Local Match										
144063	Bridges - Replacement and Rehabilitation Programs										
a	Bridge No. 275 - 10100 E. 36th St. N.	Jun-18	Dec-19	K-H		95%	Sep-24	Sep-25	Becco	\$4,097	56%
144094	ODOT Rehabilitation and Replacement Program										
144003	Citywide guardrail replacement (materials & misc repairs)			Misc.	\$119,073	100%					
	Citywide guardrail replacement (Condition Analysis & Inventory)			Kimley Horn	\$350,000	100%					
	Citywide guardrail replacement (Repairs)			Garver	\$127,600	64%			Becco	\$403,328	86%
144004	Citywide traffic signalization (materials & misc repairs)			Misc.	\$537,536	100%					
	Citywide traffic signalization (ATMS & TMC)			Misc.	\$394,942	100%					
	Citywide traffic signalization (On-call timing)			Kimley Horn	\$400,000	100%					
	Citywide traffic signalization (Inventory)			Kimley Horn	\$493,553	100%					
	Citywide traffic signalization (SS4A Match)				\$173,878	100%					
144005	Roadway, pedestrian, and decorative lighting replacement (materials and misc repairs)			Misc.	\$417,044	100%					
	Roadway, pedestrian, and decorative lighting replacement (On-call services)			Garver	\$100,000	82%					
	Roadway, pedestrian, and decorative lighting replacement (repair services)								TLS	\$482,956	100%
144006	Signing, pavement marking and delineation (Materials)				\$1,035,369	100%					
	Signing, pavement marking and delineation (Inventory)			Kimley Horn	\$706,199	100%					
	Signing, pavement marking and delineation (Installation Services)								Direct Traffic Control	\$87,500	98%
	Signing, pavement marking and delineation (Installation Services)								Action Safety	\$137,500	100%
	Signing, pavement marking and delineation (SS4A Grant Match)				\$533,432	100%					

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144007	Traffic calming (Administration)			CEC	\$375,000	100%					
	Traffic calming (Materials and Installation)			Misc.	\$625,000	100%					
144008	Traffic signal installation, modification, and safety improvements (Materials and Repairs)			Misc.	\$1,679,635	100%					
	Traffic signal installation, modification, and safety improvements (School Pager System Replacement)			RTC	\$335,435	100%					
	Traffic signal installation, modification, and safety improvements (61st & 90th E. Ave. Signalization)			Gonzalez	\$25,803	100%			TLS	\$204,803	100%
	Traffic signal installation, modification, and safety improvements (31st & 121st E. Ave. Signalization)			Garver	\$41,098	100%			Gradeline	\$394,762	100%
	Traffic signal installation, modification, and safety improvements (Inventory)			Kimley Horn	\$835,644	100%					
	Traffic signal installation, modification, and safety improvements (SS4A Grant Match)				\$187,987	100%					
144009	Traffic signal pole replacement (Materials and Repairs)			Misc.	\$9,760	100%					
	Traffic signal pole replacement Green Arm Pole Matching Funds)					100%			ODOT Grant Match	\$582,389	
	Traffic signal pole replacement (Lighting Pole Study and Design)			Garver	\$178,360	95%					
	Traffic signal pole replacement (ODOT Project Matching Funds - BA Expwy)					100%			ODOT Grant Match	\$66,056	
	Traffic signal pole replacement (SS4A Grant Match)				\$163,435	100%					
144010	Creek Turnpike Trail pedestrian bridge over Memorial Dr. (\$200,000 for study only)			Garver	\$93,900	100%					
	Creek Turnpike Trail pedestrian bridge over Memorial Dr. (\$200,000 for study only) - REAPPROPRIATED to 144008				\$106,100	100%					
144011	GPS emergency vehicle preemption system (approx. 30 intersections) - BUILD Grant Matching Funds for EVP/TSP system				\$400,000	58%					
144109	Citywide ADA Transition Plan Implementation (Minimum for 30-Year Schedule - High and Medium Priority Needs)	Feb-16	Aug-18	BKL	\$639	90%					
	ADA Transition Plan - Package #3		Mar-23	BKL		95%	Oct-24	Apr-25	Rand L Const.	\$1,495	19%
144093	Citywide Matching Funds										
144018	Bicycle/Pedestrian Master Plan Implementation										

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
COMPLETED Projects for 405											
144017	Arterial Street Rehab										
e	Southwest Blvd. - W. 23rd St. to W. 31st St.	Dec-16	Sep-17	Dewberry/Poe	\$300	100%	Jul-22	Mar-24	Becco	\$7,097	100%
f	Southwest Blvd. - W. 31st St. to W. 40th St.	Dec-16	Sep-17	Dewberry/Poe	\$315	100%	Jul-22	Mar-24			
h	Union Ave. - W. 51st St. to W. 61st St	Jun-15	Aug-17	Garver	\$157	100%	Jan-21	Aug-21	Ellsworth	\$1,598	100%
i	Riverside Dr. - Joe Creek to 81st St.	Jan-17	Oct-17	CGA	\$53	100%	Jul-18	Sep-18	Becco	\$787	100%
n	Mingo Rd. - 46th St. N. to 36th St. N.	Aug-15	Apr-16	McClelland	\$241	100%	Oct-17	May-18	Becco	\$3,743	100%
o	Mingo Rd. - 36th St. N. to Pine St.	Nov-16	Nov-17	McClelland	\$727	100%	Mar-19	Sep-21	Becco	\$8,435	100%
p	Mingo Rd. - Admiral Blvd. to 11th St.	Oct-18	Aug-09	Wallace	\$89	100%	Nov-21	Sep-22	Ellsworth	\$1,187	100%
q	11th St. - 89th E. Ave. to Mingo Rd.	Feb-15	Nov-15	CEC	\$162	100%	Apr-19	Oct-19	Ellsworth	\$1,631	100%
r	15th St. - Peoria Ave. to Lewis Ave.	May-15		Garver	\$248	100%	Sep-19	Nov-20	Crossland	\$3,094	100%
ab	31st St. - Riverside Dr. to Peoria Ave.	Jun-15	Aug-16	Walter P Moore	\$131	100%	Sep-17	Jan-18	Tri-Star	\$1,449	100%
ad	Memorial Dr. - 21st St. to 31st St.	Nov-15	Jun-16	BKL	\$289	100%	Jul-19	Oct-21	Grade Line	\$5,086	100%
af	71st St. - Memorial Dr. to Mingo Rd.			COT		100%	Apr-21	Jun-22	Crossland	\$2,228	100%
ag	91st. St. - Mingo Rd. to Hwy 169.			COT/Poe		100%	May-20	Aug-20	Becco		100%
ah	Memorial Dr. - 81st St. to 91st St.	Sep-17	Mar-18	Marquardt	\$129	100%	Mar-21	Jan-22	Crossland Heavy	\$2,987	100%
ai	Memorial Dr. - 91st St. to Creek Tpk.	Jun-15	Dec-15	Marquardt	\$58	100%	Mar-21	Jan-22	Crossland Heavy		100%
af	71st St. - Memorial Dr. to Mingo Rd.			COT		100%	Apr-21	Jun-22	Crossland	\$2,228	100%
ag	91st. St. - Mingo Rd. to Hwy 169.			COT/Poe		100%	May-20	Aug-20	Becco		100%
ah	Memorial Dr. - 81st St. to 91st St.	Sep-17	Mar-18	Marquardt	\$129	100%	Mar-21	Jan-22	Crossland Heavy	\$2,987	100%
ak	51st St. - Pittsburg Ave. to Yale Ave.	Jan-16	Sep-16	Schemmer	\$74	100%	Dec-18	May-19	Ellsworth	\$926	100%
am	36th. St. N. - Mingo Rd. to Hwy 169	Jun-18	Apr-19	K-H	\$301	100%	Jan-23	Jul-23	TriStar	\$4,739	100%
ao	Downtown Arterial Streets										
	Phase 3 - 6th Street South		Mar-16	Poe		100%	Oct-16	Mar-17			100%
	Phase 5 - 6th Street / 7th Street		Jul-17	Poe		100%	Apr-20	Feb-21	Crossland	\$4,663	100%
ar	Pine St. & Lewis Ave. Intersection	Mar-17	Aug-17	Wallace	\$75	100%	Jan-21	Jun-21	Gradeline	\$1,598	100%
at	51st St. & Union Ave. Intersection			Garver		100%			ODOT		100%
au	46th St. N. & Mingo Rd. Intersection	Aug-15	Apr-16	McClelland	\$241	100%	Oct-17	Oct-18	Becco		100%
av	36th St. N. & Mingo Rd. Intersection	Nov-16	Nov-17	McClelland	\$727	100%	Aug-19	Sep-21	Becco		100%
az	21st St. & Memorial Dr. Intersection	Nov-15	Apr-16	BKL	\$289	100%	Jul-19	Jul-21	Gradeline		100%
bc	61st St. & Sheridan Rd. Intersection	Jun-15	Aug-16	CGA	\$105	100%	Jan-17	Jun-17	Becco	\$5,889	100%
bd	71st St. & Memorial Dr. Intersection			COT		100%	Apr-21	Jan-22	Crossland		100%
be	81st St. & Memorial Dr. Intersection	May-17	Dec-17	Benham		100%	Jun-21	Jan-23	Becco	\$13,875	100%
bf	61st St. & Yale Ave. Intersection	Dec-16	Aug-17	C&K	\$77	100%	Mar-21	Aug-21	Crossland	\$1,747	100%
144101	Widen Yale Avenue, 81st St. to 91st Street South	Jun-15	Jul-17	Benham	\$600	100%	Oct-21	Apr-24	Becco	\$31,153	100%
144102	Widen 81st Street South, Sheridan Road to Memorial Drive	Sep-16	May-18	Benham	\$950	100%	May-21	May-23	Becco	\$13,875	100%
144103	Widen Yale Avenue, 96th St. South to 101st St. South	Aug-16	Jul-17	CEC	\$200	100%	Mar-20	Jan-22	Becco	\$8,752	100%
144104	Widen Riverside Drive, 24th to 33rd Place South	Jun-14	Mar-15	HNTB	\$1,600	100%	Aug-15	Feb-17	Becco	\$14,999	100%

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144063	Bridges - Replacement and Rehabilitation Programs										
b	Bridge No. 185 - 4000 N. Hartford Ave.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
c	Bridge No. 285 - 1900 W. 43rd St.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
d	Bridge No. 232 - 3600 S. Southwest Blvd.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
e	Bridge No. 181 - 300 N. Garnett Rd.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
f	Bridge No. 204A - 200 S. Mingo Rd.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
g	Bridge No. 250 - 11200 E. 11th St.	Jun-15	Dec-15	Cowen	\$39	100%			Becco	\$693	100%
h	Bridge No. 247 - 9200 E. 11th St.	Jun-15	Dec-15	Cowen	\$39	100%			Becco	\$693	100%
i	Bridge No. 239 - 2600 S. Yorktown Ave.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
j	Bridge No. 311 - 3900 S. 90th E. Ave.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
k	Bridge No. 401 - 3800 S. Memorial Dr.	Jun-15	Dec-15	Cowen	\$39	100%	Sep-19	Feb-20	Becco	\$693	100%
l	Bridge No. 310 - 2750 S. 90th E. Ave.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line		100%
m	Bridge No. 254 - 8330 E. 14th St.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line		100%
n	Bridge No. 403 - 4400 S. Memorial Dr.	Jun-15	Jan-16	Cowen	\$39	100%	Sep-19	Feb-20	Becco	\$693	100%
o	Bridge No. 402 - 4200 S. Memorial Dr.	Nov-15	Jun-16	Cowen	\$62	100%	Jul-18	Oct-18	Crossland	\$274	100%
p	Bridge No. 307 - 2900 S. 87th E. Ave.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
q	Bridge No. 266 - 13700 E. 28th St.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
r	Bridge No. 262 - 19200 E. 21st St.	Jun-15	Dec-15	Cowen	\$39	100%	Sep-19	Feb-20	Becco	\$693	100%
s	Bridge No. 333 - 1300 S. 177th E. Ave.	Jun-20	Oct-21	CP&Y		100%	Jan-22	Oct-22	Grade Line	\$503	100%
t	Bridge No. 316 - 3800 S. 93rd E. Ave.		Jun-18	Cowen		100%	Oct-18	Mar-19	Grade Line	\$2,346	100%
u	Bridge No. 209 - 3000 N. Mingo Rd.	Nov-16	Nov-17	K-H	\$727	100%					
v	Bridge No. 352 - 12300 E. State Farm Blvd.	Nov-16	Nov-17	Cowen	\$177	100%	Jul-18	Apr-19	Grade Line	\$2,346	100%
w	Bridge No. 226 - 8200 S. Pittsburg Ave.		Jun-18	Cowen		100%	Jul-18	Apr-19	Grade Line	\$2,346	100%
x	Bridge No. 222 - 3200 S. Peoria Ave.	May-18	Jul-19	Garver	\$227	100%	Nov-21	Jun-22	Tri-Star	\$2,275	100%
y	Bridge No. 166 - 3200 S. Cincinnati Ave.		Jun-18	Cowen	\$177	100%	Jul-18	Apr-19	Grade Line	\$2,346	100%
z	Bridge No. 210 - 5600 S. Harvard Ave.	Jun-15	Dec-15	Cowen	\$39	100%	Sep-19	Feb-20	Becco	\$693	100%
aa	Bridge No. 194 - 5300 S. Louisville Ave.		Jun-18	Cowen		100%	Jul-18	Apr-19	Grade Line	\$2,346	100%
ab	Bridge No. 217 - 5300 S. New Have Ave.		Jun-18	Cowen		100%	Jul-18	Apr-19	Grade Line	\$2,346	100%
144109	Citywide ADA Transition Plan Implementation (Minimum for 30-Year Schedule - High and Medium Priority Needs)										
	ADA Transition Plan - Package #2			BKL		100%			Crossland		100%
	ADA Transition Plan - Package #1		Sep-17	BKL		100%	Mar-20	Nov-20	Daris	\$1,642	100%
144019	IDL Entrance Rehabilitation (1st, 7th, and 8th Streets; signals at 1st and Greenwood)	see ao 144017		Garver	\$1	100%			Crossland		100%
TOTAL FUND 405 INCOMPLETE PROJECTS											
FUNDS 4270-4276 - 2014 STREETS GENERAL OBLIGATION BOND											
	Streets, Expressways, Sidewalks, Traffic Calming										
	Arterial Street Rehabilitation and Citywide Projects:										

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144200	36th St. - N. MLK Jr. Blvd. to Peoria Ave.	Jun-15	Mar-20	PEC	\$232	95%	Sep-21	Feb-24	Ground Level	\$4,895	100%
144202	Apache St. - Peoria Ave. to Lewis Ave.	Aug-16	Mar-17	C&K	\$500	98%	TBD		R&L Construction	\$1,958	
144203	W. 41st St. S. - 41st W. Ave. to S. 33rd W. Ave.	Sep-14	Aug-15	Poe	\$175	95%	Mar-22	Dec-23	Grade Line	\$3,692	100%
144204	S. 33rd W. Ave. - 41st St. to 51st St.	Sep-14	Aug-15		\$275	95%					
144213	91st St. - Harvard Ave. to Yale Ave.		May-24	CEC	\$177	85%					
144309	Citywide - Arterial Rehabilitation										
144110	Citywide - Arterial Sidewalk Improvements										
144020	Citywide - Arterial Routine and Preventive Maintenance										
144093	Citywide Matching Funds										
144094	ODOT Rehabilitation and Replacement Program										
	Non-Arterial Rehabilitaiton and Citywide Projects.										
144111	Maintenance Zone 1001:	May-15	Feb-16	MAR / ARB	271 / 284	95%	Feb-22	Oct-24	Gradeline	\$8,291	100%
144168	Maintenance Zone 1068: N	Sep-16	Sep-17	TEP	152.	95%					
144168	Maintenance Zone 1068: S	Sep-16	Sep-17	Poe		95%	Jun-24	Dec-24	Tri-Star	\$1,149	100%
144153	Maintenance Zone 1153:	Sep-14	Jun-15	POE	\$334+	95%	Jul-23	Apr-24	Crossland Heavy	\$4,784	100%
144310	Maintenance Zone 3010:	May-15	Jan-16	K-H	\$544	90%	Sep-24	Sep-25	Becco	\$4,365	48%
144317-N	Maintenance Zone 3017:	Oct-17	Jul-18	HUB	\$324	80%					
144317-S	Maintenance Zone 3017:	Aug-24	Aug-24	Poe	\$164	80%	May-25				
144320	Maintenance Zone 3020:	Aug-16	May-17	Garner	\$345	80%	TBD		Becco	\$2,157	
144380	Maintenance Zone 3080:	Oct-14	Mar-15	CP&K	\$19	95%		Jan-16	Crossland	\$176	100%
144413	Maintenance Zone 4013:	Sep-14	Apr-15	LEIDOS	\$512	95%		TBD	Becco	\$5,868	
144421	Maintenance Zone 4021:	Jul-16	Apr-17	CEC	\$343	96%	Oct-23	Aug-24	Crossland Heavy	\$2,908	100%
144431	Maintenance Zone 4031:	May-15	Feb-16	GARVER	\$576	95%	Nov-22	Apr-24	Crossland Heavy	\$10,082	100%
144467	Maintenance Zone 4067 phase 2			COT		90%	Nov-24	Nov-25	Gradeline	\$2,289	29%
144452	Maintenance Zone 4152:	Oct-17	Jul-18	HUB	\$373	85%					
144546	Maintenance Zone 5046:	Jun-16	Mar-17	K-H	\$540	95%	TBD		Ellsworth	\$3,703	
144547N	Maintenance Zone 5047: North			GARVER			Mar-24	Dec-25	Becco	\$5,544	100%
144547S	Maintenance Zone 5047: South	Aug-16	Jun-17	GARVER	\$584	90%	Apr-23	Jun-24	RLConstr	\$1,690	100%
144628E	Maintenance Zone 6028: East	Jan-18	Aug-19	K-H	\$428	95%	TBD		Becco	\$2,487	
144628W	Maintenance Zone 6028: West			MESHEK		90%	Feb-23	Mar-25	Becco	\$9,827	95%
144628W	Maintenance Zone 6028: West Phase 2			WSB							
144754	Maintenance Zone 7054:	Sep-17	Feb-19	POE	\$747	80%					
144863B	Maintenance Zone 8063: South	Oct-17	Sep-19	PEC	\$195	95%	Sep-23	Sep-25	R & L	\$4,008	43%
144949	Maintenance Zone 9049:	Sep-17	May-19	GARVER	\$770	90%					
144015	Citywide Non-Arterial Rehabilitation										
144021	Citywide Non-Arterial Routine and Preventive Maintenance										

85

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144016	Citywide Non-Arterial Sidewalk Improvements										
COMPLETED Projects---4270-4276											
144201	Apache St. - MLK Jr. Blvd. to Peoria Ave.	Nov-14	Aug-15	MESHEK	\$267	100%	Mar-19	Nov-19	Crossland	\$3,380	100%
144214	Sheridan Rd. - 81st St. to 91st St.	101/14	Jun-15	POE	\$136	100%	Oct-16	Mar-17	Crossland	\$1,509	100%
144215	Peoria Ave. - 41st St. to 51st St.	Dec-16	Aug-17	MARQUARDT	\$340	100%	Feb-23	Sep-24	Becco	\$3,082	100%
144093	Citywide Matching Funds										
193140000Z	Mingo Creek Trail - 41st to 51			RL Shears		100%	Feb-19	Jul-19	Crossland		100%
144094	ODOT Rehabilitation and Replacement Program										
	Non-Arterial Rehabilitation and Citywide Projects.										
144318	Maintenance Zone 3018:	Oct-14	May-15	SCHEMMER	\$44	100%	Mar-17	Jan-18	Becco	\$484	100%
144467	Maintenance Zone 4067 phase 1	Oct-14	Jun-15	GUY	\$344	100%	Jan-20	Aug-20	Crossland	\$3,127	100%
144627	Maintenance Zone 6027:	Sep-14	Apr-15	PEC	\$83	100%	Nov-16	Mar-17	Ellsworth	\$920	100%
144060	Bridge No.189 - 4700 N. Iroquois Ave.	Nov-14	Jul-15	MEHLBURGER		100%	Mar-19	Oct-19	Crossland		100%
144061	Bridge No. 298 - 2100 E. 61st St.	Oct-14	Apr-15	G&K	\$70	100%	Jul-16	Oct-16	MX Corp	\$637	100%
144062	Bridge No. 323B - 12000 E. 21st	Dec-14		GARVER	\$10	100%	Oct-20	Aug-21	Becco		100%
TOTAL FUNDS 4270-4273 - 2014 Streets General Obligation Bond											
FUNDS 4281-4285 - 2020 STREETS GENERAL OBLIGATION BOND											
'Non-Arterial Street Rehabilitation Projects:											
2036N1007Z	Maintenance Zone 1007:	Dec-20	Aug-21	COT	\$81	98%	Feb-25				
2036N1068Z	Maintenance Zone 1068:										
2036N1070Z	Maintenance Zone 1070:	Feb-21	Oct-21	CGA	\$204	97%					
2036N1071Z	Maintenance Zone 1071:	Apr-24		PEC	\$98	60%					
2036N1072Z	Maintenance Zone 1072:	Apr-24	Sep-24	BKL	161%	80%					
2036N1076Z	Maintenance Zone 1076:		Mar-24	K-H	\$236	90%	Oct-25				
2036N1078Z	Maintenance Zone 1078:	Oct-20	Jun-21	Olsson	\$253	85%					
2036N1097Z	Maintenance Zone 1097:										
2036N1098Z	Maintenance Zone 1098:										
2036N1153Z	Maintenance Zone 1153:	Apr-22	Feb-23	Poe	\$164	95%					
2036N1155Z	Maintenance Zone 1155:	Aug-22	Apr-23	CGA/HUB	\$45	95%	TBD		Tri-Star	\$306	
2036N1157Z	Maintenance Zone 1157:	Sep-24	Jun-24	Poe	-	95%	TBD		Ellsworth (GMR #3)		
2036N2056Z	Maintenance Zone 2056:	Oct-22	Mar-24	TEP	\$180	95%	TBD		Becco	\$925	
2036N2065Z	Maintenance Zone 2065:	Jan-21	Sep-21	Garver	\$218	100%	Feb-24	Jan-25	Crossland	\$3,518	96%
2036N2066Z	Maintenance Zone 2066:	Oct-20	Jul-21	C&K	\$101	95%	Aug-24	Jan-24	Tri-Star	\$1,050	96%
2036N2131Z	Maintenance Zone 2131:										
2036N3004Z	Maintenance Zone 3004:	Dec-23	Mar-24	Marquardt	\$72	95%	TBD		Gradeline	\$1,038	
2036N3005Z	Maintenance Zone 3005:	Jul-25	Jun-25	CEC	\$183	35%					
2036N3008Z	Maintenance Zone 3008:										
2036N3010Z	Maintenance Zone 3010:	Aug-23	Nov-24	K-H	\$145	90%					
2036N3011Z	Maintenance Zone 3011:										
2036N3017Z	Maintenance Zone 3017:	Feb-24	Jul-24	HUB	\$164	90%					
2036N3075Z	Maintenance Zone 3075:	Aug-22	Apr-23	CGA/HUB	\$45	95%	TBD		Tri-Star	\$318	

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036N3080Z	Maintenance Zone 3080:										
2036N3081Z	Maintenance Zone 3081:	Feb-21	Mar-22	EST	\$58	95%	Apr-24	Jun-25	Tri-Star	\$552	69%
2036N3082Z	Maintenance Zone 3082:										
2036N4014Z	Maintenance Zone 4014:	Oct-20	May-21	Poe	\$136	95%					
2036N4015Z	Maintenance Zone 4015:										
2036N4021Z	Maintenance Zone 4021:	Sep-20	Feb-22	CEC	\$256	90%					
2036N4022Z	Maintenance Zone 4022:	Oct-20	Apr-21	BKL	\$322	90%					
2036N4023Z	Maintenance Zone 4023:	Aug-22	Apr-23	CGA/HUB	\$45	95%			Tri-Star	\$326	
2036N4029Z	Maintenance Zone 4029:										
2036N4030Z	Maintenance Zone 4030:	Dec-20	Aug-21	Poe	\$143	95%	Dec-22	Oct-23	R&L	\$1,886	100%
2036N4031Z	Maintenance Zone 4031:										
2036N4067Z	Maintenance Zone 4067:	Dec-23	Jun-24	Benham	\$91	90%					
2036N4069Z	Maintenance Zone 4069:	Aug-22	Jul-23	BKL	\$200	90%					
2036N5016Z	Maintenance Zone 5016:	Jun-22	Apr-23	Garver	\$576	92%					
2036N5026Z	Maintenance Zone 5026:										
2036N5027Z	Maintenance Zone 5027:	Sep-22	Jul-23	Wallace	\$46	95%	Nov-24				
2036N5033Z	Maintenance Zone 5033:										
2036N5039Z	Maintenance Zone 5039:	Jun-23	Dec-23	FNI	\$86	95%	Sep-24	Feb-25	Becco	\$992	96%
2036N5040Z	Maintenance Zone 5040:	Apr-21	Mar-22	TEP	\$81	95%	Apr-24	Jul-24	Crossland	\$1,067	100%
2036N6035Z	Maintenance Zone 6035:			Benham		95%			H&G	\$819	24%
2036N6142Z	Maintenance Zone 6142:	Jul-22	Nov-22	C&K	\$50	95%	Oct-23	Dec-23	Ellsworth	\$543	100%
2036N6144Z	Maintenance Zone 6144:										
2036N6148Z	Maintenance Zone 6148:										
2036N6149Z	Maintenance Zone 6149:										
2036N6150Z	Maintenance Zone 6150:	Dec-23	Aug-24	Poe	\$217	40%					
2036N7048Z	Maintenance Zone 7048:	Nov-20	Mar-22	Benham	\$252	95%					
2036N7060Z	Maintenance Zone 7060:	Dec-20	Dec-21	HUB	\$73	95%	Jan-24	May-24	Gradeline	\$1,483	100%
2036N7104Z	Maintenance Zone 7104:										
2036N7109Z	Maintenance Zone 7109:	Aug-23	Apr-24	Keithline	\$94	90%					
2036N7115Z	Maintenance Zone 7115:										
2036N8057Z	Maintenance Zone 8057:	Feb-21	Mar-22	Wallace	\$107	95%	Aug-23	Nov-23	Ellsworth	\$1,478	100%
2036N8102Z	Maintenance Zone 8102:	Oct-20	Apr-22	FNI	\$171	95%	Apr-25	Feb-25	Ellsworth	\$1,539	100%
2036N8113Z	Maintenance Zone 8113:	Aug-22	Feb-23	Keithline		95%	Jan-24	Aug-24	R&L Construction	\$300	100%
2036N8116Z	Maintenance Zone 8116:										
2036N9036Z	Maintenance Zone 9036:	Sep-22	Feb-24	CEC	\$236	90%					
2036N9037Z	Maintenance Zone 9037:	Jan-21	Aug-21	CP&Y	\$183	90%	Jun-24	Feb-25	H & G Paving	\$1,453	37%
2036N9038Z	Maintenance Zone 9038:	Dec-20	Oct-21	PEC	\$71	95%	Jul-23	Oct-23	Tri-Star	\$520	100%
2036N9043Z	Maintenance Zone 9043:										
2036N9044Z	Maintenance Zone 9044:	Sep-22	Apr-24	Benham	\$201	70%					
2036N9045Z	Maintenance Zone 9045:	Aug-22	Feb-23	Keithline	\$21	95%	Jan-24	Oct-24	R&L Construction	\$300	100%
2036N9049Z	Maintenance Zone 9049:	Jun-22	Mar-23	Marquardt	\$207	91%					
2036N9050Z	Maintenance Zone 9050:	Jan-21	Sep-21	CP&Y	\$98	90%	Mar-24	Oct-24	R&L Construction	\$1,162	100%
2036N9051Z	Maintenance Zone 9051:	Sep-20	Apr-21	Keithline	\$83	95%	Sep-25	Feb-25	Tri-Star	\$907	75%

98

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036N9052Z	Maintenance Zone 9052:			Keithline		95%	Jan-24	Oct-24	R&L Construction	\$300	100%
Arterial Street Rehabilitation Projects:											
	Arterial Street Projects:										
2036A0001Z	56th St N-MLK Blvd to 1500ft W of Peoria										
2036A0002Z	46th St N - Peoria Ave to Lewis Ave	Apr-22	Mar-23	C&K	\$273	90%	May-24	Jan-25	Becco	\$2,967	100%
2036A0003Z	46th St N - Elwood Ave to MLK Jr Blvd										
2036A0004Z	36th St N - Peoria Ave to Lewis Ave										
2036A0005Z	36th St N - Osage Cnty Line to MLK Blvd	Jul-23	Aug-24	Benham	\$52	25%					
2036A0006Z	31st St N - 53rd W Ave to 41st W Ave										
2036A0007Z	Apache St - Harvard Ave to Yale Ave	Jun-22	Jan-23		\$49	20%					
2036A0008Z	Pine St - Gilcrease Museum Rd to Union	Sep-21	Sep-22	Poe		90%	Aug-23	Jul-24	Becco		100%
2036A0009Z	Pine St - Peoria Ave to Lewis Ave			CEC		50%			ODOT-STP		
2036A0010Z	Edison St - 33rd W Ave to Union Ave	Sep-21	Sep-22	Poe		90%	Aug-23	Jul-24	Becco		100%
2036A0011Z	33rd W Ave - Apache St to Pine St	Sep-21	Sep-22	Poe		90%	Aug-23	Jul-24	Becco		100%
2036A0012Z	33rd W Ave - Pine St to Edison St	Sep-21	Sep-22	Poe		90%	Aug-23	Jul-24	Becco		100%
2036A0013Z	Gilcrease Museum Rd - Apache to Pine	Sep-21	Sep-22	Poe		90%					
2036A0014Z	MLK Jr Blvd - 56th St N to 46th St N										
2036A0015Z	MLK Jr Blvd - 36th St N to Apache St	Jul-23	Aug-24	Benham	\$100	90%					
2036A0016Z	MLK Jr Blvd - Apache St to Pine St	Jul-23	Aug-24	Benham	\$50	90%					
2036A0017Z	Peoria Ave - 56th St N to 46th St N	Apr-22	Mar-23	C&K	\$273	90%	May-24	Jan-25	Becco	\$2,697	100%
2036A0018Z	Peoria Ave - 46th St N to 36th St N	Apr-22	Mar-23	C&K	\$273	90%	May-24	Jan-25	Becco	\$2,697	100%
2036A0019Z	Peoria Ave - Pine St to Admiral Blvd	May-24	Apr-25	K-H		60%			ODOT-STP		
2036A0020Z	Lewis Ave - Pine St to Admiral PI	Oct-22	Feb-24	CEC	\$179	60%			ODOT-STP		
2036A0021Z	Harvard Ave - Mohawk Blvd to 36th St N			Schemmer	\$49						
2036A0025Z	41st St S - Union Ave to Elwood Ave	Jan-23	Sep-23	BKL	\$223	90%					
2036A0026Z	51st St S - 33rd W Ave to Union Ave										
2036A0028Z	Elwood Ave - 71st St S to 81st St S										
2036A0029Z	Lewis Ave - 61st St S to 71st St S										
2036A0030Z	Lewis Ave - 71st St S to 81st St S										
2036A0031Z	Delaware Ave - 81st St S to 91st St S	Jun-23	Nov-23	BKL	\$109	90%	Jun-24	24-Oct	Crossland Heavy	\$1,421	100%
2036A0032Z	Harvard Ave - 61st St S to 71st St S										
2036A0033Z	Harvard Ave - 71st St S to 81st St S			Benham							
2036A0034Z	Harvard Ave - 81st St S to 91st St S										
2036A0039Z	36th St N - Garnett Rd to 129th E Ave	Nov-23	Aug-24	Keithline	\$88	90%					
2036A0040Z	36th St N - 129th E Ave to 141st E Ave										
2036A0041Z	Apache St - Gilcrease Expy to Sheridan Rd										
2036A0042Z	Pine St - Lewis Ave to Harvard Ave	May-24	Apr-25	K-H		60%			ODOT-STP		
2036A0043Z	Pine St - State Hwy 11 to Mingo Rd	Jun-23	Feb-24	Garver	\$189	85%			ODOT-STP		
2036A0044Z	Pine St - Mingo Rd to Garnett Rd										
2036A0045Z	Pine St - Garnett Rd to 129th E Ave	Jan-23	Oct-24	PEC	\$75	85%					
2036A0046Z	Admiral PI - Sheridan Rd to Memorial Dr			CEC							
2036A0047Z	Admiral PI - Memorial Dr to Mingo Rd			CEC							
2036A0048Z	Admiral PI - Garnett Rd to 129th E Ave			CEC							

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0049Z	11th St S - Memorial Dr to 89th E Ave								ODOT-STP		
2036A0050Z	Yale Ave - Apache St to Pine St	Jul-23	Apr-24	HUB	\$200	90%					
2036A0051Z	Yale Ave - Pine St to Admiral Pl										
2036A0052Z	Sheridan Rd - 36th St N to Apache St										
2036A0053Z	Garnett Rd - Admiral Pl to 11th St S										
2036A0054Z	129th E Ave - 36th St N to Apache St	Nov-22	Aug-23	Keithline	\$88	90%					
2036A0055Z	129th E Ave - Apache St to Pine St	Feb-23	Jun-23	HUB		90%	Oct-25				
2036A0065Z	11th St S - Harvard Ave to Yale Ave										
2036A0066Z	15th St S - Boston Ave to Denver Ave										
2036A0067Z	15th St S - Harvard Ave to Yale Ave	Nov-22	May-24	Garver	\$110	90%					
2036A0068Z	21st St S - Lewis Ave to Harvard Ave										
2036A0069Z	21st St S - Harvard Ave to Yale Ave										
2036A0070Z	Peoria Ave - 21st St S to 31st St S										
2036A0077Z	15th St S - Sheridan Rd to 73rd E Ave										
2036A0078Z	41st St S - Yale Ave to Sheridan Ave										
2036A0079Z	Yale Ave - 31st St S to 36th St S										
2036A0080Z	Yale Ave - 41st St S to I-44										
2036A0081Z	Sheridan Rd - 21st St S to 31st St S										
2036A0082Z	Sheridan Rd - 31st St S to 41st St S										
2036A0083Z	Sheridan Rd - 41st St S to 51st St S	Aug-25	Jul-25	Garver	\$363	30%					
2036A0086Z	Admiral Pl: 225th EA to 22200 Blk E Adm.			CEC							
2036A0087Z	11th St S - 145th E Ave to 161st E Ave										
2036A0088Z	11th St S - 161st E Ave to 177th E Ave	Jun-23	Aug-24	TEP	\$54	90%					
2036A0089Z	11th St S - 177th E Ave to 193rd E Ave	Jun-23	Aug-24	TEP	\$84	90%					
2036A0090Z	21st St S - 145th E Ave to 161st E Ave										
2036A0091Z	21st St S - 161st E Ave to 177th E Ave										
2036A0092Z	31st St S - Garnett Rd to 129th E Ave			Marquardt					ODOT-STP		
2036A0093Z	41st St S - 177th E Ave to 193rd E Ave										
2036A0094Z	129th E Ave - 51st St S to 61st St S										
2036A0095Z	145th E Ave - 11th St S to 21st St S										
2036A0096Z	145th E Ave - 21st St S to 31st St S										
2036A0097Z	161st E Ave - 11th St S to 21st St S	Jun-23		TEP	\$91	90%					
2036A0108Z	61st St S - Sheridan Rd to Memorial Dr										
2036A0109Z	Memorial Dr - 51st St S to 61st St S	Jan-23	May-24	Poe	\$438	85%					
2036A0110Z	Mingo Rd - 61st St S to 71st St S	Jun-24	Jul-25	HUB	\$130	60%			ODOT-STP		
2036A0111Z	Mingo Rd - 91st St S to 101st St S										
2036A0113Z	101st St S - Yale Ave to Sheridan Ave										
2036A0114Z	101st St S - Sheridan Rd to Memorial Dr										
2036A0115Z	111st St S - Yale Ave to Sheridan Rd										
2036A0116Z	121st St S - Yale Ave to Sheridan Rd										
2036A0117Z	Yale Ave - 61st St S to 71st St S										
2036A0118Z	Yale Ave - 111th St S to 121st St S	Dec-24	Aug-25	CEC	\$68	20%					
2036A0119Z	Sheridan Rd - 71st St S to 81st St S	Apr-25	Jul-25	HUB	\$138	60%			ODOT-STP		

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0122Z	41st St S - Riverside Dr to Peoria Ave										
2036A0123Z	41st St S - Peoria Ave to Lewis Ave										
2036A0124Z	Peoria Ave - 31st St S to 41st St S	Jun-23	Oct-24	Marquardt	\$59	67%			ODOT-STP		
2036A0125Z	Lewis Ave - 41st St S to I-44	Aug-22	Jun-24	Benham	\$85	64%					
	Intersection Projects										
2036A0022Z	36th St N & Harvard Ave Intersection			Schemmer							
2036A0023Z	Apache St & MLK Jr Blvd Intersection			Benham							
2036A0024Z	Pine St & Gilcrease Museum Rd Intersection										
2036A0035Z	41st St S & Elwood Ave Intersection	Jan-23	Sep-23	BKL	\$223	90%					
2036A0036Z	51st St S & 33rd W Ave Intersection										
2036A0037Z	71st St S & Union Ave Intersection										
2036A0038Z	81st St S & Union Ave Intersection										
2036A0056Z	36th St N & 129th E Ave Intersection	Nov-22	Aug-23	Keithline	\$65	90%					
2036A0057Z	Pine St & Sheridan Rd Intersection										
2036A0058Z	Pine St & Mingo Rd Intersection	Jan-23	Feb-24	Garver		88%			ODOT-STP		
2036A0059Z	Pine St & Garnett Rd Intersection	Jun-23	Oct-24	PEC	\$35	85%					
2036A0060Z	Admiral PI & Sheridan Rd Intersection			CEC							
2036A0061Z	Admiral PI & Garnett Rd Intersection										
2036A0062Z	11th St S & Sheridan Rd Intersection										
2036A0063Z	11th St S & Mingo Rd Intersection										
2036A0071Z	11th St S & Peoria Ave Intersection										
2036A0073Z	11th St S & Harvard Ave Intersection										
2036A0074Z	15th St S & Harvard Ave Intersection	Mar-25	Feb-25	Garver	\$130	90%					
2036A0075Z	21st St S & Harvard Ave Intersection										
2036A0076Z	31st St S & Peoria Ave Intersection	Jun-23		Marquardt	\$42	67%					
2036A0084Z	15th St S & Sheridan Rd Intersection										
2036A0085Z	41st St S & Yale Ave Intersection										
2036A0098Z	11th St S & 145th E Ave Intersection										
2036A0099Z	11th St S & 161st E Ave Intersection	Jun-23	Aug-24	TEP	\$16	90%					
2036A0100Z	11th St S & 177th E Ave Intersection	Jun-23	Aug-24	TEP	\$14	90%					
2036A0101Z	11th St S & 193rd E Ave Intersection	Jun-23	Aug-24	TEP	\$14	90%					
2036A0102Z	21st St S & 145th E Ave Intersection										
2036A0103Z	21st St S & 161st E Ave Intersection										
2036A0104Z	21st St S & 177th E Ave Intersection										
2036A0105Z	21st St S & 193rd E Ave Intersection										
2036A0106Z	31st St S & 145th E Ave Intersection										
2036A0107Z	41st St S & 177th E Ave Intersection										
2036A0112Z	91st St S & Memorial Dr Intersection										
2036A0120Z	121st St S & Yale Ave Intersection										
2036A0121Z	111th St S & Yale Ave Intersection			CEC							
2036A0126Z	41st St S & Peoria Ave Intersection										
	Arterial Street Widening Projects:										
2036W0001Z	Gilcrease Museum Rd - Pine to Admiral	Sep-22	Aug-23	Poe		90%	May-25				

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT**

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036W0002Z	81st St S - Tacoma Ave to Maybelle Ave			ODOT					ODOT		
2036W0003Z	81st St S & Elwood Ave Intersection	Oct-24	Dec-25	BKL	\$468	20%					
2036W0004Z	91st St S - Memorial Dr to Mingo Rd	Mar-20	Dec-23	Garver	\$814	95%	Jun-25	27-Feb	Tri-Star	\$12,800.00	10%
2036W0005Z	101st St S & Sheridan Rd Intersection	Nov-23	Aug-25	CEC	\$603	40%	Oct-27				
2036W0006Z	81st St S - Harvard Ave to Yale Ave	Jun-23	Jan-24	Garver	\$1,485	33%					
Central Business District (CBD)											
	Streets and Alleyways										
2036D0001Z	4th St	6/1/2023	Feb-24	Poe		80%					
2036D0002Z	MLK Ave & Detroit Ave north of BNSF	Aug-20	Feb-21	Poe	\$130	95%	Oct-21	May-22	Crossland	\$1,592.00	100%
2036D0003Z	Cincinnati Ave	Oct-23		Poe		25%					
2036D0004Z	Detroit Ave south of BNSF	Aug-23	Sep-24	Poe		30%					
2036D0005Z	Reconciliation Way	Aug-20	Feb-21	Poe		95%	Oct-21	May-22	Crossland	\$1,592.00	100%
2036D0006Z	Lansing Ave	Jun-23	Feb-24	Poe		60%					
2036D0007Z	Alleyways			Str & Stwtr							
Bridge Maintenance & Rehabilitation											
2037B0201C	Bridge #201C	Oct-22	Oct-23	Benham	\$8	90%					
2037B0216Z	Bridge #216										
2037B0219D	Bridge #219D										
2037B0286Z	Bridge #286	Oct-22	Oct-23	Benham	\$8	90%					
2037B0340Z	Bridge #340										
2037B0343Z	Bridge #343	Oct-22	Oct-23	Benham	\$8	90%					
2037B0179Z	Bridge #179										
2037B0232Z	Bridge #232										
2037B0245Z	Bridge #245	Jan-21	Sep-21	Garver	\$89	95%	Sep-23	Jan-24	Gradeline	\$600.00	100%
2037B0258Z	Bridge #258	Jan-21	Sep-21	Garver	\$35	95%	Sep-23	Jan-24	Gradeline	\$300.00	100%
2037B0263Z	Bridge #263	Jul-21		CP&Y	\$30	90%					
2037B0301Z	Bridge #301	Jul-21		CP&Y	\$30	90%					
2037B0359Z	Bridge #359	Feb-22	Dec-22	Garver		95%	Aug-23	Feb-24	Daris	\$150.00	100%
2037B0232A	Bridge #232A	Jan-21	Sep-21	Garver		95%					
2037B0301A	Bridge #301A										
2037B0425Z	Bridge #425										
2037B0225Z	Bridge #225										
2037B0167Z	Bridge #167	Feb-22	Dec-22	Garver		90%	Aug-23	Feb-24	Daris	\$60.00	100%
2037B0173Z	Bridge #173			Poe							
2037B0236Z	Bridge #236										
2037B0241Z	Bridge #241	Jul-21		CP&Y	\$54	60%					
2037B0261A	Bridge #261A	Feb-22	Dec-22	Garver		90%	Aug-23	Feb-24	Daris	\$120.00	100%
2037B0261B	Bridge #261B	Feb-22	Dec-22	Garver		90%	Aug-23	Feb-24	Daris	\$100.00	100%
2037B0269Z	Bridge #269			Benham							
2037B0474Z	Bridge #474										
2037B0482Z	Bridge #482										
2037B0153Z	Bridge #153										
2037B0183Z	Bridge #183										

CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2037B0252Z	Bridge #252										
2037B0271Z	Bridge #271										
2037B0322Z	Bridge #322	Oct-22	Jul-23	Benham	\$8	95%			H&G		
2037B0329Z	Bridge #329										
2037B0478Z	Bridge #478										
2037B0204Z	Bridge #204	Mar-21	Jul-24	CP&Y	\$35	90%	Aug-24	Apr-25	Bright Lighting	\$1,245.00	40%
2037B0315Z	Bridge #315										
2037B0336Z	Bridge #336										
2037B0404Z	Bridge #404										
2037B0346Z	Bridge #346										
2037B0423Z	Bridge #423	Oct-22	Feb-25	Benham	\$8	60%					
2037B0424Z	Bridge #424										
2037B1000Z	Citywide Bridge Rehab and Inspection										
Citywide Projects											
	Citywide ADA Transition Plan Impl & Update (ROW)										
2036X0001Z	Transition Plan Update										
2036X0002Z	Transit Stops			BKL							
2036X0003Z	Signalized Intersections (Design)										
	Signalized Intersections (Harvard - 15th & 21st Signal)									\$200,000.00	
	Signalized Intersections (11th & Delaware Signal)									\$100,000.00	
	Signalized Intersections (Lewis - Apache & 36th N)									\$200,000.00	
	Signalized Intersections (51st - Mingo & US169)									\$200,000.00	
	Signalized Intersections (Utica - Pine & Admiral)									\$350,000.00	
	Signalized Intersections (11th & Utica)									\$200,000.00	
	Signalized Intersections (BA Expwy & Hudson)									\$200,000.00	
2036S0001Z	Sidewalk Corridors			BKL							
2036X0004Z	Citywide Infrastructure Partnership Funds										
2036N0001Z	Citywide Non-Arterial Routine & Preventive										
2036A1000Z	Citywide Arterial Routine and Preventive										
2036A1001Z	Pavement Reinspection										
2035X0001Z	Transit-MTTA-Route 66 Bus Rapid Transit			HNTB	\$1,317	80%					
	Traffic Engineering										
2036X0005Z	Signal Coordination & Communication (TMC)			Misc.	\$362,884	100%					
	Signal Coordination & Communication (On-Call)			Kimley-Horn	\$200,000	38%					
	Signal Coordination & Communication (SS4A Grant Match)			SS4A	\$111,717						
	Signal Coordination & Communication (Hardware)			Econolite	\$100,000	100%					
2036X0006Z	Signal Installation, Repair and Replace (Repairs)			Misc.	\$201,481	100%					
	Signal Installation, Repair and Replace (Equipment)			Misc.	\$885,645	55%					
	Signal Installation, Repair and Replace (Harvard - 15th to 21st)			Garver	\$15,750					\$600,000.00	
	Signal Installation, Repair and Replace (31st - Yale to Sheridan)			Garver	\$26,000						
	Signal Installation, Repair and Replace (11th & Utica)									\$600,000.00	
2036X0007Z	Traffic Calming (Administration & Design)			Misc.	\$383,659	87%					
	Traffic Calming (Materials and installation)								APAC	\$69,925.85	99%

CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE
TRANSPORTATION PROJECTS STATUS REPORT

Engineer: Doug Helt
Traffic Ops: Tracy Nyholm

Design & Construction as of:
dhelt@cityoftulsa.org
tryholm@cityoftulsa.org

04/01/25

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036X0008Z	Lighting Repair and Replacement (Citywide, On-Call)			Garver	\$75,000				3rd Generation Electric	\$262,983.32	5%
	Lighting Repair and Replacement (BA)								ODOT	\$7,559.89	100%
	Lighting Repair and Replacement (Materials)			Misc.	\$110,729	100%					
	Lighting Repair and Replacement (WZ Traffic Control)								Advanced WZ	\$50,000.00	89%
2036X0009Z	Pavement Markings and Signs (Materials)			Misc.	\$829,984	100%					
	Pavement Markings and Signs (Equipment)			Misc.	\$68,434	100%					
	Pavement Markings and Signs (Administration)			CEC	\$200,000	40%					
	Pavement Markings and Signs (SS4A Grant Match)			SS4A	\$832,551						
	Pavement Markings and Signs (Contractor Services)								Action Safety	\$400,000.00	1%
2036X0010Z	Guardrail Repair and Replacement (Repairs and Materials)			Misc.	\$21,420	100%					
	Guardrail Repair and Replacement (Citywide)			Advertisement	\$657	100%			Becco	\$363,872.98	100%
2039X0009Z	Traffic Studies (Street Light Data Services)			INCOG	\$71,839	100%					
	Bicycle-Pedestrian Infrastructure										
2036S0002Z	Go Plan Implementation - Engineering			Garver							
2036S0003Z	Go Plan Implementation-Traffic Operation			Traffic							
2036S0004Z	Arterial Sidewalk			Strt & Strmwtr							
2036S0005Z	Non Arterial Sidewalk			Strt & Strmwtr							
2036X0011Z	Arena District Mstr Plan Implementation			Landplan					ODOT-STP		
COMPLETED Projects --FUNDS 4281-4285											
Arterial Street Rehabilitation Projects:											
	Arterial Street Projects:										
2036A0027Z	61st St S - Lewis Ave to Harvard Ave	Jun-22	Jan-23	COT	\$49	100%	Apr-24	24-Jun	Becco	\$679	100%
2036A0064Z	11th St S - Utica Ave to Lewis Ave			Wallace		100%			TIF-IDP		100%
2036A0072Z	11th St S & Lewis Ave Intersection			Wallace		100%			TIF-IDP		100%
TOTAL FUNDS 4281-4285 - 2020 STREETS GENERAL OBLIGATION BOND											
* Same design contract for \$35,000											
** Same design contract for \$15,000											
*** Total contract with Becco is \$4,448,000 for stormwater project 993311 & street projects 6008-014180 & 6312-994526											

(6) Finance and Economic Factor

STOC

SALES TAX OVERVIEW COMMITTEE

Ashley Webb
Chair

Ashley R. Webb
Riggs, Abney, Neal, Turpen, Orbison & Lewis Inc.
Attorney At Law
Tulsa, OK 74119
(918) 699-8905

To: City Council
Date: May 7, 2025
Subject: May Report to City Council

Attached is the April 2025 Sales Tax Overview Committee (STOC) Status Report

2006 Special Extended Sales Tax

March expenditures totaled \$52,000, of which \$52,000 was spent on the Energy Efficiency Facility Improvements project. Encumbrances and commitments total \$692,000. Current appropriations for the 2006 Third Penny Sales Tax Extension Fund total \$273,275,000. There is a current appropriation balance of \$5,782,000.

2008 Sales Tax Special Temporary Streets

March expenditures totaled \$4,000, of which \$4,000 was spent on the Citywide General Engineering project. Encumbrances and commitments total \$151,000. Current appropriations for the 2008 Sales Tax Special Temporary Streets Fund total \$149,658,000. There is a current appropriation balance of \$4,165,000.

2014 Sales Tax

March expenditures totaled \$2,432,000, of which \$1,087,000 was spent on the Citywide Arterial streets routine and preventative maintenance project. Encumbrances and commitments total \$52,850,000. Current appropriations for the 2014 Sales Tax Fund total \$580,369,000. There is a current appropriation balance of \$75,342,000.

2016 Sales Tax

March expenditures totaled \$5,118,000, of which \$4,462,000 was spent on the the Tulsa Vision Advanced Sales Tax Revenue Bonds debt service project. Encumbrances and commitments total \$5,001,000. Current appropriations for the 2016 Sales Tax Fund total \$399,172,000. There is a current appropriation balance of \$64,011,000.

2016 Revenue Bond

March expenditures totaled \$905,000, of which \$590,000 was spent on the South Mingo Corridor project. Encumbrances and commitments total \$10,647,000. Current appropriations for the 2016 Revenue Bond Fund total \$350,600,000. There is a current appropriation balance of \$6,393,000.

2020 Sales Tax

March expenditures totaled \$2,632,000, of which \$1,050,000 was spent on the CW - Outdoor Park Play Ameniti project. Encumbrances and commitments total \$8,538,000. Current appropriations for the 2020 Sales Tax Fund total \$150,556,000. There is a current appropriation balance of \$48,421,000.

2024 General Obligation Bonds

March expenditures totaled \$1,416,000, of which \$603,000 was spent on the Citywide Grant-Matching Funds for Streets project. Encumbrances and commitments total \$8,661,000. Current appropriations for the 2024 General Obligation Bonds Fund total \$156,285,000. There is a current appropriation balance of \$102,724,000.

2020 General Obligation Bonds

March expenditures totaled \$887,000, of which \$282,000 was spent on the Maintenance Zone 1071 project. Encumbrances and commitments total \$32,265,000. Current appropriations for the 2020 General Obligation Bonds Fund total \$224,405,000. There is a current appropriation balance of \$108,664,000.

2014 General Obligation Bonds

March expenditures totaled \$1,451,000, of which \$301,000 was spent on the Maintenance Zone 3010 project. Encumbrances and commitments total \$31,180,000. Current appropriations for the 2014 General Obligation Bonds Fund total \$355,000,000. There is a current appropriation balance of \$48,283,000.

2008 General Obligation Bonds

There were no expenditures in March. Encumbrances and commitments total \$1,049,000. Current appropriations for the 2008 General Obligation Bonds Fund total \$231,104,000. There is a current appropriation balance of \$294,000.

2005 General Obligation Bonds

March expenditures totaled \$138,000, of which \$138,000 was spent on the Bridge #162: Boston Ave project. Encumbrances and commitments total \$747,000. Current appropriations for the 2005 General Obligation Bonds Fund total \$75,966,000. There is a current appropriation balance of \$13,000.

Respectfully submitted,

Ashley Webb, Chair



Attachments

cc: Christy Basgall
Jarrod Moore
Jake Epp



FINANCIAL REPORT TO CITY COUNCIL

Wednesday, May 7, 2025

I. Financial Report

Revenue: 2016 Vision 0.805 Percent and 2020 Sales Tax 0.45 Percent Sales Tax Funds

		Fiscal Year to Date	
	March	Thru March	
Actual	\$ 9,188,772	\$	90,312,964
Adopted Budget - Current Year	9,614,684		90,550,466
Actual vs Budget	\$ (425,912)	\$	(237,502)

Expenditures

Fund	March	Fiscal Year to Date Thru March	
409 - 2020 Sales Tax	\$ 2,631,057	\$	18,667,348
4001, 4003, 4004 - Tulsa Vision Rev Bonds	904,258		3,275,320
4000 - Tulsa Vision Sales Tax	5,117,759		43,843,945
405 - 2014 Sales Tax	2,431,983		14,607,373
404 - 2008 Streets Temporary Sales Tax	3,719		22,792
402 - 2006 Special Extended Sales Tax	51,728		590,923
TOTAL	\$ 11,140,504	\$	81,007,702

II. Expenditures in Other Funds

Fund	March	Fiscal Year to Date Thru March	
401 - 2001 Sales Tax	-		14,360
429 - 2024 GO Bond	1,415,344		38,921,456
428 - 2020 GO Bond	886,776		23,018,680
427 - 2014 GO Bond	1,450,548		13,164,462
426 - 2008 GO Bond	-		-
425 - 2005 GO Bond	137,990		302,441
TOTAL	\$ 3,890,659	\$	75,421,398

III. Items for the City Council's Attention

- A. Monthly Financial Reports
- B. STOC Committee and Subcommittee Minutes and Reports

IV. Attachments

- A. Attendance Record for the last 12 months
- B. STOC Committee and Subcommittee Minutes and Reports

Respectfully submitted,

Ashley R. Webb, Chair

Attachments

cc: Christy Basgall
Jarrod Moore
Jake Epp

MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY

As of March 31, 2025

	CURRENT APPROPRIATIONS	EXPENDITURES		ENCUMBERED/ COMMITTED	PERCENT	BALANCE
		Current Month	Life To Date			
Fund 401 and Fund 403						
2001 Third Penny Sales Tax and 2006 Advance Funded Sales Tax	\$ 112,613,794	\$ -	\$ 112,611,407	\$ -	100%	\$ 2,387
Fund 402						
2006 Third Penny Sales Tax Extension	\$ 273,274,569	\$ 51,728	\$ 266,800,370	\$ 691,826	98%	\$ 5,782,374
Fund 404						
2008 Sales Tax Special Temporary Streets Fund	\$ 149,658,132	\$ 3,719	\$ 145,342,551	\$ 150,945	97%	\$ 4,164,636
Fund 405						
2014 Sales Tax Fund	\$ 580,368,725	\$ 2,431,983	\$ 452,177,005	\$ 52,849,831	87%	\$ 75,341,889
Fund 406: 4000						
2016 Sales Tax Fund	\$ 399,171,895	\$ 5,117,759	\$ 330,159,510	\$ 5,000,897	84%	\$ 64,011,488
Fund 406: 4001, 4003, 4004						
2016 Revenue Bond Fund	\$ 350,600,000	\$ 904,258	\$ 333,559,799	\$ 10,647,292	98%	\$ 6,392,909
Fund 409						
2020 Sales Tax Fund	\$ 150,556,112	\$ 2,631,057	\$ 93,596,511	\$ 8,538,350	68%	\$ 48,421,250

MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY

As of March 31, 2025

	CURRENT APPROPRIATIONS	EXPENDITURES		ENCUMBERED/ COMMITTED	PERCENT	BALANCE
		Current Month	Life To Date			
Fund 429						
2024 General Obligation Bonds	\$ 156,285,000	\$ 1,415,344	\$ 44,900,337	\$ 8,660,922	34%	\$ 102,723,741
Fund 428						
2020 General Obligation Bonds	\$ 224,405,000	\$ 886,776	\$ 83,475,536	\$ 32,265,429	52%	\$ 108,664,034
Fund 427						
2014 General Obligation Bonds	\$ 355,000,000	\$ 1,450,548	\$ 275,537,498	\$ 31,179,520	86%	\$ 48,282,981
Funds 426						
2008 General Obligation Bonds	\$ 231,103,878	\$ -	\$ 229,760,841	\$ 1,048,941	100%	\$ 294,096
Funds 425						
2005 General Obligation Bonds	\$ 75,966,289	\$ 137,990	\$ 75,205,895	\$ 747,384	100%	\$ 13,009
Fund 740: 7401-7408						
TMUA--Water Capital Fund	\$ 552,745,405	\$ 6,582,000	\$ 430,858,760	\$ 58,278,330	88%	\$ 63,608,316
Funds 750: 7501-7522						
TMUA--Sanitary Sewer Capital Funds	\$ 684,741,671	\$ 3,841,158	\$ 559,156,151	\$ 68,343,186	92%	\$ 57,242,334

Short Term Capital Purchases Summary (Fund 477) as of March 2025
2006 Sales Tax Capital Equipment Replacement Report

Department/Entitiy	Appropriations	Month's		Year to Date		Encumbrances		Balance
		Expenditures	Expenditures	Expenditures	Expenditures	Commitments	Commitments	
Human Resources	\$ 2,400	\$ -	\$ -	\$ -	\$ 2,400	\$ -	\$ -	-
Finance	\$ 261,988	\$ -	\$ 121,330	\$ 94,301	\$ 46,357	\$ -	\$ -	46,357
Legal	\$ 4,800	\$ -	\$ -	\$ -	\$ 4,800	\$ -	\$ -	4,800
Asset Management	\$ 743,581	\$ 4,660	\$ 137,184	\$ 401,063	\$ 205,335	\$ -	\$ -	205,335
Communications	\$ 9,028	\$ -	\$ 5,075	\$ -	\$ 3,953	\$ -	\$ -	3,953
Information Technology	\$ 8,817,127	\$ 132,304	\$ 1,993,852	\$ 3,579,754	\$ 3,243,521	\$ -	\$ -	3,243,521
Police	\$ 10,640,302	\$ 335,169	\$ 7,202,564	\$ 3,224,825	\$ 212,914	\$ -	\$ -	212,914
Fire	\$ 8,421,974	\$ 949,335	\$ 5,240,451	\$ 1,915,147	\$ 1,266,377	\$ -	\$ -	1,266,377
Public Works	\$ 5,855,288	\$ 79,907	\$ 2,760,053	\$ 2,864,498	\$ 230,737	\$ -	\$ -	230,737
Parks & Recreation	\$ 1,284,484	\$ 335,457	\$ 780,413	\$ 464,062	\$ 40,009	\$ -	\$ -	40,009
Manage Entities - Culture & Recreation	\$ 173,000	\$ -	\$ -	\$ -	\$ 173,000	\$ -	\$ -	173,000
Dept. of City Experience	\$ 581,011	\$ 2,398	\$ 214,186	\$ 92,015	\$ 274,809	\$ -	\$ -	274,809
Development Services	\$ 133,774	\$ -	\$ -	\$ 21,305	\$ 112,469	\$ -	\$ -	112,469
Transfer to Other Funds*	\$ 123,000	\$ -	\$ 123,000	\$ -	\$ -	\$ -	\$ -	-
Transfer to River Parks*	\$ 729,513	\$ -	\$ 507,849	\$ 109,513	\$ 112,151	\$ -	\$ -	112,151
Transfer to TAEMA*	\$ 30,405	\$ -	\$ -	\$ -	\$ 30,405	\$ -	\$ -	30,405
Transfer to Tulsa Transit*	\$ 115,000	\$ -	\$ 115,000	\$ -	\$ -	\$ -	\$ -	-
	\$ 38,074,631.00	\$ 1,845,417.51	\$ 19,342,912.26	\$ 12,768,882.80	\$ 5,962,835.94			

* Total appropriation is transferred to the agency in a lump sum during the year and incorporated into their budget.

Report On Tulsa Economic Indicators February 2025

Economic Overview

The next Economic Overview will be updated with the March 2025 report.

Wage & Salary Employment Conditions

Tulsa's labor force declined a bit in February, ending at 525,500 participants. Overall employment for our area dropped from 509,900 to 506,800 in February. The area unemployment rate was reported at 3.5% for February - which is higher than last month. Total unemployment for the area was 4.0% during the same month last year. According to the second employment survey, Wage and Salary Employment increased in February, to report a total of 479,100. The Manufacturing sector held steady for the month, reporting 53,800 jobs. The Service sector grew this month; the position count is 243,200 for February. The Trade sector decreased a bit to 87,000 total positions.

Freight Conditions

Freight at the Port of Catoosa reported 150,860 of barge tonnage for the month, this is compared to the previous month of 151,698 tons. Compared to the same month a year ago, we have experienced a decrease of 7.9% in barge tonnage. We are currently down 42% YTD compared to Jan-Feb 2024 in airport freight. Passenger counts at Tulsa Int'l Airport were down a little more than 5% in February compared to the same month in 2024.

Enterprise Customers

Month over month total Sewer customers saw a decrease in February, totaling 135,830 for the current period. The current customer base is 0.2% greater than the same month last year. The water customer count saw a decrease in February from the previous period, totaling 147,925 for the month. However, the current customer base is still 0.22% greater than the same month a year ago.

Price Indices

PPI moved up 0.3% in February at 218.9

MCI moved up by 0.4% in February to 321.3

CPI in February dropped a bit from the previous month, now it's 2.8% YoY

Bond Rates

20-Year GO Bond rates moved up slightly to 4.17% in February.

Revenue Bonds (A+) came up to 4.46% this month.

30-Day T Bill rates fell to 4.32% in February, this continues the lower trajectory that began several months ago.


Tulsa Economic Indicators

Most Recent Twelve Months


(unless otherwise Indicated)

	March 24 to February 25	March 23 to February 24	Change
Wage & Salary			
Employment (TMSA 12 Mo. Avg.):	<u>Feb-25</u>	<u>Feb-24</u>	
Manufacturing	53,800	50,900	5.7%
Services	241,500	236,600	2.1%
Trade	87,100	87,300	(0.2%)
Other	<u>97,300</u>	<u>89,900</u>	8.2%
Total	479,700	464,700	3.2%
Unemployment Rates (TMSA 12 Mo. Avg):	<u>Feb-25</u>	<u>Feb-24</u>	
Tulsa MSA	3.3%	3.2%	0.1%
Oklahoma	3.4%	3.1%	0.3%
United States	4.1%	3.7%	0.4%
Air Passengers (Calendar YTD):	<u>Feb-25</u>	<u>Feb-24</u>	
	199,516	209,530	(4.8%)
Barge Tonnage (Calendar YTD):	<u>Feb-25</u>	<u>Feb-24</u>	
	302,558	306,400	(1.3%)
Price and Cost Indices:	<u>Feb-25</u>	<u>Feb-24</u>	
Consumer Price Index - Urban	302.1	294.1	2.7%
Producer Price Index	218.9	211.8	3.3%
Municipal Cost Index (Est.)	321.3	314.7	2.1%
(Indices are not adjusted for seasonality)			
Financial Rates (Monthly Avg.):	<u>Feb-25</u>	<u>Feb-24</u>	
30-Day Treasury Bill	4.32%	5.38%	(1.07)
Municipal General Obligation Bond			
Buyer 11 Bond Index (20 Yr. A-AAA)	4.17%	3.89%	0.28
Municipal Revenue Bond Buyer			
25 Bond Index (25 Yr. A-AA+)	4.46%	3.70%	0.76
Utilities:	<u>Feb-25</u>	<u>Feb-24</u>	
Water Customers	147,900	147,500	0.3%
Sewer Customers	135,800	135,500	0.2%

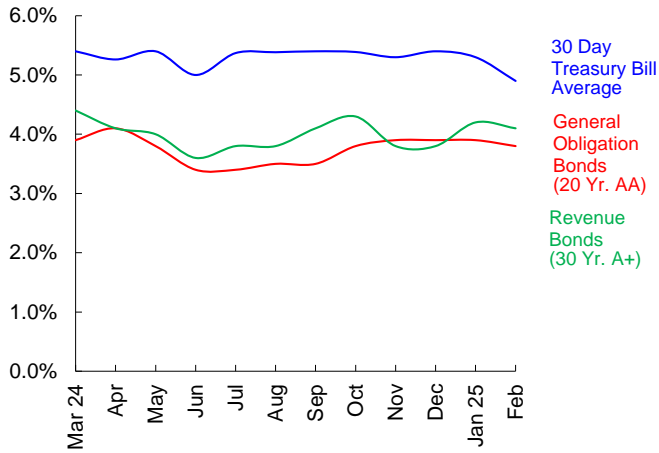
Rates on Municipal Investments and Cost of Financing**



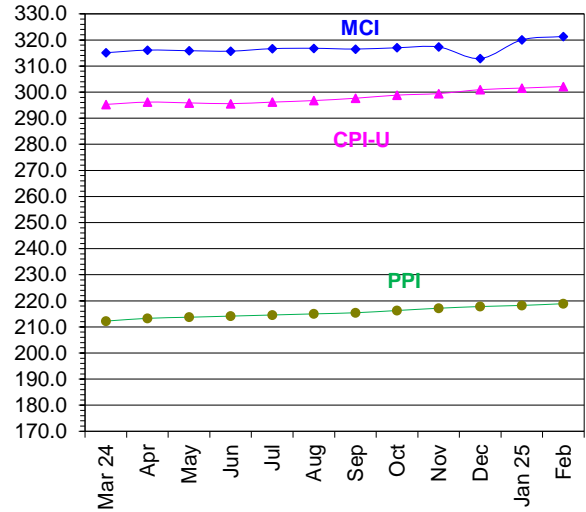
Consumers, Producers, and Municipal Price/Cost Indices



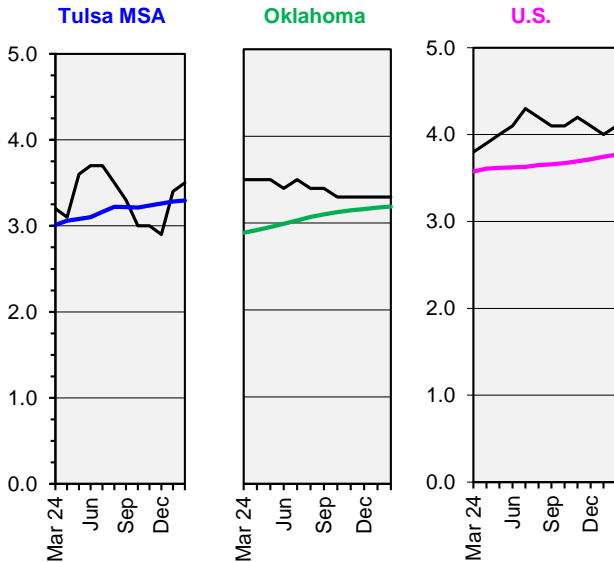Monthly (- -) and Average (—) Unemployment Rates (Most Recent 12 Months)



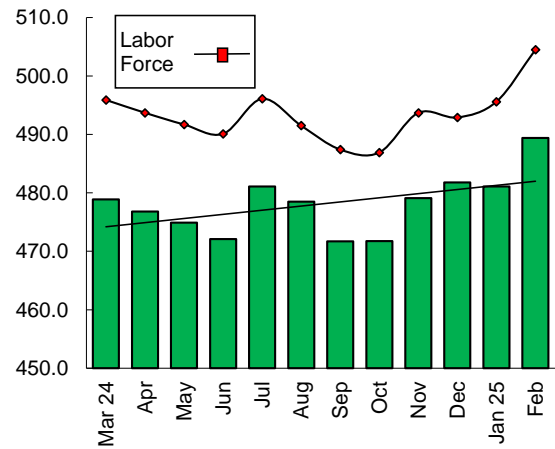Tulsa MSA Wage & Salary Employment, 12 Month MA, and Labor Force (000's)



City of Tulsa
Department of Finance
FINANCIAL REPORT



FINANCE
Budget and Planning

SALES TAX OVERVIEW COMMITTEE

PERIOD ENDING **March 31, 2025**

City of Tulsa

Department of Finance

FINANCIAL REPORT



Monroe Nichols

Mayor

Christy Basgall
Director of Finance

MAYOR

MONROE NICHOLS

CITY COUNCIL

VANESSA HALL-HARPER	DISTRICT 1
ANTHONY ARCHIE	DISTRICT 2
JACKIE DUTTON	DISTRICT 3
LAURA BELLIS	DISTRICT 4
KAREN GILBERT	DISTRICT 5
CHRISTIAM BENGEL	DISTRICT 6
LORI DECTER WRIGHT	DISTRICT 7
PHIL LAKIN JR	DISTRICT 8
CAROL BUSH	DISTRICT 9

CITY AUDITOR

CATHY CRISWELL

SALES TAX OVERVIEW COMMITTEE

Ashley Webb, Chair
Kathy Sebert, Vice Chair
Linda Jenkins, Secretary

Charles Wilkes	Linda Jenkins
Scott Asbjornson	Sylvia Powell
Ashley Webb	Jeffery Covington
Kathy Sebert	James Deming
Maia Treleven	Steve King
Matt Meyer	Paul Hassink
Deborah McKinney	Pamela Amburgy
Scott Grizzle	Mareo Johnson
Jennifer White	Brett Freisen

SALES TAX OVERVIEW COMMITTEE REPORT

Table of Contents

<u>FUND NO.</u>	<u>PAGE NO.</u>
TABLE OF CONTENTS	3
CONSOLIDATED REPORTS	
Balance Sheets.....	4
Schedule of Sales Tax Revenue	5
402.....2006 SPECIAL EXTENDED SALES TAX.....	6
Statement of Revenue, Expenditures, and Encumbrances.....	7
405.....2014 EXTENDED 1.1% SALES TAX.....	10
Statement of Revenue, Expenditures, and Encumbrances.....	11
409.....2020 SALES TAX.....	15
Statement of Revenue, Expenditures, and Encumbrances.....	16
40002016 LIMITED PURPOSE TEMPORARY SALES TAX	18
Statement of Revenue, Expenditures, and Encumbrances.....	19
40012016 VISION ADVANCE FUNDED REVENUE BOND FUND.....	21
Statement of Revenue, Expenditures, and Encumbrances.....	22
40032016 VISION ADVANCE FUNDED REVENUE BOND FUND.....	24
Statement of Revenue, Expenditures, and Encumbrances.....	25
40042016 VISION ADVANCE FUNDED REVENUE BOND FUND.....	27
Statement of Revenue, Expenditures, and Encumbrances.....	28
4270-4276.....2014 GO BOND FUNDS	30
Statement of Revenue, Expenditures, and Encumbrances.....	31
4281-4285.....2020 GO BOND FUNDS	38
Statement of Revenue, Expenditures, and Encumbrances.....	39
4291-4296.....2024 GO BOND FUNDS	48
Statement of Revenue, Expenditures, and Encumbrances.....	49
COMBINED STATEMENT OF OTHER FUND ACTIVITY	51
(401, 403, 404, 425, 426)	52
BUDGET ACTIONS.....	53

CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
BALANCE SHEET
March 2025

	FUND 402 2006 SPECIAL EXTENDED SALES TAX	FUND 405 2014 EXTENDED 1.1% SALES TAX	FUND 409 2020 SALES TAX	FUND 4000 2016 LIMITED PURPOSE TEMPORARY SALES TAX	FUNDS 4270 through 4278 2014 GO BOND FUNDS	FUNDS 4281 through 4285 2020 GO BOND FUNDS	FUNDS 4291 through 4296 2024 GO BOND FUNDS	TOTAL
ASSETS:								
POOLED EQUITY WITH TREASURER	6,648,088.23	141,573,446.89	\$73,260,810.54	\$139,835,598.19	\$659,182.77	\$138,242,852.72	\$111,413,584.36	\$500,219,979.34
ACCRED INTERST RECEIVABLE	41,177.16	890,668.65	447,718.56	897,455.83				\$2,277,020.20
OTHER CURRENT RECEIVABLES				10,164,668.58				\$10,164,668.58
TAX RECEIVABLE			5,682,112.83	1,771,415.48				\$7,453,528.31
TOTAL ASSETS	\$6,689,265.39	\$142,464,115.54	\$79,390,641.93	\$152,669,138.08	\$659,182.77	\$138,242,852.72	\$111,413,584.36	\$520,115,196.43
LIABILITIES, RESERVES, AND FUND BALANCE:								
LIABILITIES AND RESERVE FOR ENC.:								
ACCOUNTS PAYABLE	42,700.00	12,468.04	103,852.76	10,000.00	11,164.97	38,484.13		218,669.90
CONTRACTS PAYABLE - RETAINAGE	35.20	977,674.37	48,807.87		772,068.09	455,975.16	28,921.77	2,254,560.69
CONTRACTS RETAINAGE CLEAR								
PURCHASING CARD ESCROW								
DUE TO OTHER FUNDS								
ADVANCES FROM OTHER FUNDS								
RESERVE FOR ENCUMBRANCES	691,825.83	53,222,081.92	7,389,195.12	4,935,927.47	30,994,697.32	28,757,489.97	8,246,393.36	125,991,217.63
RESERVE FOR COMMITMENTS								
UNENCUMBERED FUND BALANCE:								
APPROPRIATED	5,782,373.50	75,341,888.67	48,421,250.42	48,421,250.43	294,095.52	48,282,981.24	102,723,740.56	226,543,839.78
UNAPPROPRIATED	172,330.86	12,910,002.54	23,427,535.76	99,301,960.18	51,354,997.94	60,707,922.22	414,528.67	247,874,749.50
RESERVED FOR ADVANCES								
TOTAL FUND BALANCE	5,954,704.36	88,251,891.21	71,848,786.18	147,723,210.61	51,649,093.46	108,990,903.46	103,138,269.23	474,418,589.28
TOTAL LIABILITIES, RESERVES, AND FUND BALANCE	\$6,689,265.39	\$142,464,115.54	\$79,390,641.93	\$152,669,138.08	\$83,427,023.84	\$138,242,852.72	\$111,413,584.36	\$602,883,037.50

CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
SCHEDULE OF SALES TAX REVENUE
March, 2025

Month	COMPARISON TO BUDGET (2024-2025)			COMPARISON TO PRIOR YEAR				
	BUDGET	ACTUAL		2023-2024	2024-2025	AMOUNT	PERCENT	
	AMOUNT	AMOUNT	DIFFERENCE	ACTUAL	ACTUAL	INCREASE (DECREASE)	INCREASE/DECREASE ACTUAL BUDGET	
July	\$10,349,764.41	\$ 9,996,764.50	\$ (352,999.91)	\$ 9,845,859.25	\$ 9,996,764.50	\$ 150,905.25	1.5%	5.1%
August	\$10,323,915.14	\$ 10,079,388.62	(244,526.52)	\$ 10,095,265.54	\$ 10,079,388.62	(15,876.92)	-0.2%	2.3%
September	\$10,106,613.79	\$ 10,181,108.56	74,494.77	\$ 9,641,274.74	\$ 10,181,108.56	539,833.82	5.6%	4.8%
October	\$10,385,003.09	\$ 10,170,441.73	(214,561.36)	\$ 10,019,197.63	\$ 10,170,441.73	151,244.10	1.5%	3.7%
November	\$10,062,271.57	\$ 9,854,520.61	(207,750.96)	\$ 9,615,664.08	\$ 9,854,520.61	238,856.53	2.5%	4.6%
December	\$10,062,794.34	\$ 10,530,488.72	467,694.38	\$ 9,937,888.82	\$ 10,530,488.72	592,599.90	6.0%	1.3%
January	\$10,342,586.55	\$ 10,730,724.45	388,137.90	\$ 10,072,232.25	\$ 10,730,724.45	658,492.20	6.5%	2.7%
February	\$10,321,393.09	\$ 10,724,508.29	403,115.20	\$ 10,361,653.82	\$ 10,724,508.29	362,854.47	3.5%	-0.4%
March	\$ 8,867,104.32	\$ 8,969,145.18	102,040.86	\$ 9,110,866.55	\$ 8,969,145.18	(141,721.37)	-1.6%	-2.7%
April	\$ 9,612,324.83			\$ 9,378,599.48				2.5%
May	\$ 9,978,654.79			\$ 10,291,299.34				-3.0%
June	\$ 9,765,595.50			\$ 9,712,756.46				0.5%
TOTAL	\$ 120,178,021.42	\$ 91,237,090.66	\$ 415,644.36	\$ 118,082,557.96	\$ 91,237,090.66	\$ 2,537,187.98	2.9%	1.8%

PERCENT INCREASE (DECREASE) 0.46%

2006 SPECIAL EXTENDED SALES TAX

FUND 402

(SIXTH THIRD PENNY SALES TAX PROGRAM)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 402 - 2006 SPECIAL EXTENDED SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Sales Tax	\$	\$	\$	\$ 430,935,953.99	\$
Donations					
Interest on Investments		19,859.72	329,286.58	16,843,010.44	(329,286.58)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue				1,424,225.61	
Total Revenue		19,859.72	329,286.58	449,203,190.04	-329,286.58
<u>Expenditures</u>					
Project Expenditures	273,274,569.47	51,727.53	2,099,361.08	266,800,370.14	6,474,199.33
Total Expenditures	273,274,569.47	51,727.53	2,099,361.08	266,800,370.14	6,474,199.33
Excess (Deficiency) of Revenue					
Over Expenditures			(1,770,074.50)	182,402,819.90	
Completed Projects				174,416,586.99	
Encumbrances			691,825.83	691,825.83	
Excess (Deficiency) of Revenue Over					
Expenditures and Encumbrances			(2,461,900.33)	7,294,407.08	
June 30, 2022 Ending Fund Balance			8,882,061.76		
Prior year expenditures					
June 30, 2022 Encumbrances			874,245.65		
Adjusted Beginning Fund Balance			9,756,307.41		
Ending Fund Balance			\$ 7,294,407.08	\$ 7,294,407.08	

2006 SPECIAL EXTEND SALES TAX

Fund	402									
As of:	03/31/2025	\$	273,274,569.47	\$	51,727.53	\$	590,923.45	\$	266,800,370.14	\$ 691,825.83 \$ - \$ 5,782,373.50

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
402	016100	Forensic Lab Expansion	\$ 14,729,241.90	\$ -	\$ -	\$ 14,729,241.90	\$ -	\$ -	\$ -
402	016130	Replace 2 Police Helicopters	\$ 4,344,475.00	\$ -	\$ -	\$ 4,344,475.00	\$ -	\$ -	\$ -
402	016200	Apparatus Replacement	\$ 12,863,575.91	\$ -	\$ -	\$ 12,863,575.91	\$ -	\$ -	\$ -
402	016240	Site Acq. For Addnl. Station	\$ 5,300,000.00	\$ -	\$ -	\$ 4,834,838.97	\$ -	\$ -	\$ 465,161.03
402	016310	Network System Replacement	\$ 1,402,150.04	\$ -	\$ -	\$ 1,402,150.04	\$ -	\$ -	\$ -
402	017110	General Park Improvements	\$ 4,829,359.78	\$ -	\$ -	\$ 4,828,917.98	\$ 441.80	\$ -	\$ -
402	064060	Bridge Replacement	\$ 2,500,000.00	\$ -	\$ 282.40	\$ 2,499,896.13	\$ -	\$ -	\$ 103.87
402	064062	Bridge Rehab/Repair Cw	\$ 2,500,000.00	\$ -	\$ -	\$ 2,490,497.85	\$ -	\$ -	\$ 9,502.15
402	064093	City Match-Fed/St/Co Projs	\$ 1,500,000.00	\$ -	\$ -	\$ 1,410,000.00	\$ -	\$ -	\$ 90,000.00
402	064101	41St-Garnett To 129Th E Ave	\$ 500,000.00	\$ -	\$ -	\$ 498,500.00	\$ 1,500.00	\$ -	\$ -
402	064102	81St-Memorial To Mingo	\$ 7,402,272.09	\$ -	\$ -	\$ 7,402,272.09	\$ -	\$ -	\$ -
402	064103	91St & Harvard Intersection	\$ 2,217,000.00	\$ -	\$ -	\$ 2,217,000.00	\$ -	\$ -	\$ -
402	064104	91St And Sheridan Inters	\$ 4,417,718.54	\$ -	\$ -	\$ 4,414,613.00	\$ -	\$ -	\$ 3,105.54
402	064105	61St St Riverside To Peoria	\$ 800,000.00	\$ -	\$ -	\$ 705,989.93	\$ -	\$ -	\$ 94,010.07
402	064106	Garnett-11Th To I-244	\$ 500,000.00	\$ -	\$ -	\$ 499,555.00	\$ -	\$ -	\$ 445.00
402	064107	Mingo 71St To 81St	\$ 500,000.00	\$ -	\$ -	\$ 498,721.40	\$ -	\$ -	\$ 1,278.60
402	064108	Pine St-Memorial To Mingo	\$ 500,000.00	\$ -	\$ -	\$ 487,498.67	\$ -	\$ -	\$ 12,501.33
402	064109	129Th-31St To 41St	\$ 5,500,000.00	\$ -	\$ -	\$ 5,500,000.00	\$ -	\$ -	\$ -
402	064110	61St-Riverside To Peoria	\$ 7,369,000.00	\$ -	\$ -	\$ 7,369,000.00	\$ -	\$ -	\$ -
402	064111	91St-Memorial To Mingo	\$ 500,000.00	\$ -	\$ 704.00	\$ 500,000.00	\$ -	\$ -	\$ -
402	065100	Public Facilities Renov	\$ 7,080,000.00	\$ -	\$ 13,174.99	\$ 6,985,637.26	\$ 84,579.60	\$ -	\$ 9,783.14
402	065300	Energy Efficiency Facil Impr	\$ 1,600,000.00	\$ 51,727.53	\$ 51,727.53	\$ 1,238,782.87	\$ 58,272.47	\$ -	\$ 302,944.66
402	065320	Gilcrease Museum Renovation	\$ 4,451,158.00	\$ -	\$ -	\$ 4,450,747.45	\$ 410.55	\$ -	\$ -
402	067120	Plgnd Splashpad Park Surfs	\$ 3,095,280.61	\$ -	\$ 26,100.00	\$ 3,055,633.40	\$ -	\$ -	\$ 39,647.21
402	067130	Playground Equip Repl/Renov	\$ 1,063,517.00	\$ -	\$ -	\$ 1,054,597.78	\$ -	\$ -	\$ 8,919.22
402	067170	Carl Smith Facil Devel	\$ 235,421.96	\$ -	\$ -	\$ 231,991.95	\$ 3,430.01	\$ -	\$ -
402	067510	Trails Resurf And Widening	\$ 2,924,423.01	\$ -	\$ -	\$ 2,924,423.01	\$ -	\$ -	\$ -
402	067520	EST BANK IMPR 11TH-21STS	\$ 5,250,000.00	\$ -	\$ 498,934.53	\$ 845,865.82	\$ 31,500.00	\$ -	\$ 4,372,634.18
402	068160	New Parking Garage	\$ 5,000,000.00	\$ -	\$ -	\$ 4,488,308.60	\$ 511,691.40	\$ -	\$ -
402	069100	Mtta System Projects	\$ 2,410,000.00	\$ -	\$ -	\$ 2,409,999.89	\$ -	\$ -	\$ 0.11
402	203400001Z	Tulsa Zoo Department	\$ 1,027,836.86	\$ -	\$ -	\$ 1,027,836.86	\$ -	\$ -	\$ -
402	2036D0008Z	1st 2nd & 4th St Two-Way Conv	\$ 354,207.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 354,207.00
402	914411	Tulsa Trails	\$ 1,492,500.00	\$ -	\$ -	\$ 1,492,500.00	\$ -	\$ -	\$ -
402	962301	Tulsa Convention Center Impr	\$ 2,000,000.00	\$ -	\$ -	\$ 1,981,869.61	\$ -	\$ -	\$ 18,130.39
402	966120	Gilcrease Exp Osage Exp-41st	\$ 4,500,000.00	\$ -	\$ -	\$ 4,500,000.00	\$ -	\$ -	\$ -

2014 EXTENDED 1.1% SALES TAX

FUND 405

(2014 EXTENDED 1.1% SALES TAX FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 405 - 2014 EXTENDED 1.1% SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Sales Tax	\$	\$	\$	\$ 551,323,376.53	\$
Donations					
Interest on Investments		426,984.11	6,780,974.76	26,215,117.25	(6,780,974.76)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue				98,580.75	
Total Revenue		426,984.11	6,780,974.76	577,637,074.53	-6,780,974.76
Expenditures					
Project Expenditures	580,368,725.22	2,431,982.52	37,351,389.97	440,219,815.84	140,148,909.38
Total Expenditures	580,368,725.22	2,431,982.52	37,351,389.97	440,219,815.84	140,148,909.38
Excess (Deficiency) of Revenue Over Expenditures			(30,570,415.21)	137,417,258.69	
Completed Projects Encumbrances			52,849,831.09	52,849,831.09	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(83,420,246.30)	84,567,427.60	
June 30, 2022 Ending Fund Balance			129,725,585.23		
Prior year expenditures					
June 30, 2022 Encumbrances			38,262,088.67		
Adjusted Beginning Fund Balance			167,987,673.90		
Ending Fund Balance			\$ 84,567,427.60	\$ 84,567,427.60	

2014 SALES TAX

Fund 405

As of: 03/31/2025

\$	580,368,725.22	\$	2,431,982.52	\$	14,607,372.52	\$	452,177,005.46	\$	52,826,843.09	\$	22,988.00	\$	75,341,888.67
----	----------------	----	--------------	----	---------------	----	----------------	----	---------------	----	-----------	----	---------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
405	140040	Cng Fuel Expansion	\$ 1,800,000.00	\$ -	\$ -	\$ 1,787,810.17	\$ -	\$ -	\$ 12,189.83
405	140050	Radio Frequency ID Devices	\$ 750,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 750,000.00
405	140060	Emd Emergency Generators	\$ 200,000.00	\$ -	\$ -	\$ 196,879.85	\$ -	\$ -	\$ 3,120.15
405	140070	Emd Facilities Maintenance	\$ 1,000,000.00	\$ -	\$ -	\$ 888,975.46	\$ 9,337.00	\$ -	\$ 101,687.54
405	140080	Emd Lights, Hvac, Plumbing	\$ 2,300,000.00	\$ -	\$ 65,726.93	\$ 1,546,084.63	\$ -	\$ -	\$ 753,915.37
405	140100	Capital Equipment	\$ 46,235,000.00	\$ -	\$ -	\$ 46,234,996.00	\$ -	\$ -	\$ 4.00
405	143001	Levee District #12 Rehab	\$ 3,400,000.00	\$ -	\$ 111,375.00	\$ 557,838.00	\$ -	\$ -	\$ 2,842,162.00
405	144006	Signing Pvmnt Mark DIntion	\$ 2,510,000.00	\$ 1,405.67	\$ 599,617.32	\$ 2,509,999.98	\$ -	\$ -	\$ 0.02
405	144008	TRAFFIC SIGNAL INSTALLATION	\$ 3,151,264.92	\$ 497.00	\$ 244,913.99	\$ 3,051,144.12	\$ 30,120.80	\$ -	\$ 70,000.00
405	144017	Art Street Rehab & Citywide	\$ 127,340,000.00	\$ 1,086,261.03	\$ 2,375,803.39	\$ 79,904,485.13	\$ 15,773,427.51	\$ -	\$ 31,662,087.36
405	144018	Bike Ped Master Plan Improv	\$ 4,200,000.00	\$ -	\$ -	\$ 4,199,999.07	\$ -	\$ -	\$ 0.93
405	144063	Bridge Replacement And Rehab	\$ 14,685,000.00	\$ 298,434.08	\$ 2,208,797.35	\$ 10,181,127.61	\$ 3,578,586.02	\$ -	\$ 925,286.37
405	144093	Citywide Matching Funds	\$ 8,429,500.00	\$ -	\$ -	\$ 3,429,967.73	\$ 3,467,936.70	\$ -	\$ 1,531,595.57
405	144094	ODOT Rehab & Replacement	\$ 3,800,000.00	\$ -	\$ -	\$ 3,770,928.06	\$ -	\$ -	\$ 29,071.94
405	144101	Yale Ave 81St - 91St Wdn	\$ 30,250,000.00	\$ -	\$ 718,822.99	\$ 25,160,873.68	\$ 2,391,235.25	\$ -	\$ 2,697,891.07
405	144102	81St St Sheridan - Meml Wdn	\$ 12,000,000.00	\$ -	\$ -	\$ 9,864,642.94	\$ 86,665.72	\$ -	\$ 2,048,691.34
405	144103	Yale 96th - 101st St Wdn	\$ 13,000,000.00	\$ -	\$ -	\$ 11,406,496.12	\$ 168,336.52	\$ -	\$ 1,425,167.36
405	144104	Riverside Dr & Rltd Infrstr	\$ 19,678,159.48	\$ -	\$ -	\$ 19,657,945.32	\$ -	\$ -	\$ 20,214.16
405	144108	Pine St: Mingo-U.S. 169 (DS-W)	\$ 500,000.00	\$ 6,916.89	\$ 14,826.43	\$ 118,944.99	\$ 319,855.01	\$ -	\$ 61,200.00
405	144109	Ada Transition Plan - Street	\$ 10,200,000.00	\$ 65,172.82	\$ 385,544.79	\$ 7,013,114.17	\$ 2,026,108.03	\$ -	\$ 1,160,777.80
405	144120	Gilcrease Exp Local Match	\$ 7,500,000.00	\$ -	\$ 16,783.79	\$ 3,528,029.66	\$ 1,026,273.00	\$ -	\$ 2,945,697.34
405	145200	Ada Transition Plan - Parks	\$ 1,140,000.00	\$ -	\$ -	\$ 962,477.21	\$ 13,820.00	\$ -	\$ 163,702.79
405	145300	Public Facilities, Otc	\$ 3,295,000.00	\$ 19,620.00	\$ 125,649.48	\$ 1,960,093.05	\$ 26,698.55	\$ -	\$ 1,308,208.40
405	145330	Pac - Fire Alarm System	\$ 520,000.00	\$ -	\$ -	\$ 520,000.00	\$ -	\$ -	\$ -
405	145340	Pac - Fire Sprinklers	\$ 1,140,000.00	\$ -	\$ -	\$ 1,085,865.08	\$ 7,795.85	\$ -	\$ 46,339.07
405	145350	Pac - Renovations	\$ 1,840,000.00	\$ -	\$ 2,224.53	\$ 1,738,125.88	\$ 3,540.59	\$ -	\$ 98,333.53
405	145360	Pac - Fan Coil Replacement	\$ 555,000.00	\$ -	\$ -	\$ 523,971.07	\$ -	\$ -	\$ 31,028.93
405	145370	Pac - Hvac Motor Replacement	\$ 175,000.00	\$ -	\$ -	\$ 20,000.00	\$ -	\$ -	\$ 155,000.00
405	145380	PAC: Roof Replacement	\$ 1,300,000.00	\$ -	\$ -	\$ 1,241,015.27	\$ 10,353.77	\$ -	\$ 48,630.96
405	145500	Animal Shelter Expn Ph 1	\$ 8,850,000.00	\$ -	\$ 124,128.36	\$ 876,172.64	\$ 6,370,117.29	\$ -	\$ 1,603,710.07
405	145600	Animal Shelter Facility Imp	\$ 750,000.00	\$ -	\$ -	\$ 705,467.71	\$ -	\$ -	\$ 44,532.29
405	146110	Police Academy-Crt-Compstat	\$ 4,040,000.00	\$ -	\$ -	\$ 2,943,752.18	\$ -	\$ -	\$ 1,096,247.82
405	146120	Uniform Division Renovations	\$ 3,000,000.00	\$ 414,175.97	\$ 889,792.99	\$ 1,276,890.67	\$ 1,423,402.60	\$ -	\$ 299,706.73
405	146210	Apparatus Replacement	\$ 17,000,000.00	\$ -	\$ 794,765.36	\$ 16,961,137.19	\$ -	\$ -	\$ 38,862.81
405	146220	Fire Station Rehabilitation	\$ 7,250,000.00	\$ 4,375.00	\$ 258,372.30	\$ 7,055,348.77	\$ 125,277.04	\$ -	\$ 69,374.19
405	146230	Fire Station Generators	\$ 1,500,000.00	\$ -	\$ -	\$ 1,441,943.79	\$ -	\$ -	\$ 58,056.21
405	146240	Fire Department Facilities	\$ 2,000,000.00	\$ -	\$ -	\$ 180,807.50	\$ 61,854.50	\$ -	\$ 1,757,338.00
405	146300	Financial Sys Replacement	\$ 10,000,000.00	\$ -	\$ 28,930.53	\$ 8,569,422.39	\$ -	\$ -	\$ 1,430,577.61
405	146310	Law Enforcement Records Mgmt	\$ 7,030,000.00	\$ 29,247.50	\$ 128,262.12	\$ 6,633,094.77	\$ 225,867.38	\$ -	\$ 171,037.85
405	147100	Rp - Park Facilities Refurb	\$ 4,000,000.00	\$ -	\$ 6,129.86	\$ 3,355,369.54	\$ -	\$ -	\$ 644,630.46
405	147130	Security System Upgrades	\$ 160,000.00	\$ -	\$ -	\$ 140,896.78	\$ -	\$ -	\$ 19,103.22
405	147170	Hunter: Restroom (Exp & Repr)	\$ 400,000.00	\$ -	\$ -	\$ -	\$ 19,330.00	\$ -	\$ 380,670.00

2014 SALES TAX

Fund 405

As of: 03/31/2025

\$	580,368,725.22	\$	2,431,982.52	\$	14,607,372.52	\$	452,177,005.46	\$	52,826,843.09	\$	22,988.00	\$	75,341,888.67
----	----------------	----	--------------	----	---------------	----	----------------	----	---------------	----	-----------	----	---------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
405	147210	Mohawk Golf Club House	\$ 265,000.00	\$ 3,028.28	\$ 7,654.68	\$ 253,186.45	\$ 9,462.36	\$ -	\$ 2,351.19
405	147220	Page Belcher Improvements	\$ 400,000.00	\$ 11,194.68	\$ 14,646.93	\$ 196,437.13	\$ 58,460.44	\$ -	\$ 145,102.43
405	147230	Savage Park Improvements	\$ 120,000.00	\$ -	\$ -	\$ 15,313.82	\$ 8,501.87	\$ -	\$ 96,184.31
405	147260	Cousins Park Improvements	\$ 1,975,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,975,000.00
405	147270	Carl Smith Improvements	\$ 185,000.00	\$ -	\$ -	\$ 76,935.35	\$ 7,388.98	\$ -	\$ 100,675.67
405	147300	Chamberlain - Pool Reconstruct	\$ 2,721,207.52	\$ 210,582.25	\$ 1,243,328.68	\$ 1,494,322.81	\$ 955,676.17	\$ -	\$ 271,208.54
405	147400	Lacy - Pool	\$ 2,640,000.00	\$ -	\$ -	\$ 2,634,677.94	\$ 2,450.08	\$ -	\$ 2,871.98
405	147520	Playground Safety Surfaces	\$ 7,300,000.00	\$ -	\$ 1,916.25	\$ 3,513,632.27	\$ 999.88	\$ -	\$ 3,785,367.85
405	148100	Annual Economic Development	\$ 6,675,000.00	\$ -	\$ 303.51	\$ 4,740,342.68	\$ 1,893,628.57	\$ -	\$ 41,028.75
405	148110	Op Ser - Strategic Mobility	\$ 1,500,000.00	\$ -	\$ -	\$ 528,679.00	\$ 20,000.00	\$ -	\$ 951,321.00
405	148120	Op Ser - Corridor & Small Ar	\$ 2,000,000.00	\$ -	\$ 2,056.24	\$ 1,161,564.31	\$ 7,199.00	\$ -	\$ 831,236.69
405	148130	Op Ser - Northland Str. Acq	\$ 5,000,000.00	\$ -	\$ 119,913.70	\$ 2,870,880.66	\$ 5,101.54	\$ 22,988.00	\$ 2,101,029.80
405	148140	Retail and Res Development	\$ 4,000,000.00	\$ -	\$ -	\$ 3,998,400.00	\$ -	\$ -	\$ 1,600.00
405	148150	Pearl District Flood Control	\$ 5,000,000.00	\$ 2,950.00	\$ 130,218.00	\$ 2,839,151.30	\$ -	\$ -	\$ 2,160,848.70
405	148160	Charles Page Boulevard - Plan	\$ 445,000.00	\$ -	\$ 24,000.00	\$ 237,502.33	\$ -	\$ -	\$ 207,497.67
405	148170	Eugene Field Redevelopment	\$ 10,900,000.00	\$ 13,079.20	\$ 195,295.56	\$ 10,004,452.26	\$ 625,109.51	\$ -	\$ 270,438.23
405	148180	Route 66 Restrooms & Parking	\$ 550,000.00	\$ -	\$ -	\$ 524,394.54	\$ -	\$ -	\$ 25,605.46
405	149100	Transit Coach & Lift Match	\$ 14,750,000.00	\$ -	\$ 2,374,704.00	\$ 12,412,162.28	\$ -	\$ -	\$ 2,337,837.72
405	149200	Peoria (Brt) Project	\$ 14,052,005.06	\$ -	\$ 19,349.00	\$ 13,651,409.05	\$ 195.00	\$ -	\$ 400,401.01
405	2036D0008Z	1st 2nd & 4th St Two-Way Conv	\$ 729,020.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 729,020.00
405	2059FR0046	Consulting Services - Match	\$ 70,500.00	\$ -	\$ -	\$ 27,488.00	\$ 27,650.00	\$ -	\$ 15,362.00
405	2125X0001Z	Computer Aided Dispatch (CAD)	\$ 660,000.00	\$ -	\$ -	\$ 659,998.00	\$ -	\$ -	\$ 2.00
405	2132X0001Z	MTTA Parking Lot	\$ 947,994.94	\$ -	\$ -	\$ 689,501.75	\$ -	\$ -	\$ 258,493.19
405	2134B0001Z	Gilcrease Museum Facility Imp	\$ 8,262,134.89	\$ -	\$ -	\$ 8,136,581.57	\$ -	\$ -	\$ 125,553.32

2020 SALES TAX

FUND 409

(2020 SALES TAX FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 409 - 2020 SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Sales Tax	\$ 43,091,720.83	\$ 3,216,028.15	\$ 75,728,100.51	\$ 161,328,552.49	\$ (32,636,379.68)
Donations					
Interest on Investments		4,711.60	948,212.43	1,714,919.09	(948,212.43)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue					
Total Revenue	<u>43,091,720.83</u>	<u>3,220,739.75</u>	<u>76,676,312.94</u>	<u>163,043,471.58</u>	<u>-33,584,592.11</u>
<u>Expenditures</u>					
Project Expenditures	<u>150,506,112.00</u>	<u>2,631,056.59</u>	<u>44,260,528.34</u>	<u>86,865,327.64</u>	<u>63,640,784.36</u>
Total Expenditures	<u>150,506,112.00</u>	<u>2,631,056.59</u>	<u>44,260,528.34</u>	<u>86,865,327.64</u>	<u>63,640,784.36</u>
Excess (Deficiency) of Revenue					
Over Expenditures			32,415,784.60	76,178,143.94	
Completed Projects					
Encumbrances			<u>8,538,350.12</u>	<u>8,538,350.12</u>	
Excess (Deficiency) of Revenue Over					
Expenditures and Encumbrances			23,877,434.48	67,639,793.82	
June 30, 2022 Ending Fund Balance			25,377,927.47		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>18,384,431.87</u>		
Adjusted Beginning Fund Balance			<u>43,762,359.34</u>		
Ending Fund Balance			<u>\$ 67,639,793.82</u>	<u>\$ 67,639,793.82</u>	

2020 SALES TAX

Fund 409

As of: 03/31/2025

\$ 150,556,112.00 \$ 2,631,056.59 \$ 18,667,348.30 \$ 93,596,511.46 \$ 7,689,195.12 \$ 849,155.00 \$ 48,421,250.42

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
409	2215X00001	Capital Equipment	\$ 45,111,112.00	\$ 939,814.83	\$ 8,458,333.47	\$ 42,291,667.47	\$ -	\$ -	\$ 2,819,444.53
409	2225X00013	Fire Apparatus and Equipment	\$ 21,490,000.00	\$ -	\$ 3,338,852.03	\$ 17,305,987.16	\$ 1,075,544.99	\$ 822,860.00	\$ 2,285,607.85
409	2225X00014	911 Station Alert System	\$ 3,000,000.00	\$ 446,892.68	\$ 1,505,094.19	\$ 2,368,352.39	\$ 407,457.05	\$ -	\$ 224,190.56
409	2225X00015	Police Helicopter Replacement	\$ 4,700,000.00	\$ -	\$ -	\$ 4,700,000.00	\$ -	\$ -	\$ -
409	2225X00016	Municipal Lockup Data Storage	\$ 510,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 510,000.00
409	2234B00000	Greenwood Cultural Center Reha	\$ 5,340,000.00	\$ 18,052.54	\$ 32,019.90	\$ 274,203.97	\$ 534,760.56	\$ -	\$ 4,531,035.47
409	2234B00004	Gilcrease Museum Improvements	\$ 6,660,000.00	\$ -	\$ -	\$ 6,660,000.00	\$ -	\$ -	\$ -
409	2234B00006	CW- Public Facilities - Roofs	\$ 1,930,000.00	\$ -	\$ -	\$ 1,064,911.15	\$ -	\$ -	\$ 865,088.85
409	2234B00007	Animal Shelter Phase II	\$ 2,080,000.00	\$ -	\$ -	\$ -	\$ 2,080,000.00	\$ -	\$ -
409	2234B00008	One Technology Center - Maint/	\$ 1,000,000.00	\$ -	\$ -	\$ 26,297.48	\$ -	\$ -	\$ 973,702.52
409	2234B00024	CW - Public Facilities Rehab/R	\$ 4,950,000.00	\$ 23,326.04	\$ 575,817.69	\$ 1,394,637.50	\$ 331,592.87	\$ 26,295.00	\$ 3,197,474.63
409	2234B00025	ADA Imp for City Facilities	\$ 3,000,000.00	\$ 57,300.62	\$ 58,770.62	\$ 64,076.06	\$ 52,411.00	\$ -	\$ 2,883,512.94
409	2234B00029	600 Civic Center - Equip Reloc	\$ 200,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 200,000.00
409	2235X00019	Transit Fleet Replacement	\$ 10,900,000.00	\$ -	\$ -	\$ 1,713,617.80	\$ -	\$ -	\$ 9,186,382.20
409	2236S00002	Parking Facilities	\$ 8,000,000.00	\$ -	\$ -	\$ 8,000,000.00	\$ -	\$ -	\$ -
409	2242P00030	Swan Lake Rehabilitation	\$ 1,700,000.00	\$ 29,562.65	\$ 1,087,047.26	\$ 1,674,260.90	\$ 25,739.10	\$ -	\$ -
409	2242P00031	Hill Park Improvements	\$ 500,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 500,000.00
409	2242P00032	Mohawk Park Rehab and Renovati	\$ 100,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 100,000.00
409	2244B00009	CW - Park Facilities	\$ 7,750,000.00	\$ 140,896.00	\$ 1,480,252.22	\$ 3,112,801.31	\$ 1,292,009.30	\$ -	\$ 3,345,189.39
409	2244B00027	ADA Imp for City Parks	\$ 2,000,000.00	\$ -	\$ -	\$ -	\$ 48,850.00	\$ -	\$ 1,951,150.00
409	2244P00010	CW - Outdoor Park Play Ameniti	\$ 3,600,000.00	\$ 1,049,965.46	\$ 1,234,070.01	\$ 1,234,070.01	\$ 94,456.45	\$ -	\$ 2,271,473.54
409	2244P00011	CW - Tennis Court Rehab/Replac	\$ 2,700,000.00	\$ -	\$ 571,105.39	\$ 838,429.38	\$ 5,752.50	\$ -	\$ 1,855,818.12
409	2244P00012	Fred Johnson Rehab	\$ 3,125,000.00	\$ 59,541.47	\$ 237,749.71	\$ 370,859.04	\$ 470,528.19	\$ -	\$ 2,283,612.77
409	2246S00026	Tulsa Zoo Entrance and Parking	\$ 600,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 600,000.00
409	2246S00027	CW - Park System Parking Rehab	\$ 525,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 525,000.00
409	2258X00017	CW - Eco Devo Infrastructure	\$ 5,200,000.00	\$ -	\$ -	\$ -	\$ 109,447.81	\$ -	\$ 5,090,552.19
409	2259X00018	CW - Commty Dev Priority Proje	\$ 3,885,000.00	\$ (134,295.70)	\$ 88,235.81	\$ 502,339.84	\$ 1,160,645.30	\$ -	\$ 2,222,014.86

2016 VISION TULSA ECONOMIC DEVELOPMENT SALES FUND

FUND 4000

(2016 LIMITED PURPOSE TEMPORARY SALES TAX FUND)

CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4000 - 2016 VISION TULSA ECONOMIC DEVELOPMENT

STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Sales Tax	\$ 74,848,175.00	\$ 5,753,117.03	\$ 103,356,155.29	\$ 403,208,173.47	\$ (28,507,980.29)
Donations					
Interest on Investments		467,618.38	2,245,016.62	5,622,907.76	(2,245,016.62)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue					
Total Revenue	<u>74,848,175.00</u>	<u>6,220,735.41</u>	<u>105,601,171.91</u>	<u>408,831,081.23</u>	<u>-30,752,996.91</u>
<u>Expenditures</u>					
Project Expenditures	<u>399,171,894.98</u>	<u>5,117,759.32</u>	<u>106,297,411.66</u>	<u>329,731,822.55</u>	<u>69,440,072.43</u>
Total Expenditures	<u>399,171,894.98</u>	<u>5,117,759.32</u>	<u>106,297,411.66</u>	<u>329,731,822.55</u>	<u>69,440,072.43</u>
Excess (Deficiency) of Revenue Over Expenditures			(696,239.75)	79,099,258.68	
Completed Projects Encumbrances			<u>5,000,896.90</u>	<u>5,000,896.90</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(5,697,136.65)	74,098,361.78	
June 30, 2023 Ending Fund Balance			77,299,614.67		
Prior year expenditures					
June 30, 2023 Encumbrances			<u>2,495,883.86</u>		
Adjusted Beginning Fund Balance			<u>79,795,498.53</u>		
Ending Fund Balance			<u>\$ 74,098,361.88</u>	<u>\$ 74,098,361.78</u>	

2016 VISION ED CAPITAL PROJ

Fund 4000

As of: 03/31/2025 \$ 399,171,894.98 \$ 5,117,759.32 \$ 43,843,945.34 \$ 330,159,509.89 \$ 4,950,896.90 \$ 50,000.00 \$ 64,011,488.19

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4000	170000	Zink Lake and Related Improvem	\$ 21,690,000.00	\$ 369,610.00	\$ 685,341.96	\$ 21,023,234.00	\$ 415,150.00	\$ -	\$ 251,616.00
4000	170005	Low-Water Dam and Pedestrian B	\$ 26,284,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 26,284,000.00
4000	170010	Turkey Mountain Urban Wilderne	\$ 2,600,000.00	\$ -	\$ -	\$ 2,600,000.00	\$ -	\$ -	\$ -
4000	170015	Levee Dist #12 Rehab (Match)	\$ 5,000,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 5,000,000.00
4000	170020	Trail E Bank 101 Cousins Park	\$ 2,800,000.00	\$ -	\$ -	\$ 2,399,980.41	\$ 400,019.59	\$ -	\$ -
4000	170025	23rd Jackson Redevelop Study	\$ 1,000,000.00	\$ -	\$ -	\$ 762,600.95	\$ 610.71	\$ 50,000.00	\$ 186,788.34
4000	170035	Cox Center & Dist Master Plan	\$ 14,100,000.00	\$ -	\$ -	\$ 14,100,000.00	\$ -	\$ -	\$ -
4000	170060	BMX National Headquarters	\$ 5,801.19	\$ -	\$ 5,681.19	\$ 5,801.19	\$ -	\$ -	\$ -
4000	170065	South Mingo Corridor	\$ 1,000,000.00	\$ -	\$ -	\$ 1,000,000.00	\$ -	\$ -	\$ -
4000	170075	Capital Equip (Non Pub Safety)	\$ 12,000,000.00	\$ 250,000.00	\$ 2,250,000.00	\$ 11,250,000.00	\$ -	\$ -	\$ 750,000.00
4000	170080ENGR	CW & Rt 66 Beaut Rvst_ENGR	\$ 1,762,500.00	\$ 25,950.46	\$ 65,048.90	\$ 65,048.90	\$ 576,860.10	\$ -	\$ 1,120,591.00
4000	170080MOED	CW & Rt 66 Beaut Rvst_MOED	\$ 3,550,000.00	\$ -	\$ -	\$ 2,357,000.00	\$ 500,000.00	\$ -	\$ 693,000.00
4000	170080PLAN	CW & Rt 66 Beaut Rvst_PLAN	\$ 1,882,593.79	\$ 10,498.86	\$ 278,579.61	\$ 1,260,030.02	\$ 199,860.18	\$ -	\$ 422,703.59
4000	170085	Peoria - Mohawk: Business Park	\$ 3,300,000.00	\$ -	\$ -	\$ 1,817,410.02	\$ 1,482,589.98	\$ -	\$ -
4000	170090	Public School Partnership	\$ 10,000,000.00	\$ -	\$ 199,418.67	\$ 7,006,284.09	\$ 1,250,581.34	\$ -	\$ 1,743,134.57
4000	170095	Community Health Connection	\$ 4,570,000.00	\$ -	\$ -	\$ 4,570,000.00	\$ -	\$ -	\$ -
4000	170105	Discovery Lab Site	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
4000	170110	N Peoria Conn 56-Mohawk	\$ 3,100,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,100,000.00
4000	170125	McCullough Park	\$ 3,060,000.00	\$ -	\$ -	\$ 3,059,999.99	\$ -	\$ -	\$ 0.01
4000	170145	Tulsa Arts Commission	\$ 1,200,000.00	\$ -	\$ 71,775.00	\$ 893,964.19	\$ 125,225.00	\$ -	\$ 180,810.81
4000	170155	PAC Improvement Master Plan	\$ 1,000,000.00	\$ -	\$ -	\$ 1,000,000.00	\$ -	\$ -	\$ -
4000	170160	Transfer to TPFA 2017	\$ 279,267,000.00	\$ 4,461,700.00	\$ 40,288,100.01	\$ 254,988,156.13	\$ -	\$ -	\$ 24,278,843.87

2016 VISION ADVANCE FUNDED REVENUE BOND FUND

FUND 4001

(2016 ADVANCE FUNDED BOND FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4001 - 2017 VISION ECONOMIC DEVELOPMENT BOND ISSUE 1**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Bond Sale Receipts	\$	\$	\$	\$ 115,300,000.00	\$
Donations					
Miscellaneous Revenue				3,175,000.00	
Total Revenue				118,475,000.00	
<u>Expenditures</u>					
Project Expenditures	118,475,000.00	589,597.20	873,395.87	115,783,549.27	2,691,450.73
Total Expenditures	118,475,000.00	589,597.20	873,395.87	115,783,549.27	2,691,450.73
Excess (Deficiency) of Revenue Over Expenditures			(873,395.87)	2,691,450.73	
Completed Projects Encumbrances			73.00 <u>1,883,498.23</u>	<u>1,883,498.23</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(2,756,894.10)	807,952.50	
June 30, 2022 Ending Fund Balance			2,373,213.10		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>1,191,633.50</u>		
Adjusted Beginning Fund Balance			3,564,846.60		
Ending Fund Balance			<u>\$ 807,952.50</u>	<u>\$ 807,952.50</u>	

2017 VISION ED ISSUE 1

Fund 4001

As of: **03/31/2025**

\$ 118,475,000.00	\$ 589,597.20	\$ 1,017,171.67	\$ 116,468,060.91	\$ 1,883,498.23	\$ -	\$ 123,440.86
-------------------	---------------	-----------------	-------------------	-----------------	------	---------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4001	170000	Zink Lake and Related Improve	\$ 24,425,000.00	\$ -	\$ 44,571.89	\$ 24,344,434.74	\$ 80,565.26	\$ -	\$ -
4001	170030	Gilcrease Museum Expansion	\$ 1,000,000.00	\$ -	\$ -	\$ 1,000,000.00	\$ -	\$ -	\$ -
4001	170035	Cox Center & Dist Master Plan	\$ 13,250,000.00	\$ -	\$ -	\$ 13,144,135.27	\$ 104,865.74	\$ -	\$ 998.99
4001	170040	Tulsa Fairgrounds	\$ 26,325,000.00	\$ -	\$ -	\$ 26,325,000.00	\$ -	\$ -	\$ -
4001	170045	Airport Infrastructure	\$ 9,100,000.00	\$ -	\$ -	\$ 8,886,530.80	\$ 213,469.20	\$ -	\$ -
4001	170055	Langston Health Complex Exp	\$ 1,800,000.00	\$ -	\$ -	\$ 1,800,000.00	\$ -	\$ -	\$ -
4001	170060	BMX National Headquarters	\$ 1,350,000.00	\$ -	\$ -	\$ 1,350,000.00	\$ -	\$ -	\$ -
4001	170065	South Mingo Corridor	\$ 11,000,000.00	\$ 589,597.20	\$ 959,442.78	\$ 9,493,348.97	\$ 1,484,598.03	\$ -	\$ 22,053.00
4001	170070	Public School Safety First	\$ 5,000,000.00	\$ -	\$ 3,157.00	\$ 4,998,271.75	\$ -	\$ -	\$ 1,728.25
4001	170095	Community Health Connection	\$ 5,405,000.00	\$ -	\$ -	\$ 5,405,000.00	\$ -	\$ -	\$ -
4001	170100	Air National Guard Training Ce	\$ 9,400,000.00	\$ -	\$ 10,000.00	\$ 9,400,000.00	\$ -	\$ -	\$ -
4001	170110	N Peoria Conn 56-Mohawk	\$ 900,000.00	\$ -	\$ -	\$ 900,000.00	\$ -	\$ -	\$ -
4001	170115	TCC Career Placement	\$ 5,320,000.00	\$ -	\$ -	\$ 5,320,000.00	\$ -	\$ -	\$ -
4001	170120	UCAT Auth OSU Tulsa	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
4001	170130	Mohawk Sports Complex	\$ 3,500,000.00	\$ -	\$ -	\$ 3,475,000.00	\$ -	\$ -	\$ 25,000.00
4001	170135	Go Plan Priority Projects	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
4001	170140	Rt 66 Village Train Depot	\$ 400,000.00	\$ -	\$ -	\$ 400,000.00	\$ -	\$ -	\$ -
4001	170150A	2017 Vision ED Issue Costs_1	\$ 300,000.00	\$ -	\$ -	\$ 226,339.38	\$ -	\$ -	\$ 73,660.62

2016 VISION ADVANCE FUNDED REVENUE BOND FUND

FUND 4003

(2016 ADVANCE FUNDED BOND FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4003 - 2017 VISION ECONOMIC DEVELOPMENT BOND ISSUE 2**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Bond Sale Receipts	\$	\$	\$	\$ 118,100,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				118,100,000.00	
<u>Expenditures</u>					
Project Expenditures	118,100,000.00		5,479,292.83	116,287,801.93	1,812,198.07
Total Expenditures	118,100,000.00		5,479,292.83	116,287,801.93	1,812,198.07
Excess (Deficiency) of Revenue Over Expenditures			(5,479,292.83)	1,812,198.07	
Completed Projects Encumbrances			216,564.43	216,564.43	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(5,695,857.26)	1,595,633.64	
June 30, 2022 Ending Fund Balance			1,616,107.21		
Prior year expenditures					
June 30, 2022 Encumbrances			5,675,383.69		
Adjusted Beginning Fund Balance			7,291,490.90		
Ending Fund Balance			\$ 1,595,633.64	\$ 1,595,633.64	

2017 VISION ED ISSUE 2

Fund 4003

As of: 03/31/2025

\$	118,100,000.00	\$	-	\$	82,318.56	\$	117,085,700.31	\$	216,564.43	\$	-	\$	797,735.26
----	----------------	----	---	----	-----------	----	----------------	----	------------	----	---	----	------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4003	170000	Zink Lake and Related Improvem	\$ 16,885,000.00	\$ -	\$ -	\$ 16,885,000.00	\$ -	\$ -	\$ -
4003	170005	Low-Water Dam and Pedestrian B	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
4003	170010	Turkey Mountain Urban Wilderne	\$ 5,000,000.00	\$ -	\$ -	\$ 4,999,980.00	\$ 20.00	\$ -	\$ -
4003	170030	Gilcrease Museum Expansion	\$ 6,000,000.00	\$ -	\$ -	\$ 6,000,000.00	\$ -	\$ -	\$ -
4003	170035	Cox Center & Dist Master Plan	\$ 27,650,000.00	\$ -	\$ -	\$ 27,301,956.98	\$ -	\$ -	\$ 348,043.02
4003	170040	Tulsa Fairgrounds	\$ 3,675,000.00	\$ -	\$ -	\$ 3,675,000.00	\$ -	\$ -	\$ -
4003	170045	Airport Infrastructure	\$ 9,100,000.00	\$ -	\$ -	\$ 9,100,000.00	\$ -	\$ -	\$ -
4003	170050	Tulsa Zoo & Living Museum	\$ 3,000,000.00	\$ -	\$ -	\$ 3,000,000.00	\$ -	\$ -	\$ -
4003	170055	Langston Health Complex Exp	\$ 11,450,000.00	\$ -	\$ -	\$ 11,450,000.00	\$ -	\$ -	\$ -
4003	170060	BMX National Headquarters	\$ 13,650,000.00	\$ -	\$ 37,391.31	\$ 13,458,874.23	\$ -	\$ -	\$ 191,125.77
4003	170070	Public School Safety First	\$ 4,750,000.00	\$ -	\$ -	\$ 4,671,559.38	\$ 78,440.62	\$ -	\$ -
4003	170085	Peoria - Mohawk: Business Park	\$ 2,500,000.00	\$ -	\$ -	\$ 2,500,000.00	\$ -	\$ -	\$ -
4003	170105	Discovery Lab Site	\$ 8,000,000.00	\$ -	\$ -	\$ 8,000,000.00	\$ -	\$ -	\$ -
4003	170110	N Peoria Conn 56-Mohawk	\$ 3,000,000.00	\$ -	\$ 32,927.25	\$ 2,649,820.70	\$ 130,103.81	\$ -	\$ 220,075.49
4003	170125	McCullough Park	\$ 540,000.00	\$ -	\$ -	\$ 540,000.00	\$ -	\$ -	\$ -
4003	170140	Rt 66 Village Train Depot	\$ 2,600,000.00	\$ -	\$ 12,000.00	\$ 2,587,337.93	\$ 8,000.00	\$ -	\$ 4,662.07
4003	170150B	2017 Vision ED Issue Bond Cost	\$ 300,000.00	\$ -	\$ -	\$ 266,171.09	\$ -	\$ -	\$ 33,828.91

2016 VISION ADVANCE FUNDED REVENUE BOND FUND

FUND 4004

(2016 ADVANCE FUNDED BOND FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4004 - 2017 VISION ECONOMIC DEVELOPMENT BOND ISSUE 3**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Bond Sale Receipts	\$	\$	\$	\$ 114,025,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				114,025,000.00	
<u>Expenditures</u>					
Project Expenditures	114,025,000.00	314,661.25	38,664,132.53	96,688,150.55	17,336,849.45
Total Expenditures	114,025,000.00	314,661.25	38,664,132.53	96,688,150.55	17,336,849.45
Excess (Deficiency) of Revenue Over Expenditures			(38,664,132.53)	17,336,849.45	
Completed Projects Encumbrances			8,547,229.72	8,547,229.72	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(47,211,362.25)	8,789,619.73	
June 30, 2022 Ending Fund Balance			21,151,754.78		
Prior year expenditures					
June 30, 2022 Encumbrances			34,849,227.20		
Adjusted Beginning Fund Balance			56,000,981.98		
Ending Fund Balance			\$ 8,789,619.73	\$ 8,789,619.73	

2017 VISION ED ISSUE 3

Fund 4004

As of: 03/31/2025

\$	114,025,000.00	\$	314,661.25	\$	2,175,830.12	\$	100,006,037.39	\$	8,547,229.72	\$	-	\$	5,471,732.89
----	----------------	----	------------	----	--------------	----	----------------	----	--------------	----	---	----	--------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4004	170005	Low-Water Dam and Pedestrian B	\$ 2,800,000.00	\$ 2,700.00	\$ 2,700.00	\$ 1,346,791.12	\$ -	\$ -	\$ 1,453,208.88
4004	170030	Gilcrease Museum Expansion	\$ 58,000,000.00	\$ 307,391.65	\$ 1,604,994.41	\$ 57,139,910.50	\$ 860,089.50	\$ -	\$ -
4004	170045	Airport Infrastructure	\$ 9,100,000.00	\$ -	\$ 182,935.58	\$ 3,805,683.39	\$ 1,334,045.64	\$ -	\$ 3,960,270.97
4004	170050	Tulsa Zoo & Living Museum	\$ 22,000,000.00	\$ 4,569.60	\$ 18,082.05	\$ 21,977,130.86	\$ 22,869.14	\$ -	\$ -
4004	170055	Langston Health Complex Exp	\$ 3,000,000.00	\$ -	\$ -	\$ 3,000,000.00	\$ -	\$ -	\$ -
4004	170060	BMX National Headquarters	\$ 3,600,000.00	\$ -	\$ -	\$ 3,600,000.00	\$ -	\$ -	\$ -
4004	170065	South Mingo Corridor	\$ 3,000,000.00	\$ -	\$ -	\$ -	\$ 3,000,000.00	\$ -	\$ -
4004	170070	Public School Safety First	\$ 4,750,000.00	\$ -	\$ 367,118.08	\$ 3,917,410.16	\$ 832,589.84	\$ -	\$ -
4004	170080MOED	CW & Rt 66 Beaut Reinvestment_	\$ 150,000.00	\$ -	\$ -	\$ -	\$ 140,000.00	\$ -	\$ 10,000.00
4004	170085	Peoria - Mohawk Business Park	\$ 4,200,000.00	\$ -	\$ -	\$ 1,842,364.40	\$ 2,357,635.60	\$ -	\$ -
4004	170135	Go Plan Priority Projects	\$ 3,125,000.00	\$ -	\$ -	\$ 3,125,000.00	\$ -	\$ -	\$ -
4004	170150C	2017 Vision ED Issue Bond Cost	\$ 300,000.00	\$ -	\$ -	\$ 251,746.96	\$ -	\$ -	\$ 48,253.04

2014 GO BOND FUNDS

FUND 4270~4277 COMBINED

(2014 GENERAL OBLIGATION BOND FUNDS)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4270-4276 - 2014 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Bond Sale Receipts	\$	\$	\$	\$ 313,615,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				313,615,000.00	
<u>Expenditures</u>					
Project Expenditures	355,000,000.00	1,450,548.03	27,059,930.65	256,701,167.64	98,298,832.36
Total Expenditures	355,000,000.00	1,450,548.03	27,059,930.65	256,701,167.64	98,298,832.36
Excess (Deficiency) of Revenue Over Expenditures			(27,059,930.65)	56,913,832.36	
Completed Projects				42,576,919.00	
Encumbrances			31,179,520.32	31,179,520.32	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(58,239,450.97)	(16,842,606.96)	
June 30, 2022 Ending Fund Balance			7,354,342.68		
Prior year expenditures					
June 30, 2022 Encumbrances			34,042,501.33		
Adjusted Beginning Fund Balance			41,396,844.01		
Ending Fund Balance			\$ -16,842,606.96	\$ -16,842,606.96	

2014 GO BOND PROGRAM

Fund 427

As of: 03/31/2025

\$ 355,000,000.00 \$ 1,450,548.03 \$ 13,164,461.73 \$ 275,537,498.44 \$ 31,179,520.32 \$ - \$ 48,282,981.24

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4270	144021	Citywide-Nonarterial Rt&Pv M	\$ 1,973,927.51	\$ -	\$ 46.65	\$ 1,942,455.03	\$ 31,472.48	\$ -	\$ -
4270	144106	Maintenance Zone 1006	\$ 400,000.00	\$ -	\$ -	\$ 385,556.47	\$ -	\$ -	\$ 14,443.53
4270	144153	Maintenance Zone 1153	\$ 410,000.00	\$ -	\$ -	\$ 406,531.50	\$ 3,468.50	\$ -	\$ -
4270	144219	Maintenance Zone 2119	\$ 40,000.00	\$ -	\$ -	\$ 38,500.00	\$ -	\$ -	\$ 1,500.00
4270	144255	Maintenance Zone 2055	\$ 150,000.00	\$ -	\$ -	\$ 148,972.24	\$ -	\$ -	\$ 1,027.76
4270	144265	Maintenance Zone 2065	\$ 100,000.00	\$ -	\$ -	\$ 98,763.93	\$ -	\$ -	\$ 1,236.07
4270	144309	Citywide - Arterial Rehab	\$ 276,489.24	\$ 32,783.25	\$ 33,148.25	\$ 228,762.74	\$ 47,726.50	\$ -	\$ -
4270	144533	Maintenance Zone 5033	\$ 500,000.00	\$ -	\$ -	\$ 499,987.32	\$ -	\$ -	\$ 12.68
4270	144944	Maintenance Zone 9044	\$ 400,000.00	\$ -	\$ 3,913.20	\$ 344,695.90	\$ -	\$ -	\$ 55,304.10
4270	144945	Maintenance Zone 9045	\$ 400,000.00	\$ -	\$ -	\$ 370,356.98	\$ -	\$ -	\$ 29,643.02
4271	144094	ODOT Rehab & Replacement	\$ 1,640,000.00	\$ -	\$ -	\$ 1,630,372.20	\$ 9,627.80	\$ -	\$ -
4271	144111	Maintenance Zone 1001	\$ 830,000.00	\$ -	\$ 12,547.27	\$ 822,334.73	\$ 7,665.27	\$ -	\$ -
4271	144158	Maintenance Zone 1157	\$ 219,643.46	\$ -	\$ -	\$ 211,448.65	\$ -	\$ -	\$ 8,194.81
4271	144199	Maintenance Zone 1099	\$ 320,000.00	\$ -	\$ -	\$ 316,395.78	\$ 3,604.22	\$ -	\$ -
4271	144201	Apache St: Mlk - Peoria	\$ 2,410,000.00	\$ -	\$ -	\$ 2,370,000.00	\$ -	\$ -	\$ 40,000.00
4271	144204	S33rd W: 41st St to 51st St	\$ 2,455,000.00	\$ -	\$ -	\$ 1,672,426.47	\$ -	\$ -	\$ 782,573.53
4271	144208	11th St: Sheridan - Memorial	\$ 1,600,000.00	\$ -	\$ -	\$ 1,445,764.67	\$ -	\$ -	\$ 154,235.33
4271	144212	51st St Sheridan to Memorial	\$ 915,651.29	\$ -	\$ -	\$ 907,661.29	\$ -	\$ -	\$ 7,990.00
4271	144216	41st St: Lewis to Harvard	\$ 2,455,000.00	\$ -	\$ -	\$ 2,446,437.50	\$ 1,425.50	\$ -	\$ 7,137.00
4271	144309	Citywide - Arterial Rehab	\$ 4,182,972.41	\$ -	\$ 20,885.23	\$ 4,135,562.22	\$ 47,410.19	\$ -	\$ -
4271	144318	Maintenance Zone 3018	\$ 367,056.72	\$ -	\$ -	\$ 365,498.17	\$ -	\$ -	\$ 1,558.55
4271	144431	Maintenance Zone 4031	\$ 1,200,000.00	\$ -	\$ -	\$ 1,164,794.00	\$ -	\$ -	\$ 35,206.00
4271	144635	Maintenance Zone 6035	\$ 272,007.76	\$ -	\$ -	\$ 270,496.59	\$ -	\$ -	\$ 1,511.17
4272	144311	Maintenance Zone 3011	\$ 1,000,000.00	\$ -	\$ -	\$ 970,762.05	\$ -	\$ -	\$ 29,237.95
4272	144740	Maintenance Zone 7040	\$ 350,000.00	\$ -	\$ -	\$ 349,845.00	\$ -	\$ -	\$ 155.00
4273	144093	Citywide Matching Funds	\$ 1,753,170.00	\$ 239.25	\$ 239.25	\$ 1,738,092.76	\$ 14,966.49	\$ -	\$ 110.75
4273	144213	91st Harvard - Yale	\$ 285,000.00	\$ 16,033.29	\$ 56,598.83	\$ 232,602.01	\$ 12,942.49	\$ -	\$ 39,455.50
4273	144217	Apache & Harvard Intersect	\$ 785,000.00	\$ -	\$ -	\$ 775,000.00	\$ 8,390.00	\$ -	\$ 1,610.00
4273	144225	Maintenance Zone 2125	\$ 2,310,000.00	\$ -	\$ -	\$ 2,262,500.00	\$ -	\$ -	\$ 47,500.00
4273	144452	Maintenance Zone 4152	\$ 600,000.00	\$ -	\$ 983.83	\$ 403,908.06	\$ 107,856.79	\$ -	\$ 88,235.15
4273	144467	Maintenance Zone 4067	\$ 4,370,000.00	\$ 239,242.18	\$ 520,208.22	\$ 3,407,583.33	\$ 960,452.63	\$ -	\$ 1,964.04
4273	144645	Maintenance Zone 6145	\$ 2,375,000.00	\$ -	\$ -	\$ 2,329,034.10	\$ 18,488.01	\$ -	\$ 27,477.89
4273	144700	Maintenance Zone 7100	\$ 1,012,395.47	\$ -	\$ -	\$ 1,012,395.47	\$ -	\$ -	\$ -
4273	144748	Maintenance Zone 7048	\$ 955,111.36	\$ -	\$ -	\$ 955,111.36	\$ -	\$ -	\$ -
4273	144754	Maintenance Zone 7054	\$ 1,000,000.00	\$ -	\$ 35,858.77	\$ 763,369.17	\$ 152,683.83	\$ -	\$ 83,947.00
4273	144857	Maintenance Zone 8057	\$ 1,453,081.00	\$ -	\$ -	\$ 1,453,081.00	\$ -	\$ -	\$ -
4273	144863	Maintenance Zone 8063	\$ 800,000.00	\$ 4,781.38	\$ 34,170.60	\$ 772,569.48	\$ 26,622.97	\$ -	\$ 807.55
4273	144944	Maintenance Zone 9044	\$ 2,295,000.00	\$ -	\$ -	\$ 2,295,000.00	\$ -	\$ -	\$ -
4273	144945	Maintenance Zone 9045	\$ 3,460,000.00	\$ -	\$ -	\$ 3,011,446.11	\$ -	\$ -	\$ 448,553.89
4273	144949	Maintenance Zone 9049	\$ 1,200,000.00	\$ 16,410.28	\$ 68,605.21	\$ 813,098.05	\$ 46,457.29	\$ -	\$ 340,444.66
4274	144094	ODOT Rehab & Replacement	\$ 3,280,000.00	\$ 264,014.75	\$ 292,270.15	\$ 662,002.47	\$ 1,517,121.72	\$ -	\$ 1,100,875.81

2014 GO BOND PROGRAM

Fund 427

As of: 03/31/2025

\$ 355,000,000.00 \$ 1,450,548.03 \$ 13,164,461.73 \$ 275,537,498.44 \$ 31,179,520.32 \$ - \$ 48,282,981.24

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4274	144106	Maintenance Zone 1006	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
4274	144111	Maintenance Zone 1001	\$ 7,445,000.00	\$ -	\$ 1,199,211.83	\$ 7,282,673.56	\$ 37,331.12	\$ -	\$ 124,995.32
4274	144153	Maintenance Zone 1153	\$ 1,243,000.00	\$ -	\$ -	\$ 1,243,000.00	\$ -	\$ -	\$ -
4274	144199	Maintenance Zone 1099	\$ 2,800,000.00	\$ -	\$ -	\$ 2,382,948.30	\$ 47,738.62	\$ -	\$ 369,313.08
4274	144200	36 St: N MLK - Peoria Ave	\$ 2,920,000.00	\$ -	\$ -	\$ 2,919,920.00	\$ -	\$ -	\$ 80.00
4274	144205	Apache St: Lewis To Harvard	\$ 1,860,000.00	\$ -	\$ -	\$ 1,504,705.50	\$ -	\$ -	\$ 355,294.50
4274	144209	21st St: Garnett to 129th E	\$ 2,435,000.00	\$ -	\$ -	\$ 2,018,270.64	\$ -	\$ -	\$ 416,729.36
4274	144210	21st St-129th East Ave INTERSC	\$ 1,965,000.00	\$ -	\$ -	\$ 1,828,247.11	\$ -	\$ -	\$ 136,752.89
4274	144217	Apache & Harvard INTERSCTN	\$ 990,000.00	\$ -	\$ -	\$ 880,980.76	\$ -	\$ -	\$ 109,019.24
4274	144230	Maintenance Zone 2130	\$ 3,488,081.00	\$ -	\$ -	\$ 3,291,788.46	\$ -	\$ -	\$ 196,292.54
4274	144309	Citywide - Arterial Rehab	\$ 1,800,000.00	\$ 58,614.19	\$ 558,981.82	\$ 1,312,554.23	\$ 487,445.77	\$ -	\$ -
4274	144310	Maintenance Zone 3010	\$ 145,714.88	\$ -	\$ 14,800.44	\$ 110,183.72	\$ 32,611.16	\$ -	\$ 2,920.00
4274	144311	Maintenance Zone 3011	\$ 8,485,000.00	\$ -	\$ -	\$ 6,962,932.59	\$ 19,089.00	\$ -	\$ 1,502,978.41
4274	144320	Maintenance Zone 3020	\$ 4,020,000.00	\$ -	\$ -	\$ 68,755.05	\$ 1,957,831.65	\$ -	\$ 1,993,413.30
4274	144431	Maintenance Zone 4031	\$ 10,480,000.00	\$ -	\$ 481.22	\$ 10,164,904.22	\$ -	\$ -	\$ 315,095.78
4274	144547	Maintenance Zone 5047	\$ 2,905,000.00	\$ -	\$ 233,688.20	\$ 2,712,912.25	\$ 192,087.75	\$ -	\$ -
4274	144628	Maintenance Zone 6028	\$ 6,984,285.12	\$ -	\$ 669,990.93	\$ 2,973,694.68	\$ 2,487,550.00	\$ -	\$ 1,523,040.44
4274	144740	Maintenance Zone 7040	\$ 2,925,000.00	\$ -	\$ -	\$ 2,875,000.00	\$ 48,693.75	\$ -	\$ 1,306.25
4274	144857	Maintenance Zone 8057	\$ 841,919.00	\$ -	\$ -	\$ 415,001.81	\$ 53,724.61	\$ -	\$ 373,192.58
4274	144944	Maintenance Zone 9044	\$ 1,305,000.00	\$ -	\$ -	\$ 1,270,831.97	\$ 28,899.07	\$ -	\$ 5,268.96
4274	144951	Maintenance Zone 9051	\$ 1,390,000.00	\$ -	\$ 1,524.50	\$ 1,223,189.45	\$ 95,209.45	\$ -	\$ 71,601.10
4275	144000	Bond Issuance Costs	\$ 48,000.00	\$ -	\$ 305.06	\$ 48,000.00	\$ -	\$ -	\$ -
4275	144153	Maintenance Zone 1153	\$ 2,367,000.00	\$ -	\$ -	\$ 2,366,707.94	\$ 292.06	\$ -	\$ -
4275	144168	Maintenance Zone 1068	\$ 3,200,000.00	\$ 7,914.79	\$ 785,050.76	\$ 1,101,805.63	\$ 37,768.63	\$ -	\$ 2,060,425.74
4275	144202	Apache: Peoria - Lewis Ave	\$ 2,365,000.00	\$ -	\$ 1,405.92	\$ 135,168.77	\$ 1,809,196.54	\$ -	\$ 420,634.69
4275	144215	Peoria: 41st - 51st	\$ 2,885,000.00	\$ -	\$ 265,394.96	\$ 2,880,120.00	\$ 4,880.00	\$ -	\$ -
4275	144421	Maintenance Zone 4021	\$ 3,280,000.00	\$ -	\$ 209,776.37	\$ 2,864,082.65	\$ 1,143.68	\$ -	\$ 414,773.67
4275	144547	Maintenance Zone 5047	\$ 6,465,000.00	\$ 6,987.24	\$ 3,585,768.04	\$ 3,740,396.00	\$ 576,312.80	\$ -	\$ 2,148,291.20
4275	144863	Maintenance Zone 8063	\$ 5,820,000.00	\$ -	\$ 354,612.26	\$ 2,426,440.41	\$ 2,882,538.32	\$ -	\$ 511,021.27
4275	144950	Maintenance Zone 9050	\$ 2,625,000.00	\$ -	\$ -	\$ 2,625,000.00	\$ -	\$ -	\$ -
4276	144000	Bond Issuance Cost	\$ 25,000.00	\$ -	\$ 25,000.00	\$ 25,000.00	\$ -	\$ -	\$ -
4276	144310	Maintenance Zone 3010	\$ 7,060,000.00	\$ 300,657.45	\$ 2,178,794.13	\$ 2,179,357.23	\$ 2,591,431.40	\$ -	\$ 2,289,211.37
4277	144000	Bond Issuance Cost	\$ 20,000.00	\$ -	\$ 584.45	\$ 20,000.00	\$ -	\$ -	\$ -
4277	144207	11th St - Lewis Ave to Harvard	\$ 1,970,000.00	\$ 91,680.07	\$ 451,705.85	\$ 464,345.77	\$ 1,505,654.23	\$ -	\$ -
4277	144213	91st Harvard - Yale	\$ 50,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 50,000.00
4278	144213	91st Harvard - Yale	\$ 2,505,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,505,000.00
4278	144317	Maintenance Zone 3017	\$ 5,050,000.00	\$ -	\$ -	\$ -	\$ 46,650.08	\$ -	\$ 5,003,349.92
4278	144452	Maintenance Zone 4152	\$ 3,895,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,895,000.00
4278	144546	Maintenance Zone 5046	\$ 5,410,000.00	\$ -	\$ 473.41	\$ 473.41	\$ 3,703,652.23	\$ -	\$ 1,705,874.36
4278	144754	Maintenance Zone 7054	\$ 7,635,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 7,635,000.00
4278	144949	Maintenance Zone 9049	\$ 8,795,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 8,795,000.00

2020 GO BOND FUNDS

FUND 4281~4284 COMBINED

(2020 GENERAL OBLIGATION BOND FUNDS)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4281-4285 - 2020 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Bond Sale Receipts	\$	\$	\$	\$ 149,015,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				149,015,000.00	
<u>Expenditures</u>					
Project Expenditures	224,405,000.00	886,776.30	36,146,840.57	60,645,989.56	163,759,010.44
Total Expenditures	224,405,000.00	886,776.30	36,146,840.57	60,645,989.56	163,759,010.44
Excess (Deficiency) of Revenue Over Expenditures			(36,146,840.57)	88,369,010.44	
Completed Projects Encumbrances			32,265,429.34	59,030,000.00 32,265,429.34	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(68,412,269.91)	(2,926,418.90)	
June 30, 2022 Ending Fund Balance			39,441,334.32		
Prior year expenditures					
June 30, 2022 Encumbrances			26,044,516.69		
Adjusted Beginning Fund Balance			65,485,851.01		
Ending Fund Balance			\$ -2,926,418.90	\$ -2,926,418.90	

2020 GO BOND PROGRAM

Fund 428

As of: 03/31/2025

\$	224,405,000.00	\$	886,776.30	\$	23,018,680.10	\$	83,475,536.49	\$	31,865,429.34	\$	400,000.00	\$	108,664,034.17
----	----------------	----	------------	----	---------------	----	---------------	----	---------------	----	------------	----	----------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4282	2036X0005Z	TE: Signal Coord and Communica	\$ 210,000.00	\$ -	\$ -	\$ -	\$ 210,000.00	\$ -	\$ -
4282	2036X0006Z	TE: Signal Instal, Repair and	\$ 630,000.00	\$ 5,469.51	\$ 326,129.75	\$ 416,554.99	\$ 37,298.88	\$ 176,146.13	\$ -
4283	2036A0031Z	Delaware Ave: 81st St S - 91st	\$ 1,250,000.00	\$ -	\$ 487,201.28	\$ 918,219.99	\$ 1,376.00	\$ -	\$ 330,404.01
4283	2036A0033Z	Harvard Ave-71st St to 81st St	\$ 150,000.00	\$ -	\$ -	\$ -	\$ 135,484.00	\$ -	\$ 14,516.00
4283	2036A0042Z	Pine St: Lewis Ave - Harvard A	\$ 410,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 410,000.00
4283	2036A0043Z	Pine St: State Hwy 11 - Mingo	\$ 375,000.00	\$ -	\$ 337,116.00	\$ 337,116.00	\$ -	\$ -	\$ 37,884.00
4283	2036A0054Z	129th E Ave-36th St N to Apach	\$ 200,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 200,000.00
4283	2036A0065Z	11th St S: Harvard Ave - Yale	\$ 700,000.00	\$ -	\$ 700,000.00	\$ 700,000.00	\$ -	\$ -	\$ -
4283	2036A0075Z	21st St S & Harvard Intersect	\$ 150,000.00	\$ 5,389.41	\$ 95,825.73	\$ 129,034.32	\$ 1,465.68	\$ -	\$ 19,500.00
4283	2036A0083Z	Sheridan Rd-41st St to 51st St	\$ 750,000.00	\$ 74,614.16	\$ 187,215.72	\$ 187,215.72	\$ 176,134.28	\$ -	\$ 386,650.00
4283	2036A0088Z	11th St S-161st to 177th	\$ 100,000.00	\$ -	\$ -	\$ 54,451.79	\$ -	\$ -	\$ 45,548.21
4283	2036A0100Z	11th St S & 177th E Intersect	\$ 75,000.00	\$ -	\$ -	\$ 14,001.89	\$ -	\$ -	\$ 60,998.11
4283	2036A0109Z	Memorial Dr-51st St S 61st St	\$ 437,996.00	\$ -	\$ 40,730.53	\$ 340,138.90	\$ 97,857.10	\$ -	\$ -
4283	2036A0110Z	Mingo Rd: 61st St S - 71st St	\$ 460,000.00	\$ -	\$ 460,000.00	\$ 460,000.00	\$ -	\$ -	\$ -
4283	2036A0118Z	Yale Ave-111th St to 121st St	\$ 150,000.00	\$ 2,352.87	\$ 17,272.12	\$ 17,272.12	\$ 51,206.28	\$ -	\$ 81,521.60
4283	2036A0121Z	111th St S & Yale Ave Intersec	\$ 50,000.00	\$ -	\$ 15,031.85	\$ 15,031.85	\$ -	\$ -	\$ 34,968.15
4283	2036A1000Z	CW Arterial Routine & Preventi	\$ 2,900,000.00	\$ 4,981.00	\$ 582,517.70	\$ 2,288,140.77	\$ 611,859.23	\$ -	\$ -
4283	2036D0003Z	CBD: Cincinnati Ave	\$ 250,000.00	\$ 28,839.16	\$ 91,444.34	\$ 91,444.34	\$ 158,555.66	\$ -	\$ -
4283	2036D0006Z	CBD: Lansing Ave	\$ 395,970.00	\$ -	\$ -	\$ 80,000.00	\$ -	\$ -	\$ 315,970.00
4283	2036D0007Z	CBD: Alleyways	\$ 200,000.00	\$ -	\$ -	\$ 105,019.29	\$ 59,542.90	\$ -	\$ 35,437.81
4283	2036D0008Z	1st 2nd & 4th St Two-Way Conv	\$ 250,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 250,000.00
4283	2036N0001Z	CW NonArterial Routine & Preve	\$ 8,000,000.00	\$ -	\$ 1,513,463.96	\$ 7,476,495.40	\$ 523,504.60	\$ -	\$ -
4283	2036N1068Z	Maintenance Zone 1068	\$ 300,000.00	\$ 18,688.47	\$ 18,688.47	\$ 18,688.47	\$ 169,989.67	\$ -	\$ 111,321.86
4283	2036N1071Z	Maintenance Zone 1071	\$ 180,000.00	\$ 90,091.27	\$ 90,091.27	\$ 90,091.27	\$ 8,390.67	\$ -	\$ 81,518.06
4283	2036N1072Z	Maintenance Zone 1072	\$ 300,000.00	\$ -	\$ 32,619.13	\$ 149,225.18	\$ 17,386.82	\$ -	\$ 133,388.00
4283	2036N1097Z	Maintenance Zone 1097	\$ 382,833.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 382,833.00
4283	2036N1155Z	Maintenance Zone 1155	\$ 435,000.00	\$ -	\$ 310.96	\$ 310.96	\$ 282,957.95	\$ -	\$ 151,731.09
4283	2036N2065Z	Maintenance Zone 2065	\$ 3,440,000.00	\$ -	\$ 396,383.10	\$ 2,206,982.04	\$ -	\$ -	\$ 1,233,017.96
4283	2036N2066Z	Maintenance Zone 2066	\$ 1,035,000.00	\$ -	\$ 386,404.26	\$ 386,404.26	\$ 116,046.04	\$ -	\$ 532,549.70
4283	2036N3004Z	Maintenance Zone 3004	\$ 150,000.00	\$ -	\$ 3,025.00	\$ 68,122.50	\$ 81,877.50	\$ -	\$ -
4283	2036N3005Z	Maintenance Zone 3005	\$ 350,000.00	\$ 2,464.20	\$ 62,600.72	\$ 62,600.72	\$ 120,947.54	\$ -	\$ 166,451.74
4283	2036N3011Z	Maintenance Zone 3011	\$ 325,000.00	\$ -	\$ -	\$ -	\$ 221,677.00	\$ -	\$ 103,323.00
4283	2036N3017Z	Maintenance Zone 3017	\$ 300,000.00	\$ -	\$ 94,848.86	\$ 121,711.39	\$ 43,088.61	\$ -	\$ 135,200.00
4283	2036N4015Z	Maintenance Zone 4015	\$ 100,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 100,000.00
4283	2036N4022Z	Maintenance Zone 4022	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
4283	2036N4023Z	Maintenance Zone 4023	\$ 415,000.00	\$ -	\$ -	\$ -	\$ 407,337.54	\$ -	\$ 7,662.46
4283	2036N5040Z	Maintenance Zone 5040	\$ 680,000.00	\$ 364.25	\$ 46,636.72	\$ 607,826.21	\$ 4,031.57	\$ -	\$ 68,142.22
4283	2036N6035Z	Maintenance Zone 6035	\$ 1,020,000.00	\$ -	\$ 111,177.50	\$ 164,879.32	\$ 623,114.75	\$ -	\$ 232,005.93
4283	2036N6142Z	Maintenance Zone 6142	\$ 800,000.00	\$ -	\$ 5,065.24	\$ 431,240.29	\$ 3,934.76	\$ -	\$ 364,824.95
4283	2036N6149Z	Maintenance Zone 6149	\$ 200,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 200,000.00
4283	2036N6150Z	Maintenance Zone 6150	\$ 450,000.00	\$ -	\$ 16,868.22	\$ 185,059.36	\$ 31,637.64	\$ -	\$ 233,303.00
4283	2036N7048Z	Maintenance Zone 7048	\$ 3,451,197.00	\$ 281,172.28	\$ 747,207.19	\$ 747,207.24	\$ 1,063,230.30	\$ -	\$ 1,640,759.46
4283	2036N7109Z	Maintenance Zone 7109	\$ 175,000.00	\$ -	\$ -	\$ 66,337.68	\$ 28,614.11	\$ -	\$ 80,048.21
4283	2036N8057Z	Maintenance Zone 8057	\$ 1,700,000.00	\$ -	\$ 2,209.34	\$ 1,331,218.11	\$ -	\$ -	\$ 368,781.89

2020 GO BOND PROGRAM

Fund 428

As of: 03/31/2025

\$	224,405,000.00	\$	886,776.30	\$	23,018,680.10	\$	83,475,536.49	\$	31,865,429.34	\$	400,000.00	\$	108,664,034.17
----	----------------	----	------------	----	---------------	----	---------------	----	---------------	----	------------	----	----------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4283	2036N8116Z	Maintenance Zone 8116	\$ 100,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 100,000.00
4283	2036N9037Z	Maintenance Zone 9037	\$ 1,780,000.00	\$ -	\$ 248,900.34	\$ 249,982.74	\$ 1,120,893.93	\$ -	\$ 409,123.33
4283	2036N9045Z	Maintenance Zone 9045	\$ 500,000.00	\$ -	\$ 465,693.89	\$ 467,784.50	\$ 20,889.35	\$ -	\$ 11,326.15
4283	2036N9050Z	Maintenance Zone 9050	\$ 1,200,000.00	\$ -	\$ 650,943.93	\$ 842,915.90	\$ 346,402.56	\$ -	\$ 10,681.54
4283	2036N9051Z	Maintenance Zone 9051	\$ 960,000.00	\$ -	\$ 525,090.02	\$ 525,673.42	\$ 208,189.29	\$ -	\$ 226,137.29
4283	2036S0001Z	ADA: Sidewalk Corridors	\$ 1,270,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,270,000.00
4283	2036S0002Z	BPI: Go Plan Implement - ENG	\$ 1,034,587.00	\$ 96,115.43	\$ 162,761.37	\$ 190,819.37	\$ 104,493.46	\$ -	\$ 739,274.17
4283	2036S0003Z	BPI: Go Plan Implement - Traff	\$ 15,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 15,000.00
4283	2036W0001Z	Gilcrease Rd: Pine St - Admira	\$ 9,000,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 9,000,000.00
4283	2036W0002Z	81st St S-Tacoma to Maybelle	\$ 900,000.00	\$ 5,699.14	\$ 13,788.72	\$ 44,380.05	\$ 6,989.09	\$ -	\$ 848,630.86
4283	2036W0003Z	81st St S & Elwood Intersect	\$ 755,000.00	\$ -	\$ 94,951.64	\$ 94,951.64	\$ 383,548.36	\$ -	\$ 276,500.00
4283	2036X0002Z	ADA: Transit Stops	\$ 70,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 70,000.00
4283	2036X0003Z	ADA: Signalized Intersections	\$ 460,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 460,000.00
4283	2036X0004Z	CW Infrastructure Partnership	\$ 700,413.00	\$ -	\$ -	\$ 461,963.00	\$ 5,997.35	\$ -	\$ 232,452.65
4283	2036X0005Z	TE: Signal Coord and Communica	\$ 210,000.00	\$ -	\$ -	\$ -	\$ 210,000.00	\$ -	\$ -
4283	2036X0006Z	TE: Signal Instal, Repair and	\$ 630,000.00	\$ -	\$ -	\$ -	\$ -	\$ 223,853.87	\$ 406,146.13
4283	2036X0007Z	TE: Traffic Calming	\$ 105,000.00	\$ -	\$ 80,213.15	\$ 88,373.08	\$ -	\$ -	\$ 16,626.92
4283	2036X0008Z	TE: Lighting Repair and Replac	\$ 210,000.00	\$ 10,720.47	\$ 37,130.36	\$ 67,109.38	\$ 78,388.83	\$ -	\$ 64,501.79
4283	2036X0009Z	TE: Pavement Markings and Sign	\$ 790,000.00	\$ -	\$ 488,985.10	\$ 770,984.89	\$ -	\$ -	\$ 19,015.11
4283	2036X0010Z	TE: Guardrail Repair and Repl	\$ 105,000.00	\$ -	\$ 105,000.00	\$ 105,000.00	\$ -	\$ -	\$ -
4283	2037B1000Z	CW Bridge Rehab and Inspection	\$ 100,000.00	\$ -	\$ -	\$ 2,847.00	\$ 97,153.00	\$ -	\$ -
4284	2036A1000Z	Citywide Arterial Routine and	\$ 2,999,914.00	\$ -	\$ 1,216,740.15	\$ 1,216,740.15	\$ 675,948.58	\$ -	\$ 1,107,225.27
4284	2036N0001Z	Citywide Non-Arterial Routine	\$ 6,560,000.00	\$ -	\$ 1,638,862.59	\$ 2,714,491.80	\$ 2,824,933.96	\$ -	\$ 1,020,574.24
4284	2036S0001Z	Citywide ADA Transition Plan	\$ 632,859.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 632,859.00
4284	2036S0003Z	BPI: Go Plan Implement - Traff	\$ 15,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 15,000.00
4284	2036S0004Z	Bicycle/Pedestrian Infrastruct	\$ 250,000.00	\$ -	\$ -	\$ 129,267.82	\$ 50,000.00	\$ -	\$ 70,732.18
4284	2036S0005Z	Bicycle/Pedestrian Infrastruct	\$ 75,000.00	\$ -	\$ 41,089.00	\$ 41,089.00	\$ 30,420.46	\$ -	\$ 3,490.54
4284	2036X0003Z	Citywide ADA Transition Plan	\$ 460,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 460,000.00
4284	2036X0004Z	Citywide Infrastructure Partne	\$ 1,832,227.00	\$ -	\$ 240,279.04	\$ 896,383.31	\$ 935,843.69	\$ -	\$ -
4284	2036X0005Z	Traffic Engineering - Signal C	\$ 200,000.00	\$ -	\$ 191,725.71	\$ 191,725.71	\$ 8,274.29	\$ -	\$ -
4284	2036X0006Z	Traffic Engineering - Signal	\$ 600,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 600,000.00
4284	2036X0007Z	Traffic Engineering - Traffic	\$ 30,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 30,000.00
4284	2036X0008Z	Traffic Engineering - Lighting	\$ 270,000.00	\$ -	\$ -	\$ -	\$ 250,000.00	\$ -	\$ 20,000.00
4284	2036X0009Z	Traffic Engineering - Pavement	\$ 750,000.00	\$ -	\$ 3,090.27	\$ 3,090.27	\$ 396,909.73	\$ -	\$ 350,000.00
4284	2036X0010Z	Traffic Engineering - Guardrai	\$ 240,000.00	\$ -	\$ 125,277.38	\$ 125,934.36	\$ -	\$ -	\$ 114,065.64
4284	2039X0009Z	Traffic Engineering - Traffic	\$ 40,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 40,000.00
4285	2036N1007Z	Maintenance Zone 1007	\$ 1,010,000.00	\$ -	\$ -	\$ -	\$ 1,010,000.00	\$ -	\$ -
4285	2036N4022Z	Maintenance Zone 4022	\$ 3,148,803.00	\$ 15,104.35	\$ 44,120.11	\$ 44,120.11	\$ 28,679.89	\$ -	\$ 3,076,003.00
4285	2036N4029Z	Maintenance Zone 4029	\$ 200,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 200,000.00
4285	2036N5026Z	Maintenance Zone 5026	\$ 210,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 210,000.00
4285	2036W0004Z	91 St S: Memorial - Mingo Rd W	\$ 8,500,000.00	\$ -	\$ -	\$ -	\$ 1,602,386.88	\$ -	\$ 6,897,613.12
4285	2036X0003Z	ADA: Signalized Intersections	\$ 460,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 460,000.00
4285	2036X0004Z	CW Infrastructure Partnership	\$ 427,409.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 427,409.00

2024 GO BOND FUNDS

FUNDS 4291~4296 COMBINED

(2024 GENERAL OBLIGATION BOND FUNDS)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4291-4296 - 2024 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE NINE MONTHS ENDED MARCH 31, 2025**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Bond Sale Receipts	\$ 87,610,000.00		\$ 87,610,000.00	\$ 87,610,000.00	
Donations					
Miscellaneous Revenue					
Total Revenue	<u>87,610,000.00</u>		<u>87,610,000.00</u>	<u>87,610,000.00</u>	
<u>Expenditures</u>					
Project Expenditures	<u>156,285,000.00</u>	<u>1,415,344.19</u>	<u>41,884,591.40</u>	<u>41,884,591.40</u>	<u>114,400,408.60</u>
Total Expenditures	<u>156,285,000.00</u>	<u>1,415,344.19</u>	<u>41,884,591.40</u>	<u>41,884,591.40</u>	<u>114,400,408.60</u>
Excess (Deficiency) of Revenue Over Expenditures			45,725,408.60	45,725,408.60	
Completed Projects Encumbrances			<u>8,660,922.03</u>	<u>8,660,922.03</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			37,064,486.57	37,064,486.57	
June 30, 2022 Ending Fund Balance					
Prior year expenditures					
June 30, 2022 Encumbrances					
Adjusted Beginning Fund Balance					
Ending Fund Balance			\$ <u>37,064,486.57</u>	\$ <u>37,064,486.57</u>	

2024 GO BOND PROGRAM

Fund 429

As of: 03/31/2025

\$	156,285,000.00	\$	1,415,344.19	\$	38,921,456.16	\$	44,900,337.41	\$	8,310,922.03	\$	350,000.00	\$	102,723,740.56
----	----------------	----	--------------	----	---------------	----	---------------	----	--------------	----	------------	----	----------------

Fund	Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumbrances	Committed	Balance
4291	2419X0011Z	Bond Issuance Cost	\$ 160,000.00	\$ -	\$ 2,406.03	\$ 160,000.00	\$ -	\$ -	\$ -
4291	2436A0002Z	CW Arterial Streets R&R	\$ 3,300,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,300,000.00
4291	2436N0002Z	CW: Non-Art Street Rehab & Rep	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
4291	2436S0004Z	CW Sidewalks	\$ 100,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 100,000.00
4291	2436W0003Z	41st St: Garnett - 129EA Widen	\$ 1,000,000.00	\$ -	\$ 167,254.76	\$ 167,254.76	\$ 78,645.24	\$ -	\$ 754,100.00
4291	2436X0001Z	Inflation Increases - Streets	\$ 10,400,000.00	\$ -	\$ -	\$ -	\$ 114,528.67	\$ -	\$ 10,285,471.33
4291	2443X0005Z	Chamberlain - Pool Improvement	\$ 1,000,000.00	\$ -	\$ 1,000,000.00	\$ 1,000,000.00	\$ -	\$ -	\$ -
4291	2443X0006Z	Swan Lake Renovations	\$ 500,000.00	\$ -	\$ 302,549.56	\$ 304,537.42	\$ 172,044.77	\$ -	\$ 23,417.81
4291	2443X0007Z	Zink Lake Infrastructure needs	\$ 4,352,432.22	\$ -	\$ 2,909,179.35	\$ 4,352,432.22	\$ -	\$ -	\$ -
4291	2443X0009Z	Zink Lake Infrastrucure needs	\$ 647,567.78	\$ 56,885.68	\$ 292,077.47	\$ 292,077.47	\$ 351,265.11	\$ -	\$ 4,225.20
4291	2444B0008Z	Gilcrease Museum Improvs Match	\$ 10,000,000.00	\$ -	\$ 5,623,953.45	\$ 10,000,000.00	\$ -	\$ -	\$ -
4291	2444B0009Z	Tulsa Zoo Roof Replacements	\$ 1,200,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,200,000.00
4291	2444B0010Z	Tulsa Zoo Rainforest Rehab	\$ 8,000,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 8,000,000.00
4292	2419X0011Z	Bond Issuance Cost	\$ 150,000.00	\$ -	\$ 150,000.00	\$ 150,000.00	\$ -	\$ -	\$ -
4292	2423X0012Z	Safety Training Center Drive T	\$ 4,370,000.00	\$ 292,192.79	\$ 292,192.79	\$ 292,192.79	\$ 2,943,681.53	\$ -	\$ 1,134,125.68
4292	2436A0002Z	CW Arterial Streets R&R	\$ 2,333,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,333,000.00
4292	2436B0005Z	CW: Bridge Rehab & Replacement	\$ 1,925,000.00	\$ 130,378.13	\$ 483,591.50	\$ 483,591.50	\$ 968,813.65	\$ -	\$ 472,594.85
4292	2436N0002Z	CW: Non-Art Street Rehab & Rep	\$ 6,267,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 6,267,000.00
4292	2436N0007Z	CW: Alleys	\$ 200,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 200,000.00
4292	2436S0004Z	CW Sidewalks	\$ 480,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 480,000.00
4292	2436W0003Z	41st St: Garnett - 129EA Widen	\$ 2,500,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,500,000.00
4292	2436X0001Z	Inflation Increases - Streets	\$ 5,700,000.00	\$ -	\$ -	\$ -	\$ 6,875.00	\$ -	\$ 5,693,125.00
4292	2436X0002Z	CW Street Matching Funds	\$ 3,600,000.00	\$ 602,292.13	\$ 1,170,592.13	\$ 1,170,592.13	\$ 1,282,383.47	\$ -	\$ 1,147,024.40
4292	2436X0003Z	Engineering Testing Inspection	\$ 500,000.00	\$ 158,209.32	\$ 331,019.15	\$ 331,019.15	\$ 168,980.85	\$ -	\$ -
4292	2436X0006Z	CW: Traffic Engineering	\$ 2,650,000.00	\$ 10,949.77	\$ 30,264.91	\$ 30,264.91	\$ 44,735.09	\$ -	\$ 2,575,000.00
4292	2443S0012Z	CW: Parks parking lot rehab	\$ 800,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 800,000.00
4292	2443X0005Z	Chamberlain - Park Improvement	\$ 5,000,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 5,000,000.00
4292	2443X0008Z	Mohawk Golf Courses Renovation	\$ 4,000,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 4,000,000.00
4292	2444B0009Z	Tulsa Zoo Roof Replacements	\$ 1,800,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,800,000.00
4292	2444X0010Z	BOK Center Improvements	\$ 4,675,000.00	\$ -	\$ -	\$ -	\$ 805,233.84	\$ 350,000.00	\$ 3,519,766.16
4293	2419X0011Z	Bond Issuance Cost - IoT 3	\$ 20,000.00	\$ -	\$ 10,874.00	\$ 10,874.00	\$ -	\$ -	\$ 9,126.00
4293	2436B0005Z	CW: Bridge Rehab & Replacement	\$ 500,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 500,000.00
4293	2436X0001Z	Inflation Increases - Streets	\$ 10,815,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 10,815,000.00
4293	2436X0002Z	Citywide Grant Matching Funds	\$ 3,600,000.00	\$ 137,443.87	\$ 137,443.87	\$ 137,443.87	\$ 700,008.03	\$ -	\$ 2,762,548.10
4294	2419X0011Z	Bond Issuance Cost - IoT 3	\$ 65,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 65,000.00
4294	2424B0037Z	PSC: Building Acq & Relocation	\$ 45,000,000.00	\$ 26,992.50	\$ 26,018,057.19	\$ 26,018,057.19	\$ 673,726.78	\$ -	\$ 18,308,216.03
4294	2425X0038Z	PSC: Fire/Police Equip Mainten	\$ 2,000,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,000,000.00
4294	2444B0020Z	BOK Center - Safety/Security	\$ 1,150,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,150,000.00
4294	2444B0026Z	TPAC - Design/Proj Management	\$ 5,000,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 5,000,000.00
4294	2444X0010Z	BOK Center Improvements	\$ 525,000.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 525,000.00

COMBINED STATEMENT OF OTHER FUND ACTIVITY

FUNDS 400, 401, 403, 404, 425

SALES TAX OVERVIEW COMMITTEE REPORT
(FUNDS 401, 403, 404, 425, 426)
Combined Statement of Fund Activity
March 31, 2025

Fund	LIFE-TO-DATE APPROPRIATIONS	EXPEDITURES			ENCUMBERED/ COMMITTED	BALANCE
		CURRENT MONTH	FISCAL YEAR-TO-DATE	LIFE-TO-DATE		
FUND 401 - 2001 SALES TAX FUND	\$ 84,907,871.03	\$ 14,359.57	\$ 14,359.57	\$ 84,905,730.03	\$ (0.00)	\$ 2,141.00
2036D0008Z 1st 2nd & 4th St Two-Way Conv	\$ 2,141.00	-	-	\$ -		\$ 2,141.00
2436A0000Z CW: Arterial Streets Rehab		14,359.57	14,359.57	\$ -		
FUND 403 - 2006 EXT SALES TAX ADVACE FUND	\$ 27,705,922.61	\$ -	\$ -	\$ 27,705,676.78	\$ -	\$ 245.83
017150 Woodward & Forestry Impr.	470,000.00	-	-	469,754.17	-	245.83
FUND 404 - 2008 SPECIAL TEMP SALES TAX	\$ 149,658,132.00	\$ 3,719.36	\$ 22,792.11	\$ 145,338,831.28	\$ 150,945.36	\$ 4,198,591.65
104017 Art Rehab Citywide	81,942,000.00	657.76	657.76	81,859,132.39	82,209.85	82,867.61
104021 Citywide Non-arterial RTPV	34,082,000.00	-	-	34,048,044.35	33,955.65	33,955.65
104022 Citywide General Engineering	1,383,000.00	3,061.60	22,134.35	1,348,220.14	34,779.86	-
144104 Riverside Dr & Rltd Infrstr	5,500,000.00	-	-	5,499,996.00	-	4.00
2036D0008Z 1st 2nd & 4th St Two-Way Conv	4,164,632.00	-	-	-	-	4,164,632.00
FUND 425 - 2005 BOND ISSUE (4250-4255)	\$ 75,966,288.83	\$ 45,999.65	\$ 164,450.40	\$ 75,067,905.34	\$ 885,374.34	\$ 13,009.15
055103 UDE Renovation	\$ 47,852.41	\$ -	\$ -	\$ 39,018.26		\$ 8,834.15
055105 UDSW Renovation	\$ 60,629.78	\$ -	\$ -	\$ 56,454.78	\$ -	\$ 4,175.00
2337B0162Z Bridge #162: Boston Ave	\$ 564,101.53	\$ 137,990.15	\$ 302,440.55	\$ 302,440.55	\$ 261,660.98	\$ -
2337B0162Z Bridge 162 Boston Ave	\$ 140.00	\$ -	\$ -	\$ -	\$ 140.00	\$ -
2337B0162Z Bridge # 162	\$ 319,614.89	\$ -	\$ -	\$ -	\$ 319,614.89	\$ -
2337B0162Z Bridge 162 Boston Ave	\$ 36,669.70	\$ -	\$ -	\$ -	\$ 36,669.70	\$ -
2337B0162Z Bridge 162 Boston Ave	\$ 129,298.62	\$ -	\$ -	\$ -	\$ 129,298.62	\$ -


**THERE WERE NO
BUDGET ACTIONS POSTED
THIS MONTH**

ALL FUNDS BUDGET ACTIONS

Ordinance

Version 3.5 released on 2/29/24

Use for all Ordinances including: TRO, Budget, Zoning, Declarations, Trust Indentures, etc.



CITY COUNCIL USE ONLY

Date Received:

Committee Date: 2-26-25

1st Agenda Date: 2-26-25

Tracking #:

25-119-1

Committee:

UED

Hearing Date:

2nd Agenda Date: 3-5-25

CITY CLERK USE ONLY

☐ Scanned

Date:

03.12.2025

☒ Posted

Item #

2502.00396

All department items requiring Council approval must be submitted through the Mayor's Office.

Dept. Tracking No.	Board Approval Tulsa Metropolitan Utility Authority	Other Board Name	City Council Approval <input checked="" type="radio"/> Yes <input type="radio"/> No
Department Finance	Contact Name Jarrod Moore	Email jlmoores@cityoftulsa.org	Phone 918-596-7809
Subject (Description) E4675/Waterline Road TMUA Water Capital Projects Sub-fund 7400	Ordinance Type Inter-Departmental Transfer of Funds (Council Transfer)		
Section	Township	Range	Lot
Block	Address	BA / CT Number CT74003008	
Amending Ord. No.	TRO Title No.	TRO Subtitle	Property/Non-Property
Council District	Zoning No.	PUD No.	Planning District

Funding Source(s)

TMUA Water Capital Projects / Subfund 7400/ Water & Sewer/ E4675-Waterline Road:	\$458,532.40
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Raw Water Flowline Repairs Spavinaw:	-\$125,000.00
TMUA Water Capital Projects / Subfund 7400/ Water & Sewer/ Raw Water Flowline Repairs Oolagah:	-\$333,532.40
TOTAL:	\$0.00

JE JM

Department:

Christy Basgall

Legal:

Board:

Mayor:

Other:

Date: Feb 7, 2025

Date:

Date:

Date:

Date:

FEB 12 2025

Background Information

This budget action will transfer unexpended and unencumbered appropriation balances between projects in the TMUA WATER CAPITAL PROJECTS Sub-Fund (Sub-Fund 7400). Funds will be moved from two projects with residual balance to the E4675/Waterline Road project. E4675/Waterline Road is a project in conjunction with Mayes County and the road leads to the City's Grand River Pump Station. This budget action reflects the City's portion of the repairs and maintenance to the road. Work will be over seen by Mayes County who will cover the balance of the costs. This funding request was approved by the Asset Management Committee in May of 2024.

Summation of the Requested Action

Request for Mayor and Council to approve CT74003008 to move funding to E4675/Waterline Road project. | \$458,532.40

Emergency Clause?

☐ Yes☒ No

Reason for Emergency Clause

Post Execution Processing

- ☐ Mail vendor copy (add'l signature copies attached)
- ☐ Must be filed with other governmental entity
- ☐ Add'l governmental entity approval(s) required

Additional Routing and Processing Details

Original Budget: NO to all

(Published in the Tulsa World

March 19, 2025)

ORDINANCE NO. 25541

AN ORDINANCE AMENDING THE FISCAL YEAR 2024-25 BUDGET OF THE CITY OF TULSA, OKLAHOMA, TO TRANSFER UNENCUMBERED AND UNEXPENDED APPROPRIATION BALANCES OF FOUR HUNDRED FIFTY-EIGHT THOUSAND FIVE HUNDRED THIRTY-TWO DOLLARS AND FORTY CENTS (\$458,532.40) BETWEEN PROJECTS WITHIN THE TMUA WATER CAPITAL PROJECTS SUBFUND (SUBFUND 7400), AS FOLLOWS:

BE IT ORDAINED BY THE CITY OF TULSA:

Section 1. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to transfer unencumbered and unexpended appropriation balances of Four Hundred Fifty-Eight Thousand Five Hundred Thirty-Two Dollars and Forty Cents (\$458,532.40) between Projects within the TMUA WATER CAPITAL PROJECTS SUBFUND (SUBFUND 7400), as follows:

TMUA WATER CAPITAL PROJECTS SUBFUND

WATER & SEWER DEPARTMENT

Raw Water Flowline Repairs Spavinaw	
CIP Land Improvements	\$ (125,000.00)
Raw Water Flowline Repairs Oologah	
CIP Land Improvements	\$ (333,532.40)
E4675 Waterline Road	
CIP Street Network	\$ 458,532.40
TOTAL FUND CHANGE	\$ -

Section 2. That this ordinance shall take effect immediately from and after its adoption and approval.

Adopted by the Council: MAR 05 2025
Date


Chair of the Council

OFFICE OF THE MAYOR

Received by the Mayor: _____, at _____.

JCB slg

7400-08
(02/03/2025)

Date

Time

Monroe Nichols IV, Mayor

By: _____

Secretary

Approved by the Mayor of the City of Tulsa, Oklahoma, MAR 12 2025 at

Time

Date

Mayor

(Seal)

ATTEST:

City Clerk

APPROVED:

City Attorney



Signature: *Jake Sepp*

Email: sepp@cityoftulsa.org

Signature: *Jarrod Moore*

Email: jlmoore@cityoftulsa.org

Ordinance

Version 3.5 released on 2/29/24

Use for all Ordinances including: TRO, Budget, Zoning, Declarations
Trust Indentures, etc.

APPROVED

MAR 05 2025

Tulsa City Council

**CITY COUNCIL USE ONLY**

Date Received: _____
 Committee Date: 2-26-25
 1st Agenda Date: 2-26-25

Tracking #: 25-120-1
 Committee: LED
 Hearing Date: _____
 2nd Agenda Date: 3-5-25

CITY CLERK USE ONLY

☐ Scanned Date: 03.12.2025
☒ Posted Item #: 2502.00429

All department items requiring Council approval must be submitted through the Mayor's Office.

Primary Details

Dept. Tracking No.	Board Approval Tulsa Metropolitan Utility Authority	Other Board Name	City Council Approval <input checked="" type="radio"/> Yes <input type="radio"/> No
Department Finance	Contact Name Jarrod Moore	Email jlmoores@cityoftulsa.org	Phone 918-596-7809
Subject (Description) CIP Project Cleanup 2 Stormwater Capital Fund Subfund 5600		Ordinance Type Inter-Departmental Transfer of Funds (Council Transfer)	
Section	Township	Range	Lot
Block	Address		BA / CT Number CT56003088
Amending Ord. No.	TRO Title No.	TRO Subtitle	Property/Non-Property
Council District	Zoning No.	PUD No.	Planning District

Budget**Funding Source(s)**

Stormwater Capital Projects/ Subfund 5600/ Water & Sewer/ Citywide Flood Control:	\$-13,741.97
Stormwater Capital Projects/ Subfund 5600/ Water & Sewer/ Stormwater Improvements Citywide:	\$13,741.97
Stormwater Capital Projects/ Subfund 5600/ Water & Sewer/ Owen Park:	\$-32,986.81
Stormwater Capital Projects/ Subfund 5600/ Water & Sewer/ Citywide Detention Pond Rehabilitation:	\$32,986.81
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Lynn Lane Yahola Repairs:	\$-50.50
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Lake Yahola Terminal Storage Repairs:	\$0.50
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Citywide Water Mains Replacement:	\$-52,631.05
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Central Business District Water Mains Replacement:	\$-115,008.11
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Cherokee Water Lines - 2020:	\$-35,812.96
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Citywide Water Mains Replacement:	\$203,452.12
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Citywide Large Water Valve Replacement:	\$-15,394.81
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Citywide Large Water Valve Replacement:	\$15,394.81
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Economic Development Citywide:	\$-35,893.89
TMUA Water Capital Projects/ Subfund 7400/ Water & Sewer/ Economic Development Citywide:	\$35,893.89
TOTAL:	\$0.00

Approvals JEMM

Department: _____

Signature: Christy BasgallDate: Feb 11, 2025

Legal: _____

Email: CBASGALL@cityoftulsa.org

Date: _____

Board: _____

Date: _____

Mayor: _____

Date: FEB 12 2025

Other: _____

Date: _____

Policy Statement

Background Information

This budget action will transfer unexpended and unencumbered appropriation balances between projects in the STORMWATER CAPITAL PROJECTS Fund (Sub-Fund 5600) in the amount of \$46,728.78 and between projects in the TMUA WATER CAPITAL PROJECTS Fund (Sub-Fund 7400) in the amount of \$254,741.32. The projects from which the appropriations are being transferred are completed in scope and the remaining appropriations are residual. Those projects zeroed out by this action will be closed. The appropriations will go to active projects related in scope.

This action will close the following 7 projects: 173120 Citywide Flood Control || 161013 Lynn Lane Yahola Repairs || 193310010Z Central Business District Water Mains Replacement || 193310014Z Citywide Large Water Valve Replacement || 193310015Z Cherokee Water Lines-2020 || 193310018Z Economic Development Citywide || 2331F00020 Owen Park.

Summation of the Requested Action

Request for Mayor and Council to approve CT56003088 to move residual appropriations to active projects. | \$301,470.10

Emergency Clause?

Reason for Emergency Clause

☐ Yes☒ No

Processing Information for City Clerk's Office

Post Execution Processing

☐ Mail vendor copy (add'l signature copies attached)☐ Must be filed with other governmental entity☐ Add'l governmental entity approval(s) required

Additional Routing and Processing Details

Original Budget: NO to all

(Published in the Tulsa World

March 19, 2025)

ORDINANCE NO. 25542

AN ORDINANCE AMENDING THE FISCAL YEAR 2024-25 BUDGET OF THE CITY OF TULSA, OKLAHOMA, TO TRANSFER UNENCUMBERED AND UNEXPENDED APPROPRIATION BALANCES OF FORTY SIX THOUSAND SEVEN HUNDRED TWENTY-EIGHT DOLLARS AND SEVENTY-EIGHT CENTS (\$46,728.78) BETWEEN PROJECTS WITHIN THE STORMWATER CAPITAL PROJECTS SUBFUND (SUBFUND 5600) AND TWO HUNDRED FIFTY-FOUR THOUSAND SEVEN HUNDRED FORTY-ONE DOLLARS AND THIRTY-TWO CENTS (\$254,741.32) BETWEEN PROJECTS WITHIN THE TMUA WATER CAPITAL PROJECTS SUBFUND (SUBFUND 7400), AS FOLLOWS:

BE IT ORDAINED BY THE CITY OF TULSA:

Section 1. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to transfer unencumbered and unexpended appropriation balances of Forty-Six Thousand Seven Hundred Twenty-Eight Dollars and Seventy-Eight Cents (\$46,728.78) between Projects within the STORMWATER CAPITAL PROJECTS SUBFUND (SUBFUND 5600), as follows:

STORMWATER CAPITAL PROJECTS

WATER & SEWER DEPARTMENT

Citywide Flood Control	
Capital Outlay	\$ (13,741.97)
Stormwater Improvements Citywide	
Capital Outlay	\$ 13,741.97
Owen Park	
Capital Outlay	\$ (32,986.81)
Citywide-Detention Pond Rehabilitation	
Capital Outlay	\$ 32,986.81
TOTAL FUND INCREASE / DECREASE	\$ -

Section 2. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to transfer unencumbered and unexpended appropriation balances of Two Hundred Fifty-Four Thousand Seven Hundred Forty-One Dollars and Thirty-Two Cents (\$254,741.32) between Projects within the TMUA WATER CAPITAL PROJECTS SUBFUND (SUBFUND 7400), as follows:

TMUA WATER CAPITAL PROJECTS

WATER & SEWER DEPARTMENT

Lynn Lane Yahola Repairs	
Capital Outlay	\$ (0.50)
Lake Yahola Terminal Storage Repair	
Capital Outlay	\$ 0.50
Citywide-Water Mains Replacement	
Capital Outlay	\$ (52,631.05)
Central Business District Water Mains Replacement	
Capital Outlay	\$ (115,008.11)
Cherokee Water Lines – 2020	
Capital Outlay	\$ (35,812.96)
Citywide-Water Mains Replacement	
Capital Outlay	\$ 203,452.12
Citywide – Large Water Valve Replacement	
Capital Outlay	\$ (15,394.81)
Citywide – Large Water Valve Replacement	
Capital Outlay	\$ 15,394.81
Economic Development Citywide	
Capital Outlay	\$ (35,893.89)
Economic Development Citywide	
Capital Outlay	\$ 35,893.89
TOTAL FUND INCREASE / DECREASE	\$ -

Section 3. That this ordinance shall take effect immediately from and after its adoption and approval.

Adopted by the Council: MAR 05 2025
Date


Chair of the Council

OFFICE OF THE MAYOR

Received by the Mayor: _____, at _____.
Date Time

Monroe Nichols IV, Mayor

By: _____
Secretary

Approved by the Mayor of the City of Tulsa, Oklahoma, MAR 12 2025 at _____
Date

Time

(Seal)

ATTEST:


City Clerk

APPROVED:


City Attorney




Mayor

Signature: *Jake Gipe*

Email: sepp@cityoftulsa.org

Signature: *Jarrod Moore*

Email: jlmoore@cityoftulsa.org

Ordinance

Version 3.5 released on 2/29/24

Use for all Ordinances including: TRO, Budget, Zoning, Declarations, Trust Indentures, etc.

**CITY COUNCIL USE ONLY**

Date Received: _____

Committee Date: 3-5-251st Agenda Date: 3-5-25Tracking #: 25-143-1Committee: UED

Hearing Date: _____

2nd Agenda Date: 3-12-25**CITY CLERK USE ONLY**☐ ScannedDate: 03.19.2025☒ PostedItem #: 2502.00520**All department items requiring Council approval must be submitted through the Mayor's Office.**

Dept. Tracking No.	Board Approval	Other Board Name	City Council Approval <input checked="" type="radio"/> Yes <input type="radio"/> No
Department Finance	Contact Name Jarrod Moore	Email jlmoore@cityoftulsa.org	Phone 918-596-7809
Subject (Description) Kendall Whittier Main Street Improvements 2020 Sales Tax Fund Fund 409		Ordinance Type Budget Amendment	
Section	Township	Range	Lot
Block	Address		BA / CT Number BA409541
Amending Ord. No.	TRO Title No.	TRO Subtitle	Property/Non-Property
Council District	Zoning No.	PUD No.	Planning District

Funding Source(s)

2020 Sales Tax Fund (Fund 409) / Department of City Experience / Kendall Whittier Main Street Improvements: \$50,000.00

TOTAL: \$50,000.00JE JM
JE Department:

Christy Baagall

Legal:

Board:

Mayor:

Other:

Mike Miller
Mayor Pro Tem

Date: Feb 20, 2025

Date:

Date:

Date: FEB 26 2025

Date:

Background Information

This action will appropriate a total of \$50,000.00, recognized from Unappropriated Fund Balance, appropriating to the DEPARTMENT OF CITY EXPERIENCE within the 2020 SALES TAX FUND [FUND 409].

This Budget Amendment will appropriate \$50,000.00 from fund balance within the 2020 Sales Tax Fund (Fund 409) to provide funding towards the improvement of Kendall Whittier Main Street. These improvements consist of beautification, placemaking, and art projects including Whittier Square Clock repairs; Route 66 Neon sign and neon light enhancement to Whittier Square; district wayfinding signage; district and seasonal street light banners; two pieces of public art to serve as district gateways; 8-10 utility box art installations; and public art at the Kendall Whittier Library. This project has an additional \$210,000.00 in funding from private donations and a state grant, bringing the total project funding to \$260,000.00.

Funds have been held to allow for City Council review and approval of projects proposed for funding from the Council District Priority Project allocation. The City Council and Mayor have now approved the project from the City Council District 4 portion of the City Council District Priority Project.

Summation of the Requested Action

Request for Mayor and Council to approve BA409541 | Kendall Whittier Main Street Improvements | \$50,000.00

Emergency Clause?☐ Yes☒ No**Reason for Emergency Clause**

(Published in the Tulsa World

March 26, 2025, 2025)

ORDINANCE NO. 25544

AN ORDINANCE AMENDING THE FISCAL YEAR 2024-25 BUDGET OF THE CITY OF TULSA, OKLAHOMA, TO MAKE SUPPLEMENTAL APPROPRIATIONS OF FIFTY THOUSAND DOLLARS AND ZERO CENTS (\$50,000.00), RECOGNIZED FROM UNAPPROPRIATED FUND BALANCE WITHIN THE 2020 SALES TAX FUND (FUND 409) AS FOLLOWS:

BE IT ORDAINED BY THE CITY OF TULSA:

Section 1. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to make supplemental appropriations of Fifty Thousand Dollars and Zero Cents (\$50,000.00), recognized from Unappropriated Fund Balance within the 2020 Sales Tax Fund (Fund 409) as follows:

**2020 SALES TAX FUND
(FUND 409)**

DEPARTMENT OF CITY EXPERIENCE

Kendall Whittier Main Street Improvements

Capital Outlay	\$	50,000.00
----------------	----	-----------

TOTAL DEPARTMENT CHANGE	\$	<u>50,000.00</u>
--------------------------------	-----------	-------------------------

TOTAL FUND CHANGE	\$	<u>50,000.00</u>
--------------------------	-----------	-------------------------

Section 2. That this ordinance shall take effect immediately from and after its adoption and approval.

Adopted by the Council: MAR 12 2025

Date


Chair of the Council

OFFICE OF THE MAYOR

Received by the Mayor: _____, at _____
Date Time

Monroe Nichols IV, Mayor

By: _____

Secretary

MAR 19 2025

Approved by the Mayor of the City of Tulsa, Oklahoma, _____ at
Date

Time

(Seal)

ATTEST:

City Clerk

APPROVED:

City Attorney





Mayor

25545

Ordinance

Version 3.5 released on 2/29/24

Use for all Ordinances including: TRO, Budget, Zoning, Declarations, Trust Indentures, etc.

APPROVED

MAR 12 2025

Tulsa City Council

**CITY COUNCIL USE ONLY**

Date Received: _____

Committee Date: 3-5-251st Agenda Date: 3-5-25

Tracking #

Committee

Hearing Date

2nd Agenda Date25-144-1UED3-12-253-12-25**CITY CLERK USE ONLY**☐ Scanned

Date:

☒ Posted

Item #

03/19/20252502.00521**All department items requiring Council approval must be submitted through the Mayor's Office.**

Dept. Tracking No.

Board Approval

Other Board Name

City Council Approval

☒ Yes ☐ No

Department

Contact Name

Email

Phone

Finance

Jarrod Moore

jlmoores@cityoftulsa.org

918-596-7809

Subject (Description)

Ordinance Type

TPFA 2025 Stormwater Revenue Bond | Subfund 5621

Section

Township

Range

Lot

Block

Address

BA / CT Number

BA56211569

Amending Ord. No.

TRO Title No.

TRO Subtitle

Property/Non-Property

Council District

Zoning No.

PUD No.

Planning District

Funding Source(s)

TPFA 2025 Stormwater Revenue Bond | Subfund 5621 | Water & Sewer | Hager Creek Storm

\$3,000,000.00

Sewer Relief Line:

TPFA 2025 Stormwater Revenue Bond | Subfund 5621 | Water & Sewer | Stormwater

\$7,000,000.00

Maintenance Building Expansion:

TOTAL: \$10,000,000.00

JE M

JE M

Department: Christy Baskall

Legal:

Board:

Mayor:

Other:

Mike Miller

Mayor Pro Tem

Date: Feb 24, 2025

Date: _____

Date: _____

Date: _____

Date: FEB 26 2025**Background Information**

This action will appropriate a total of \$10,000,000.00, recognized from revenue received from a sale of stormwater revenue bonds, appropriating to the Water & Sewer Department within the TPFA 2025 Stormwater Bonds Sub-Fund (Sub-fund 5621)

Resolution #20388 authorized the sale of \$10,000,000 in stormwater revenue bonds, to fund the following stormwater system improvement capital projects, as follows:

* \$3,000,000: Hager Creek - Storm Sewer Relief Line - Flood Control

* \$7,000,000: Stormwater Maintenance Building Expansion

Summation of the Requested Action

Request that Mayor and Council approve the attached budget amendment BA56211569 | TPFA 2025 Stormwater Revenue Bond | \$10,000,000.00

Emergency Clause?

☐ Yes☒ No

Reason for Emergency Clause

Post Execution Processing☐ Mail vendor copy (add'l signature copies attached)☐ Must be filed with other governmental entity☐ Add'l governmental entity approval(s) required**Additional Routing and Processing Details**

Set to Original: YES to all

(Published in the Tulsa World

March 26, 2025)

ORDINANCE NO. 25545

AN ORDINANCE AMENDING THE FISCAL YEAR 2024-25 BUDGET OF THE CITY OF TULSA, OKLAHOMA, BE AND IT IS HEREBY AMENDED TO RECOGNIZE AND MAKE SUPPLEMENTAL APPROPRIATIONS OF TEN MILLION DOLLARS AND ZERO CENTS (\$10,000,000.00), FROM REVENUE RECEIVED FROM THE SALE OF STORMWATER REVENUE BONDS, WITHIN THE TPFA 2025 STORMWATER BONDS SUB-FUND (SUB-FUND 5621), AS FOLLOWS:

BE IT ORDAINED BY THE CITY OF TULSA:

Section 1. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to recognize and make supplemental appropriations of Ten Million Dollars and Zero Cents (\$10,000,000.00), from revenue received from the sale of stormwater revenue bonds, within the TPFA 2025 Stormwater Bonds Sub-Fund (Sub-Fund 5621), as follows:

TPFA 2025 STORMATER BONDS SUBFUND

WATER & SEWER DEPARTMENT

Hager Creek Storm Sewer Relief	
Capital Outlay	\$ 3,000,000.00
Stormwater Maintenance Building	
Capital Outlay	\$ 7,000,000.00
TOTAL FUND CHANGE	\$ 10,000,000.00

Section 2. That this ordinance shall take effect immediately from and after its adoption and approval.

Adopted by the Council: MAR 12 2025

Date


Chair of the Council

OFFICE OF THE MAYOR

Received by the Mayor: _____, at _____
Date Time

Monroe Nichols IV, Mayor

By: _____
Secretary

Approved by the Mayor of the City of Tulsa, Oklahoma, MAR 19 2025 at _____
Date

Time

(Seal)

ATTEST:

City Clerk

APPROVED:

City Attorney



25546**Ordinance**

Version 3.5 released on 2/29/24

Use for all Ordinances including: TRO, Budget, Zoning, Declarations,
Trust Indentures, etc.**APPROVED**

MAR 12 2025

Tulsa City Council

**CITY COUNCIL USE ONLY**

Date Received: _____

Committee Date: 3-5-251st Agenda Date: 3-5-25Tracking #: 25-148-1Committee: UED

Hearing Date: _____

2nd Agenda Date: 3-12-25**CITY CLERK USE ONLY**☐ ScannedDate: 03.19.2025☐ PostedItem #: 2502.00522**All department items requiring Council approval must be submitted through the Mayor's Office.**

Dept. Tracking No.	Board Approval Tulsa Metropolitan Utility Authority	Other Board Name	City Council Approval <input checked="" type="radio"/> Yes <input type="radio"/> No
Department Finance	Contact Name Jarrod Moore	Email jlmoores@cityoftulsa.org	Phone 918-596-7609
Subject (Description) Trans between projects TMUA Sewer Capital Project (Subfund 7500) TMUA Sewer Operating (Fund 750)		Ordinance Type Budget Amendment	
Section	Township	Range	Lot
Block	Address		BA / CT Number BA75001154
Amending Ord. No.	TRO Title No.	TRO Subtitle	Property/Non-Property
Council District	Zoning No.	PUD No.	Planning District

Funding Source(s)

TMUA Sewer Operating Fund / Fund 750 / Transfer Department / Transfer Out:	\$5,853,942.00
TMUA Sewer Capital Projects / Subfund 7500 / Water & Sewer / Coal Creek (103-N) Parallel Interceptor:	-\$3,020,000.00
TMUA Sewer Capital Projects / Subfund 7500 / Water & Sewer / Coal Creek 103N Parallel Interceptor:	-\$1,189,635.21
TMUA Sewer Capital Projects / Subfund 7500 / Water & Sewer / Sewer Rehabilitation Area-wide:	\$9,838,577.21
TMUA Sewer Capital Projects / Subfund 7500 / Water & Sewer / Northside Lagoon Leak Design:	\$225,000.00
2024B Sewer Revenue Bond / Subfund 7523 / Water & Sewer / Sludge Dewatering Alternatives:	-\$964,075.63
2024B Sewer Revenue Bond / Subfund 7523 / Water & Sewer / Sewer Rehabilitation Area-wide:	\$964,075.63
TMUA Sewer Capital Projects / Subfund 7500 / Revenue:	-\$5,853,942.00
TOTAL:	\$5,853,942.00

JE JM

Department: Christy Basgall

Legal: _____

Board: _____

Mayor: Mike Mitter

Other: Mayor Pro Tem

Date: Feb 24, 2025

Date: _____

Date: _____

Date: FEB 26 2025

Date: _____

Background Information

This action will transfer a total of \$11,027,652.84 within the WATER & SEWER DEPARTMENT to further fund citywide concrete pipe replacement and fund designs for the Northside Lagoon. This action will facilitate this by:

1. Appropriating \$5,853,942.00 of unappropriated and available fund balance of within the TMUA SEWER OPERATING FUND (Fund 750) to the TRANSFER DEPARTMENT, and then transferring those funds to the WATER & SEWER DEPARTMENT in the TMUA SEWER CAPITAL SUBFUND (Subfund 7500).
2. Transferring unexpended and available appropriation balances between projects within the TMUA SEWER CAPITAL SUBFUND (Subfund 7500). The appropriations are being transferred are not needed and the projects from which they are being transferred will be completed to their original scope.
3. Transferring appropriation balances between projects in the 2024B SEWER REVENUE BOND SUBFUND (Subfund 7523). The project from which the appropriations are being transferred are completed in scope and the remaining appropriations are residual.

Summation of the Requested Action

Request for Mayor and Council to approve BA75001154 to move appropriations to active projects. | \$11,027,652.84

Emergency Clause?

☐ Yes

☒ No

Reason for Emergency Clause

Post Execution Processing

- ☐ Mail vendor copy (addtl signature copies attached)
- ☐ Must be filed with other governmental entity
- ☐ Addtl governmental entity approval(s) required

Additional Routing and Processing Details

Set to Original Budget: Yes to 2531S00020 ||| No to all others

(Published in the Tulsa World

March 26, 2025)

ORDINANCE NO. 25546

AN ORDINANCE AMENDING THE FISCAL YEAR 2024-25 BUDGET OF THE CITY OF TULSA, OKLAHOMA, TO MAKE SUPPLEMENTAL APPROPRIATIONS OF FIVE MILLION EIGHT HUNDRED FIFTY-THREE THOUSAND NINE HUNDRED FORTY TWO DOLLARS AND ZERO CENTS (\$5,853,942.00) FROM UNAPPROPRIATED FUND BALANCE IN THE TMUA SEWER OPERATING FUND (FUND 750) AND TO TRANSFER UNENCUMBERED AND UNEXPENDED APPROPRIATION BALANCES OF FOUR MILLION TWO HUNDRED NINE THOUSAND SIX HUNDRED THIRTY-FIVE DOLLARS AND TWENTY-ONE CENTS (\$4,209,635.21) BETWEEN PROJECTS WITHIN THE TMUA SEWER CAPITAL PROJECTS SUBFUND (SUBFUND 7500), AND TO TRANSFER UNENCUMBERED AND UNEXPENDED APPROPRIATION BALANCES OF NINE HUNDRED SIXTY-FOUR THOUSAND SEVENTY-FIVE DOLLARS AND SIXTY THREE CENTS (\$964,075.63) BETWEEN PROJECTS IN THE 2024B SEWER REVENUE BOND SUBFUND (SUBFUND 7523): AS FOLLOWS:

BE IT ORDAINED BY THE CITY OF TULSA:

Section 1. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to make supplemental appropriations of Five Million Eight Hundred Fifty-Three Thousand Nine Hundred Forty-Two Dollars and Zero Cents (\$5,853,942.00) from unappropriated fund balance in the TMUA SEWER OPERATING Fund (Fund 750), as follows:

TMUA SEWER OPERATING FUND

TRANSFER DEPARTMENT

Transfers out	\$ 5,853,942.00
TOTAL FUND CHANGE	\$ 5,853,942.00

Section 2. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to transfer unencumbered and unexpended appropriation balances of Four Million Two Hundred Nine Thousand Six Hundred Thirty-Five Dollars and Twenty-One Cents (\$4,209,635.21) between projects and make supplemental appropriations of Five Million Eight Hundred Fifty-Three Thousand Nine Hundred Forty-Two Dollars and Zero Cents (\$5,853,942.00) within the TMUA SEWER CAPITAL PROJECTS Sub Fund (Sub Fund 7500); as follows:

TMUA SEWER CAPITAL PROJECTS SUBFUND

WATER & SEWER

Coal Creek (103-N) Parallel Interceptor	
Capital Outlay	\$ (3,020,000.00)
Coal Creek 103N Parallel Interceptor	
Capital Outlay	\$ (1,189,635.21)
Sewer Rehabilitation Areawide	
Capital Outlay	\$ 9,838,577.21
Northside Lagoon Leak Design	
Capital Outlay	\$ 225,000.00
TOTAL FUND CHANGE	\$ 5,853,942.00

Section 3. That the Fiscal Year 2024-25 Budget of the City of Tulsa, Oklahoma, be and it is hereby amended to transfer unencumbered and unexpended appropriation balances of Nine Hundred Sixty-Four Thousand Seventy-Five Dollars and Sixty-Three Cents (\$964,075.63) between projects within the 2024B SEWER REVENUE BOND Sub Fund (Sub Fund 7523) as follows:

2024B SEWER REVENUE BOND SUBFUND

ENGINEERING SERVICES

Sludge Dewatering Alternatives	
Capital Outlay	\$ (964,075.63)
Sewer Rehabilitation Areawide	
Capital Outlay	\$ 964,075.63
TOTAL FUND CHANGE	\$ -

Section 4. That this ordinance shall take effect immediately from and after its adoption and approval.

Adopted by the Council: MAR 12 2025
Date



Chair of the Council

OFFICE OF THE MAYOR


Received by the Mayor: _____, at _____
Date Time

Monroe Nichols IV, Mayor

By: _____
Secretary

Approved by the Mayor of the City of Tulsa, Oklahoma, MAR 19 2025 at _____
Date

Time



Mayor

(Seal)

ATTEST:



City Clerk



APPROVED:



City Attorney
