

City Contract

Version 5.5 released on 7/1/25



WS0121716

CITY COUNCIL USE ONLY

Date Received: _____
 Committee Date: _____
 1st Agenda Date: _____

Tracking #: _____
 Committee: _____
 Hearing Date: _____
 2nd Agenda Date: _____

CITY CLERK USE ONLY

Scanned Date: _____
 Posted Item #: _____

All department items requiring Council approval must be submitted through the Mayor's Office.

Primary Details

Contract Phase

New Contract Renewal Amendment **Statutory Change Order** Supplemental
 Documentation Quantity Adjustment Final Payment Permission to Continue IDP
 Formal Acceptance Terminate/Cancel

Data Sharing

Yes No

Board Approval

Tulsa Metropolitan Utility Authority

Other Board Name

City Council Approval

Yes **No**

Contract Number

137337

Department

Water and Sewer

Contact Name

Josh White

Email

joshuawhite@cityoftulsa.org

Phone

918-404-6131

Vendor Name(s)

Daris Contractors, LLC

Vendor Number

590

Description (Subject)

E 53rd St & Riverside Dr Cherry Creek Lift Station

Contract Type

Public Const Proj

Contract Subtype

SSW I/M SCO BD

Bid/Project Number

TMUA ES 2009-07 C2 P2

Contract Amount

Site Address

Cherry Creek Lift Station

Site Parcel No.

Budget

Contract Funding Type

No Payment Involved
 Revenue Contract
 Expense Contract

Funding Source(s)

Approvals

Department: _____

Legal: _____

Board: _____

Mayor: _____

Other: _____

Stephane Solberg for LM

TOTAL:

Date: 04-24-26

Date: 4-30-26

Date: _____

Date: _____

Date: _____

Policy Statement

Background Information

CHANGE ORDER DESCRIPTION AND JUSTIFICATION: Change Order No. 3 to Contract No.137337, between the Tulsa Metropolitan Utility Authority and Daris Contractors, LLC, for Project No.TMUA ES 2009-07, CONTRACT 2 PHASE 2 EAST 53RD STREET AND RIVERSIDE DRIVE: CHERRY CREEK LIFT STATION PUMP RESTORATION AND FORCE MAIN IMPROVEMENTS, in the amount of 305 calendar days is necessary for time reconciliation associated with delays on project. Delays include working through instrumentation and control (I&C), pump 2 vibrational issues, and time delay on execution of change order 2. *John Ross tgp*

Summation of the Requested Action

Request the approval of Change Order No. 3

Other Pertinent Details

Council District 2 / SE Quadrant of Intersection 48th St and S Elwood Ave

Processing Information for City Clerk's Office

Post Execution Processing

- Mail vendor copy (add'l signature copies attached)
- Must be filed with other governmental entity
- Add'l governmental entity approval(s) required

Additional Routing and Processing Details

TULSA METROPOLITAN UTILITY AUTHORITY

CHANGE ORDER NO. 3

BOND NO. 0236700

CONTRACT NO. 137337

PROJECT NO. TMUA ES 2009-07, CONTRACT 2 PHASE 2 EAST 53RD STREET AND RIVERSIDE DRIVE: CHERRY CREEK LIFT STATION PUMP RESTORATION AND FORCE MAIN IMPROVEMENTS

CHANGE ORDER DESCRIPTION AND JUSTIFICATION: Change Order No. 3 to Contract No. 137337, between the Tulsa Metropolitan Utility Authority and Daris Contractors, LLC, for Project No. TMUA ES 2009-07, CONTRACT 2 PHASE 2 EAST 53RD STREET AND RIVERSIDE DRIVE: CHERRY CREEK LIFT STATION PUMP RESTORATION AND FORCE MAIN IMPROVEMENTS, in the amount of 305 calendar days is necessary for time reconciliation associated with delays on project. Delays include working through instrumentation and control (I&C), pump 2 vibrational issues and time delay on execution of change order 2.

Decrease in Contract Price: \$0.00


Increase in Contract Price: \$0.00

Net Change in contract Amount: \$0.00

DESCRIPTION OF CHANGES:

Original contract amount was:	\$2,770,000.00
Net dollar increase by previous Change Orders:	\$103,672.94
Net percent increase by previous Change Orders:	3.74%
Contract amount prior to this Change Order:	\$2,873,672.94
Contract sum is increased by this Change Order:	\$0.00
This Change Order is a percentage increase of:	0.00%
Contract amount including this Change Order:	\$2,873,672.94
The total dollar increase including this Change Order:	\$103,672.94
The percentage increase including this Change Order:	3.74%
Contract time prior to this Change Order:	459 Calendar Days
Contract time will be increased by:	305 Calendar Days

IN TESTIMONY WHEREOF, the parties hereto have caused this Change Order to be executed by their duly authorized officers or representatives on this _____ day of _____, 20____
(to be dated by TMUA Secretary upon approval)



TULSA METROPOLITAN UTILITY AUTHORITY:

By _____
TMUA Chairman

CONTRACTOR: Daris Contractors, LLC

By: Darrell Moorman

Printed Name: Darrell Moorman

Title: Outlaw Contracting, Inc. - Managing Member/President

Date: March 9, 2026

ATTEST:

TMUA Secretary

ATTEST:

Darrell Moorman March 9, 2026
Corporate Secretary (SEAL) Date

APPROVED:

TMUA Attorney

[Signature]
Director or Designee

SURETY:

Berkley Insurance Company

By: Kristin Lewis

Printed Name: Kristin Lewis, Attorney-in-Fact

Date: 3/6/2026

Attorney-in-Fact (SEAL)
(Attached Power of Attorney)



(Date must match Power of Attorney)

POWER OF ATTORNEY
BERKLEY INSURANCE COMPANY
WILMINGTON, DELAWARE

KNOW ALL MEN BY THESE PRESENTS, that BERKLEY INSURANCE COMPANY (the "Company"), a corporation duly organized and existing under the laws of the State of Delaware, having its principal office in Greenwich, CT, has made, constituted and appointed, and does by these presents make, constitute and appoint: *Vaughn Paul Graham, Jr.; Jamie M. Burris; John Kelly Deer; Kristin Lewis; Thomas Perrault; Faith Burleson; Brennan Morgan; or Madison Burris of Rich & Cartmill, Inc. of Tulsa, OK* its true and lawful Attorney-in-Fact, to sign its name as surety only as delineated below and to execute, seal, acknowledge and deliver any and all bonds and undertakings including bid related commitments such as Consent of Surety, with the exception of Financial Guaranty Insurance, providing that no single obligation shall exceed **Fifty Million and 00/100 U.S. Dollars (U.S.\$50,000,000.00)**, to the same extent as if such bonds had been duly executed and acknowledged by the regularly elected officers of the Company at its principal office in their own proper persons.

This Power of Attorney shall be construed and enforced in accordance with, and governed by, the laws of the State of Delaware, without giving effect to the principles of conflicts of laws thereof. This Power of Attorney is granted pursuant to the following resolutions which were duly and validly adopted at a meeting of the Board of Directors of the Company held on January 25, 2010:

RESOLVED, that, with respect to the Surety business written by Berkley Surety, the Chairman of the Board, Chief Executive Officer, President or any Vice President of the Company, in conjunction with the Secretary or any Assistant Secretary are hereby authorized to execute powers of attorney authorizing and qualifying the attorney-in-fact named therein to execute bonds, undertakings, recognizances, or other suretyship obligations on behalf of the Company, and to affix the corporate seal of the Company to powers of attorney executed pursuant hereto; and said officers may remove any such attorney-in-fact and revoke any power of attorney previously granted; and further

RESOLVED, that such power of attorney limits the acts of those named therein to the bonds, undertakings, recognizances, or other suretyship obligations specifically named therein, and they have no authority to bind the Company except in the manner and to the extent therein stated; and further

RESOLVED, that such power of attorney revokes all previous powers issued on behalf of the attorney-in-fact named; and further

RESOLVED, that the signature of any authorized officer and the seal of the Company may be affixed by facsimile to any power of attorney or certification thereof authorizing the execution and delivery of any bond, undertaking, recognizance, or other suretyship obligation of the Company; and such signature and seal when so used shall have the same force and effect as though manually affixed. The Company may continue to use for the purposes herein stated the facsimile signature of any person or persons who shall have been such officer or officers of the Company, notwithstanding the fact that they may have ceased to be such at the time when such instruments shall be issued.

IN WITNESS WHEREOF, the Company has caused these presents to be signed and attested by its appropriate officers and its corporate seal hereunto affixed this 2nd day of May, 2024.



Attest:
By *Philip S. Welt*
Philip S. Welt
Executive Vice President & Secretary

Berkley Insurance Company
By *Jeffrey M. Hafner*
Jeffrey M. Hafner
Senior Vice President

STATE OF CONNECTICUT)
) ss:
COUNTY OF FAIRFIELD)

Sworn to before me, a Notary Public in the State of Connecticut, this 2nd day of May, 2024, by Philip S. Welt and Jeffrey M. Hafner who are sworn to me to be the Executive Vice President and Secretary, and the Senior Vice President, respectively, of Berkley Insurance Company.

MARIA G. RINDBAKEN
NOTARY PUBLIC
CONNECTICUT

Maria G. Rindbaken
Notary Public, State of Connecticut

MY COMMISSION EXPIRES 04-30-2020

CERTIFICATE

I, the undersigned, Assistant Secretary of BERKLEY INSURANCE COMPANY, DO HEREBY CERTIFY that the foregoing is a true, correct and complete copy of the original Power of Attorney; that said Power of Attorney has not been revoked or rescinded and that the authority of the Attorney-in-Fact set forth therein, who executed the bond or undertaking to which this Power of Attorney is attached, is in full force and effect as of this date.

Given under my hand and seal of the Company, this 6th day of March, 2026.



Vincent P. Forte
Vincent P. Forte

AFFIDAVIT OF CLAIMANT

STATE OF Oklahoma

COUNTY OF Tulsa

The undersigned, of lawful age, being first duly sworn, on oath says that this contract is true and correct. Affiant further states that the work, services or materials will be completed or supplied in accordance with the contract, plans, specifications, orders or requests furnished to the affiant. Affiant further states that (s)he has made no payment directly or indirectly of money or any other thing of value to any elected official, officer or employee of the City of Tulsa or any public trust of which the City is a beneficiary to obtain or procure the contract or purchase order.

By: *Darrell Moorman*
Signature

Name: Darrell Moorman

Company: Daris Contractors, LLC


Title: Outlaw Contracting, Inc. - Managing Member/President

Subscribed and sworn to before me this 9th day of March, 2026.

[Signature]
Notary Public

My Commission Expires: 06-28-2029

Notary Commission Number: # 17005975



NON-COLLUSION AFFIDAVIT

(Required by Oklahoma law, 74 O.S. §85.22-85.25)

STATE OF Oklahoma)
)SS.
COUNTY OF Tulsa)

I, Darrell Moorman, of lawful age, being first duly sworn, state that:
(Authorized Agent)

1. I am the authorized agent of Contractor, Engineer, Architect or provider of professional service ["Services Provider"] herein for the purposes of certifying facts pertaining to the existence of collusion between and among Services Provider and municipal officials or employees, as well as facts pertaining to the giving or offering of things of value to government personnel in return for special consideration in the letting of any contract pursuant to which this statement is attached.
2. I am fully aware of the facts and circumstances surrounding the making of the contract to which this statement is attached, and I have been personally and directly involved in the proceedings leading to the awarding of such contract; and
3. Neither the Services Provider nor anyone subject to the Services Provider's direction or control has been a party:
 - a. to any collusion with any municipal official or employee as to quantity, quality, or price in the prospective contract, or as to any other terms of such prospective contract, nor
 - b. in any discussions between Services Provider and any municipal official concerning exchange of money or other thing of value for special consideration in the letting of a contract.


By: Darrell Moorman
Signature

Title: Outlaw Contracting, Inc. - Managing Member/President

Subscribed and sworn to before me this 9th day of March 20 24

[Signature]
Notary Public

My Commission Expires: 06-28-2029
Notary Commission Number: #17005975
County & State Where Notarized: Tulsa, OK



The Affidavit must be signed by an authorized agent and notarized.


EAST 53rd STREET AND RIVERSIDE DRIVE: CHERRY CREEK LIFT STATION PUMP RESTORATION AND FORCE MAIN IMPROVEMENTS

TMUA PROJECT NUMBER: ES 2009-07, CONTRACT 2, PHASE 2
ACCOUNT NUMBER: 2231S00005.SEWERLINES.SEWER.7500.75003122.541101

ENGINEERING SERVICES DEPARTMENT
CITY OF TULSA, OKLAHOMA

DRAWING INDEX

SHEET NUMBER	DRAWING NUMBER	TITLE
GENERAL		
1	C01	COVER V/INDEX
2	C02	PROJECT SITE MAP & CONTRACT ITEMS
		GENERAL NOTES & ADJUSTMENTS
CIVIL		
3	C01	EXISTING PROCESS FLOW DIAGRAM
4	C02	NEW PROCESS FLOW DIAGRAM
5	C03	VALVE WALK LOCATION PLAN AND YARD Piping
6	C04	TYPICAL DETAILS
7	C05	PUMP CONTROL TABLES
MECHANICAL		
8	M01	PLANS SYMBOL LEGEND
9	M02	CHERRY CREEK LIFT STATION - DEMOLITION PLANS & SECTION
10	M03	CHERRY CREEK LIFT STATION - NEW PLANS & SECTIONS
11	M04	CHERRY CREEK LIFT STATION - CONCRETE REPAIR NOTES AND DETAILS
12	M05	CHERRY CREEK LIFT STATION - ODOOR CONTROL PLANS
13	M06	CHERRY CREEK LIFT STATION - ODOOR CONTROL SECTIONS
14	M07	CHERRY CREEK VALVE WALK NO. 6
15	M08	NEW VALVE WALK NO. 8
16	M09	NEW VALVE WALK NO. 9
17	M10	NEW CHERRY CREEK TM 12" DRAIN VALVE MH
STRUCTURAL		
18	S01	GENERAL NOTES
19	S02	TYPICAL DETAILS
20	S03	MODIFIED VALVE WALK NO. 6 PLANS AND SECTIONS
21	S04	NEW VALVE WALK NO. 8 PLANS AND SECTIONS
22	S05	NEW VALVE WALK NO. 9 PLANS AND SECTIONS
23	S06	CHERRY CREEK LIFT STATION - CONCRETE REPAIR NOTES AND DETAILS
24	S07	CHERRY CREEK LIFT STATION - CONCRETE REPAIR NOTES AND DETAILS
25	S08	CHERRY CREEK LIFT STATION - CONCRETE REPAIR NOTES AND DETAILS
ELECTRICAL		
26	E01	SYMBOL LEGEND
27	E02	ONE-LINE DIAGRAM AND SCHEDULES
28	E03	CHERRY CREEK LIFT STATION - PLANS EL 504.00, EL 613.00 AND CL 613.00
29	E04	CHERRY CREEK LIFT STATION - PLANS EL 504.00, EL 613.00 AND CL 613.00
30	E05	CHERRY CREEK LIFT STATION - PLANS EL 504.00, EL 613.00 AND CL 613.00
31	E06	VFD SCHEMATICS
INSTRUMENTATION & CONTROLS		
32	I01	SYMBOL LEGEND
33	I02	CHERRY CREEK LIFT STATION V/MS (PARTIAL)

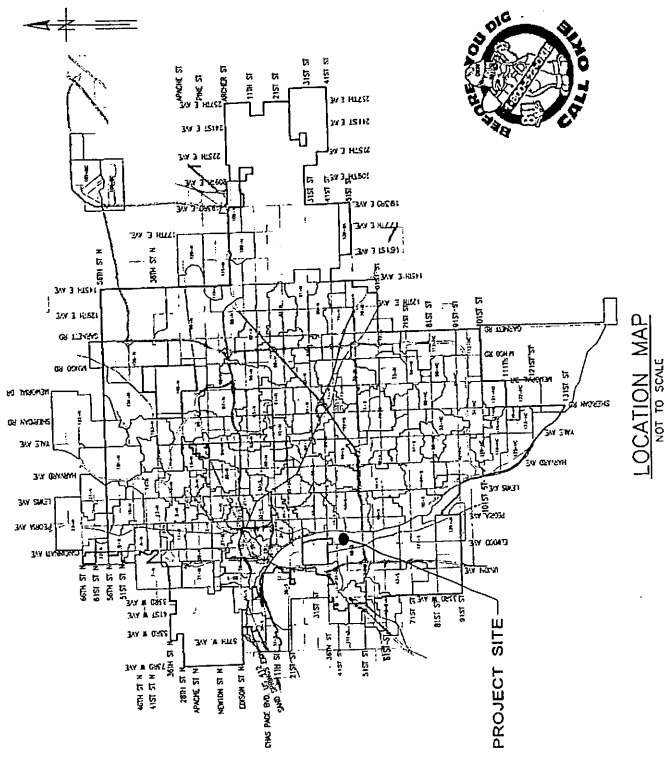

APPROVED BY: *[Signature]* DATE: 05.17.22
CITY ENGINEER ADVERTISE DATE

[Signature] DATE: 5.24.22
DIRECTOR, WATER AND SEWER DEPARTMENT ADVERTISE DATE

PREPARED BY:
GREELEY AND HANSEN
321 S. Boston Avenue, Suite 300
Tulsa, Oklahoma 74103
Ph. 312-650-9000

Certificate of Authorization No. 1975
Certificate Expires June 30, 2022

Timothy C. Guleandradze, P.E.
Oklahoma Reg. No. 33441
DATE: 05/14/2022


Certificate of Authorization No. 1975
Certificate Expires June 30, 2022

Michael J. Hansen, P.E.
Oklahoma Reg. No. 25161
DATE: 5/14/2022

IN ASSOCIATION WITH:
Wallace Design Collective
123 N. Norris
Tulsa, Oklahoma 74103
Ph 918-584-5858

Certificate of Authorization No. 1460
Certificate Expires June 30, 2023
DATE: 5/19/2022

PROJECT COORDINATION/CONTACTS	NUMBER
CITY OF TULSA ENGINEERING - AARON JOHNSON	918-596-9564
CITY OF TULSA E.I. - ERIC VANCE	918-596-9563
CITY OF TULSA OPERATIONS - MATT VAUGHAN	918-596-9565
CITY OF TULSA FIELD MANAGER - RYAN MCCASALE	918-596-9518
SOUTHSHORE W/TP - JOSHUA FISHER	918-591-4450
UTILITY COORDINATION BOX	
OKLAHOMA NATURAL GAS CO.	918-831-8261
AMERICAN ELECTRIC POWER/PUBLIC SERVICE COMPANY OF OKLAHOMA (CAP/PSO)	918-589-2844
TULSA PERMIT CENTER	918-596-1805
AT&T	918-596-4283
COX COMMUNICATIONS	918-689-4866
SOUTHWEST BELL TELEPHONE	918-586-6702
BIXBY TELEPHONE COMPANY	918-366-8000





PUBLIC WORKS
Engineering

DATE:
March 5th, 2025

TO:
Tom Prag, P.E.
Water and Sewer
Design Engineering Manager

FROM:
Ryan McKaskle, P.E., CFM
Public Works
Field Engineering Manager

Subject: CHANGE ORDER 3, Project No. TMUA ES 2009-07, CONTRACT 2 PHASE 2 EAST 53RD STREET AND RIVERSIDE DRIVE: CHERRY CREEK LIFT STATION PUMP RESTORATION AND FORCE MAIN IMPROVEMENTS (Contract No. 137337)

Original Contract -	\$	2,770,000.00
Change Order No. 1 -	\$	55,491.78
Change Order No. 1 % -		2.00%
Change Order No. 2 -	\$	48,181.16
Change Order No. 2% -		1.74%

New Contract Amount -	\$	2,873,672.94
Change Order Total -	\$	0.00
Change Order Total % -		3.74%

Original Contract Time -	365	Calendar Days
Contract Time Added by CO No. 1 -	73	Calendar Days
Contract Time Added by CO No. 2 -	21	Calendar Days
Contract Time Added by CO No. 3 -	305	Calendar Days

New Contract Time - 764 Calendar Days

Changer Order 3 consists of the following:

ITEM #1 - ADDITIONAL DAYS

Additional time of 305-days is necessary for time reconciliation associated with delays on the project. Delays include working through instrumentation and control (I&C), pump 2 vibrational issues and time delay on execution of change order 2.

ITEM #2 - ADDITIONAL COST

There are no costs associated with this change order

Total of 305-Calendar Days to be added.

1836 * 1898

TUL * USA

White, Joshua C

From: Voss, Matthew
Sent: Monday, December 22, 2025 1:34 PM
To: Markus Kellert; Darrell Moorman
Cc: McKaskle, Ryan; White, Joshua C
Subject: FW: [External Mail] Cherry Creek L.S.: Schedule
Attachments: 2205LS Cherry Creek L.S. 12.22.2025.pdf

*SUPPORTING
DOCUMENTS*

FYI..... Sent this on to Management group (see below). I am going to move forward with a day reconciliation to square to this schedule.

Thanks
Matthew S. Voss, PE

From: Voss, Matthew
Sent: Monday, December 22, 2025 1:31 PM
To: McKaskle, Ryan <RMCKASKLE@cityoftulsa.org>; Vaughan, Matt <MVAUGHAN@cityoftulsa.org>; Prag, Thomas <tprag@cityoftulsa.org>; Liechti, Andrew <aliechti@cityoftulsa.org>
Cc: White, Joshua C <JoshuaWhite@cityoftulsa.org>
Subject: FW: [External Mail] Cherry Creek L.S.: Schedule

Hi,

I know we had some internal discussions about time issues with Cherry Creek LS work and DARIS. I did have a conversation with DARIS and stated if they move forward in good faith the COT can work with them on their time issues.

I think this is the best movement forward to ensure the rest of the project good smoothly by resetting the contract time based off per attached with the vibration issues and I&C issues. Let me know if anyone objects. I am moving forward to get a change order started to incorporate all the days to hold to this attached schedule. Any day issues after this will be on DARIS.

Thanks

Matthew S. Voss, PE | Construction Manager
City of Tulsa Engineering Services
2317 S Jackson Ave., Room W104, Tulsa, OK 74107
T: 918-596-7836
C: 918-698-3068
E: mvoss@cityoftulsa.org
<http://www.cityoftulsa.org>

From: Markus Kellert <mkellert@daris.com>
Sent: Monday, December 22, 2025 11:55 AM
To: Voss, Matthew <mvoss@cityoftulsa.org>
Cc: Darrell Moorman <dmoorman@daris.com>
Subject: [External Mail] Cherry Creek L.S.: Schedule

Matt,

Thanks for meeting with me this morning and getting us on a clean slate once we start the pump pad repair. Attached is the updated schedule as of today. I show our completion date as 04/07/26. Let me know if I missed something or you need anything else from me.

Thank you and wishing you well in your new endeavor,

Markus Kellert

Project Manager



P.O. Box 897

Owasso, OK 74055

(918) 836-5700 office

(918) 378-3620 mobile

mkellert@daris.com

www.daris.com

CAUTION: This email originated from outside of the organization. Do not reply, forward, click links, or open attachments unless you recognize the sender and know the content is safe. Please report using the Phish Alert button in the Outlook Desktop Client if this message contains potentially unsafe content.



WATER AND SEWER
Engineering Design

DATE:

October 10, 2025

Darrell Moorman
Daris Contractors, LLC
PO Box 897
Owasso, OK 74055

Re: TMUA Contract No. 137337, Project No. ES 2009-07 Contract 2, Phase 2 Cherry Creek Lift Station Pump Restoration project- Notice of Noncompliance Letter – Subcontractor: Bauman Instrumentation Corporation

Dear Mr. Moorman:

Bauman Instrumentation Corporation (“BIC”), a subcontractor of Daris, has been placed on OTC suspension by the State of Oklahoma and determined inactive by the Oklahoma Secretary of State. The OTC suspension is in violation of the Contract documents and Resolution No. 7404 which provides in relevant part:

Affiant further states that the Company shall not fail to comply with and shall not knowingly allow any of its subcontractors or lower tier subcontractors to fail to comply with all applicable laws including, but not limited to, labor, employment and taxation laws, in the performance of any work on any project which is the subject of a contract between the Company and the City of Tulsa.

No contractor, or subcontractor, is allowed to work on the project, or have access to City of Tulsa property, while in violation of Resolution 7404. Daris, as the prime contractor, shall stop all work on the project until it fully complies with Resolution 7404.

Daris should immediately provide proof that the OTC suspension has been lifted, BIC is active and sign a new Affidavit of Compliance with Resolution 7404 or suspend BIC’s subcontract work until BIC cures the OTC suspension and inactive status. In accordance with General Condition GC-22, if BIC cannot immediately provide proof of compliance with Resolution 7404, you should return all security ID badges from its employees to Mr. Mathew Voss by Friday October 17, 2025.

Per Technical Specification Section 40 80 50 Part 1.1.B, Daris shall utilize the services of a contractually compliant system integrator with substantial documented experience to complete the project. Technical Specification Section 40 90 00 Part 1.8.B requires Daris to submit the credentials of its contractually compliant system integrator to Mr. Matthew Voss, along with, a plan for performing the remaining programming, site testing, commissioning, and start-up for owner approval before any work may proceed. The duration of the contract shall not be extended due to the delays caused by Daris, and BIC’s, failure to comply with Resolution 7404.



WATER AND SEWER
Engineering Design

Page 2 of 2

Re: TMUA Contract No. 137337, Project No. ES 2009-07 Contract 2, Phase 2 Cherry Creek Lift Station Pump Restoration project- Notice of Noncompliance Letter – Subcontractor: Bauman Instrumentation Corporation

Sincerely,

A handwritten signature in blue ink that reads "Thomas G. Prag".

Digitally signed by Thomas G.
Prag
Date: 2025.10.10 15:27:41 -05'00'

Thomas G. Prag, P.E. | Design Engineering Manager
City of Tulsa – Water and Sewer Department

1836 x 1898

TUL * USA



DARICON-01

JHENDON

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
3/27/2026

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER Rich & Cartmill, Inc. 2738 E. 51st Street, Suite 400 Tulsa, OK 74105	CONTACT NAME: Jane Hendon PHONE (A/C, No, Ext): (918) 293-7128 E-MAIL ADDRESS: jhendon@rcins.com	FAX (A/C, No):
	INSURER(S) AFFORDING COVERAGE	
	INSURER A : Phoenix Insurance Company	NAIC # 25623
INSURED Tulsa Metropolitan Utility Authority 175 E 2nd Street Tulsa, OK 74103	INSURER B :	
	INSURER C :	
	INSURER D :	
	INSURER E :	
	INSURER F :	

COVERAGES

CERTIFICATE NUMBER:

REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS	
A	COMMERCIAL GENERAL LIABILITY			PRS5R651000	7/20/2025	7/20/2026	EACH OCCURRENCE	\$ 1,000,000
	<input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> OCCUR						DAMAGE TO RENTED PREMISES (Ea occurrence)	\$
	<input checked="" type="checkbox"/> Owner's & Contractor						MED EXP (Any one person)	\$
	GEN'L AGGREGATE LIMIT APPLIES PER: <input checked="" type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC						PERSONAL & ADV INJURY	\$
	OTHER:						GENERAL AGGREGATE	\$ 1,000,000
							PRODUCTS - COMP/OP AGG	\$
	AUTOMOBILE LIABILITY						COMBINED SINGLE LIMIT (Ea accident)	\$
	<input type="checkbox"/> ANY AUTO OWNED AUTOS ONLY						BODILY INJURY (Per person)	\$
	<input type="checkbox"/> HIRED AUTOS ONLY						BODILY INJURY (Per accident)	\$
	<input type="checkbox"/> SCHEDULED AUTOS						PROPERTY DAMAGE (Per accident)	\$
	<input type="checkbox"/> NON-OWNED AUTOS ONLY							\$
	UMBRELLA LIAB						EACH OCCURRENCE	\$
	<input type="checkbox"/> EXCESS LIAB						AGGREGATE	\$
	<input type="checkbox"/> OCCUR							\$
	<input type="checkbox"/> CLAIMS-MADE							\$
	DED							\$
	RETENTION \$							\$
	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY						PER STATUTE	
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH)						OTH-ER	
	If yes, describe under DESCRIPTION OF OPERATIONS below						E.L. EACH ACCIDENT	\$
							E.L. DISEASE - EA EMPLOYEE	\$
							E.L. DISEASE - POLICY LIMIT	\$

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)
Project No: TMUA ES 2009-07 / Contract 2 Phase 2 East 53rd Street & Riverside Drive - Cherry Creek Lift Station Pump Restoration and Force Main Improvements

CERTIFICATE HOLDER

CANCELLATION

Tulsa Metropolitan Utility Authority 175 E 2nd Street Tulsa, OK 74103	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	AUTHORIZED REPRESENTATIVE 
